

The Sharon High School Construction Project




4 Week Look Ahead Schedule

- Temporary heaters are running. See enclosed notice.
- Major mechanical equipment (RTU's etc.) is stored locally and scheduled for installation over the coming weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior light gauge metal framing is nearing completion. In wall inspections are ongoing. Wall close-in is ongoing. Drywall finishing is ongoing.
- Paint, tile & ceiling grid subcontractors have begun. Polished concrete is ongoing.
- Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing but nearing completion. Installation of exterior panel is on the radar.
- Skylight installation is ongoing.
- Mock-up installation is ongoing- window testing is scheduled for mid-January. Window installation will follow.
- Casework installation is targeted to begin in early February.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbldg.com/>

Town of
SHARON
Massachusetts



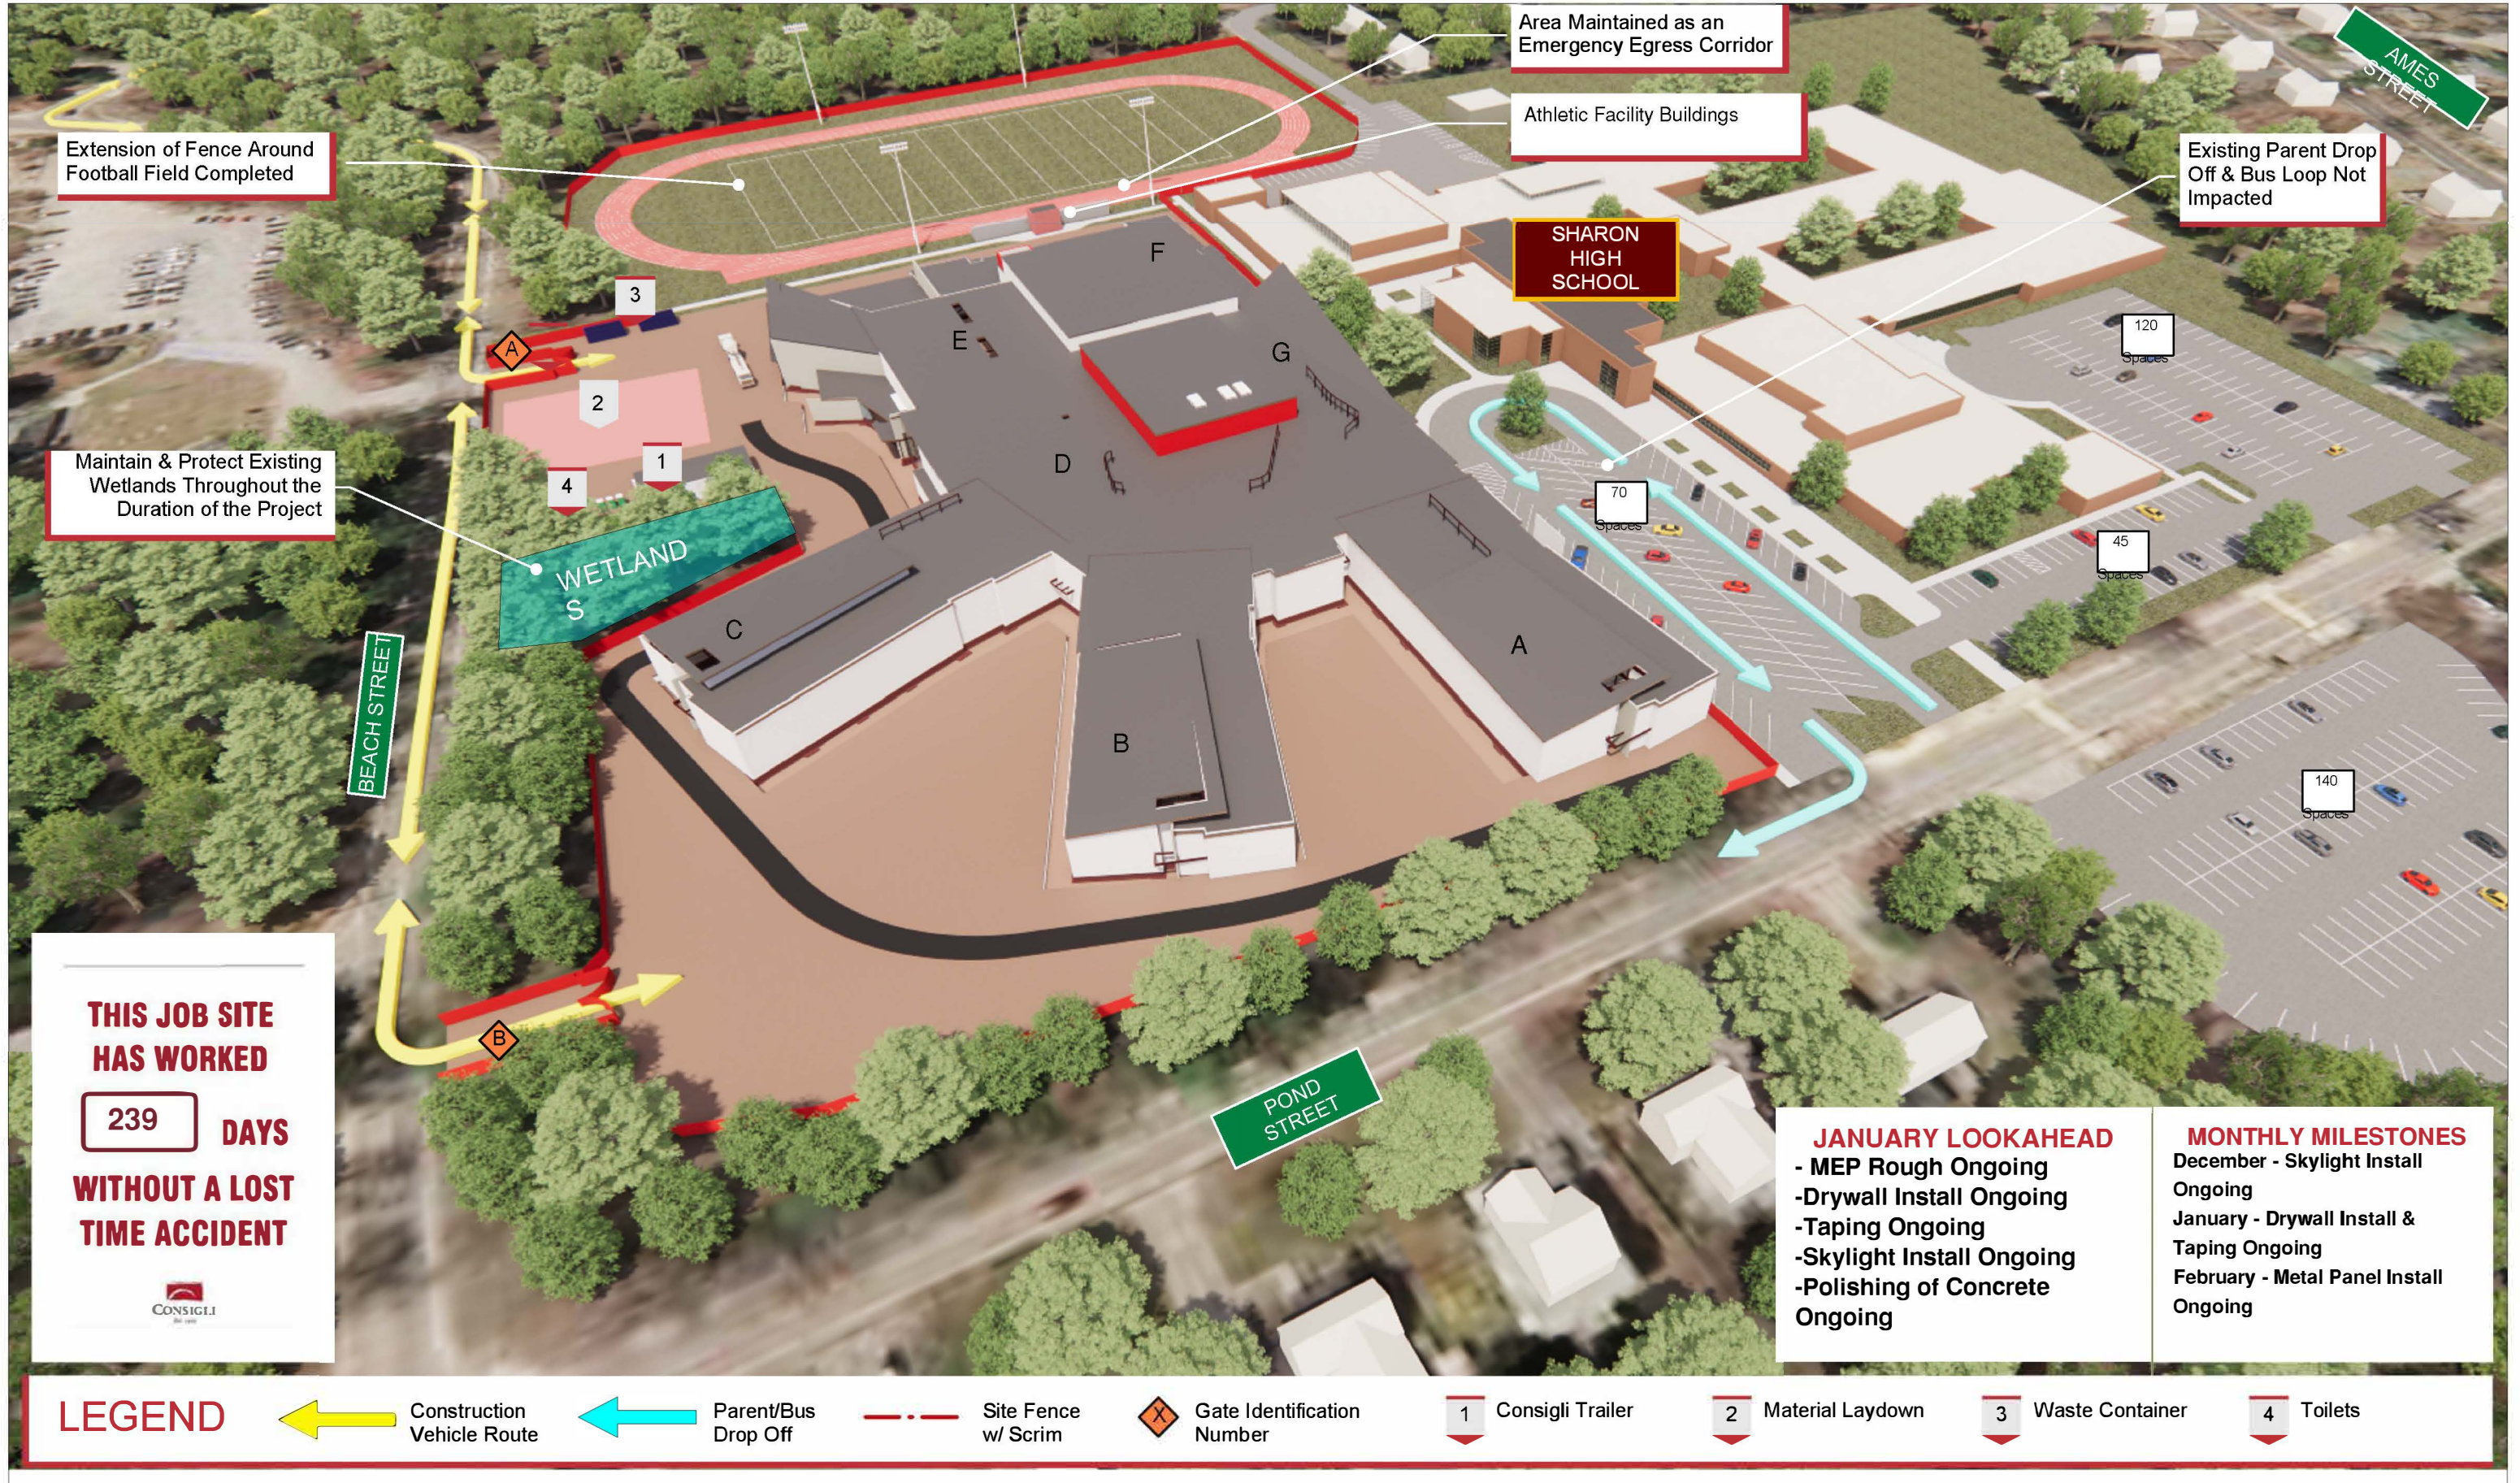

Extension of Fence Around Football Field Completed

Area Maintained as an Emergency Egress Corridor

Athletic Facility Buildings

Existing Parent Drop Off & Bus Loop Not Impacted

SHARON HIGH SCHOOL

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

WETLAND S

THIS JOB SITE HAS WORKED
239 DAYS
WITHOUT A LOST TIME ACCIDENT



JANUARY LOOKAHEAD
 - MEP Rough Ongoing
 - Drywall Install Ongoing
 - Taping Ongoing
 - Skylight Install Ongoing
 - Polishing of Concrete Ongoing

MONTHLY MILESTONES
 December - Skylight Install Ongoing
 January - Drywall Install & Taping Ongoing
 February - Metal Panel Install Ongoing

LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
