

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- Temporary heaters are running. See enclosed notice.
- Major mechanical equipment (RTU's etc.) is stored locally and scheduled for installation over the coming weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior light gauge metal framing is nearing completion. In wall inspections are ongoing. Wall close-in is ongoing- but targeted to be completed over the next month. Drywall finishing is ongoing.
- Paint, tile & ceiling grid subcontractors have begun. Polished concrete is ongoing.
- Air vapor barrier installation is ongoing. Installation of veneer masonry is ongoing but nearing completion. Installation of exterior panel (sub-girt & insulation) has started.
- Skylight installation is complete.
- Window installation has started & testing is ongoing.
- Casework installation is targeted to begin in early February.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>


Town of
SHARON
Massachusetts



SHARON HIGH SCHOOL



LOGISTICS UPDATE
January 11, 2022

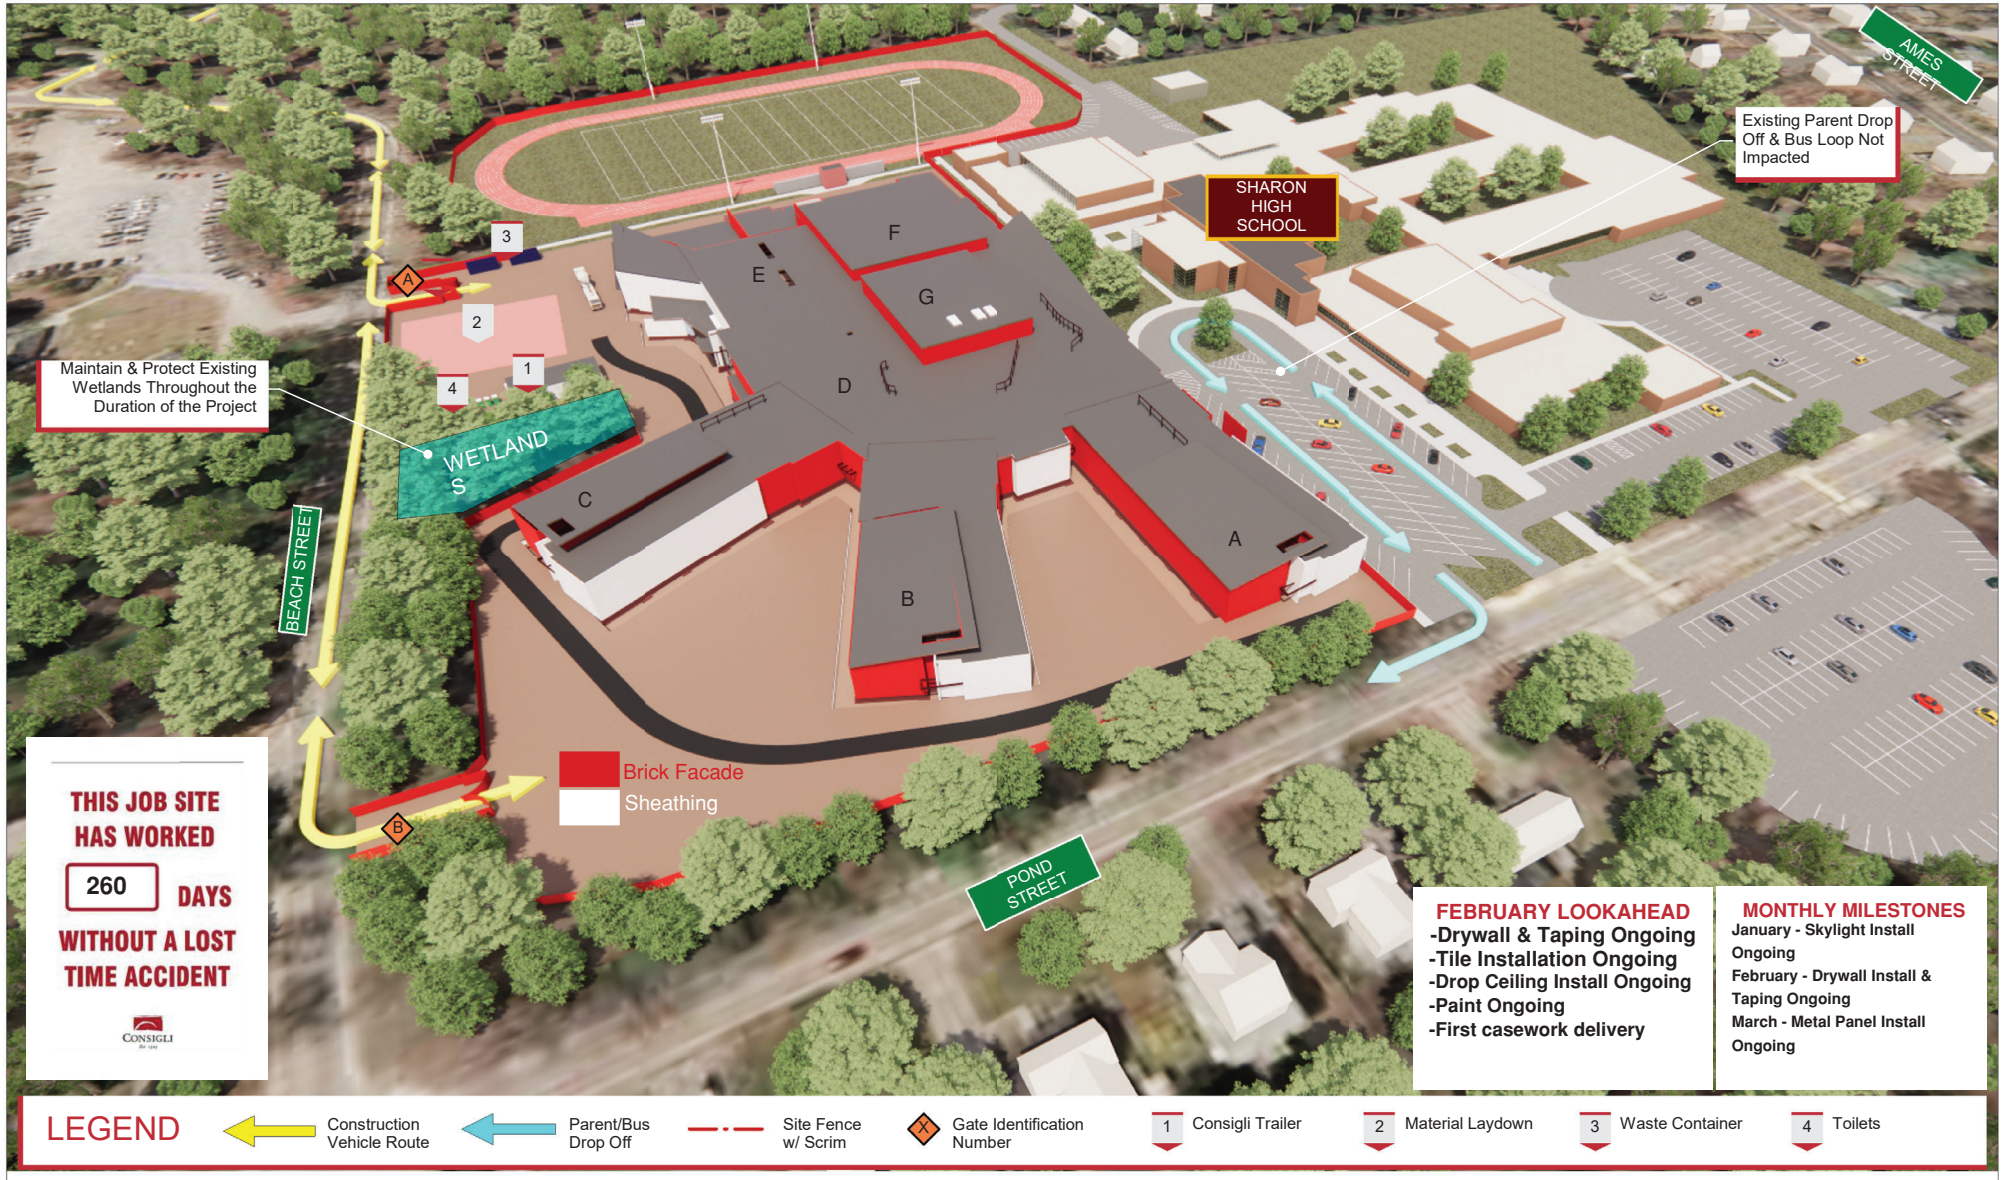

LOOK AHEAD SCHEDULE
1/31/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	1/31	2/1	2/2	2/3	2/4	2/5	2/6	2/7	2/8	2/9	2/10	2/11	2/12	2/13	2/14	2/15	2/16	2/17	2/18	2/19	2/20	2/21	2/22	2/23	2/24	2/25	2/26	2/27		
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S		
SCHOOL SCHEDULE																																		
MILESTONES																																		
G 1st Floor north of Aud inwall inspections complete																																		
G 2nd Floor north of Aud inwall inspections complete									X					X																				
A 2nd Floor Inwall inspections complete																																	X	
A 1st Floor Inwall inspections complete	4-Mar-22																																	
B 2nd Floor Inwall inspections complete	16-Mar-22																																	
B 1st Floor Inwall inspections complete	25-Mar-22																																	
HOLIDAYS																																		
WEATHER																																		
Snow 30" in Sharon 1-30-22																																		
Rain 2-3-22																																		
Snow 2-4-22																																		
MOCK UP																																		
Window Testing	Date TBD																																	
Install Metal Panels																																		
SITE UTILITIES																																		
Continual check in with Eversource for gas service																																		
Install conduit & transformer pads																																		
Install Remaining conduit for athletic facility																																		
FOOTBALL FIELD																																		
Form and install rebar for pressbox footings	Press box footings																																	
Place pressbox footings	on hold - pending re-design																																	
Form Piers at pressbox footings																																		
Place piers at pressbox footings																																		
Back fill pressbox footings																																		
ATHLETIC FACILITY																																		
Install Interior CMU Walls at Concession Stand & Bathrooms																																		
MEP Rough in CMU walls	PENDING COORDINATION AND TRUSS DESIGN																																	
Instal Vapor Barrier & Mesh																																		
Place Slabs																																		
INTERIOR FITOUT/OH ROUGH/FINISHES																																		
Building C																																		
Install MEP Drops to grid	Second Floor												X	X	X	X	X			X	X	X	X	X										
Install Ceiling Tiles	Second Floor																										X	X	X	X	X			
Install wall tile corridors & bathrooms	First Floor												X	X	X	X	X																	
Install Ceiling grid	First Floor - Classrooms																																	
Install MEP Drops to grid	First Floor																			X	X	X	X	X										
Install Ceiling grid in high hallway ceilings	2nd Floor												X	X	X	X	X			X	X	X	X	X										
Install Casework	Delivery Date TBD																																	
Building D																																		
Prime and first coat walls	Second Floor																																	
Install wall tile bathrooms and hallways	Second Floor												X	X	X	X	X																	
Install Ceiling Grid	Second Floor												X	X	X	X	X																	
Polish Concrete on 2nd floor around stair 3 opening	Second Floor												X	X	X	X	X																	
Polish Concrete in STEAM room	Second Floor																																	
Tape Walls	First Floor												X	X	X																			
Prime and first coat walls	First Floor												X	X	X	X	X																	
Install Ceiling Grid	First Floor																										X	X	X	X	X			
Building E																																		
Polish Concrete on Second Floor	Second Floor																																	
Tape Walls	Second Floor												X	X	X	X	X																	
Install Ceiling Grid	Second Floor																										X	X	X	X	X			
Prime and first coat walls	Second Floor																																	
Install ductwork -Wellness & Weight room area	First Floor																			X	X	X	X	X										
Install ductwork - Kitchen & Dining Commons	First Floor												X	X	X	X	X																	
Tape Walls	First Floor												X	X	X	X	X																	
Install Ceiling Grid	First Floor																																	
Building F - North																																		



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
