

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- Temporary heaters are running. See enclosed notice.
- Major mechanical equipment (RTU's etc.) is stored locally and scheduled for installation over the coming weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior light gauge metal framing is nearing completion. In wall inspections are ongoing. Wall close-in is ongoing- but targeted to be completed over the next month. Drywall finishing is ongoing.
- Finishes including paint, tile, concrete polishing & ceiling grid installation are ongoing.
- Air vapor barrier installation is ongoing but nearing completion. Installation of veneer masonry is ongoing but nearing completion. Installation of exterior panel (sub-girt & insulation) is ongoing.
- Skylight installation is complete.
- Window installation has started & testing is ongoing.
- Casework installation is targeted to begin in February.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbldg.com/>

Town of
SHARON
Massachusetts



PMA Consultants




TAPPÉ
ARCHITECTS



SHARON HIGH SCHOOL



LOGISTICS UPDATE
February 8, 2022

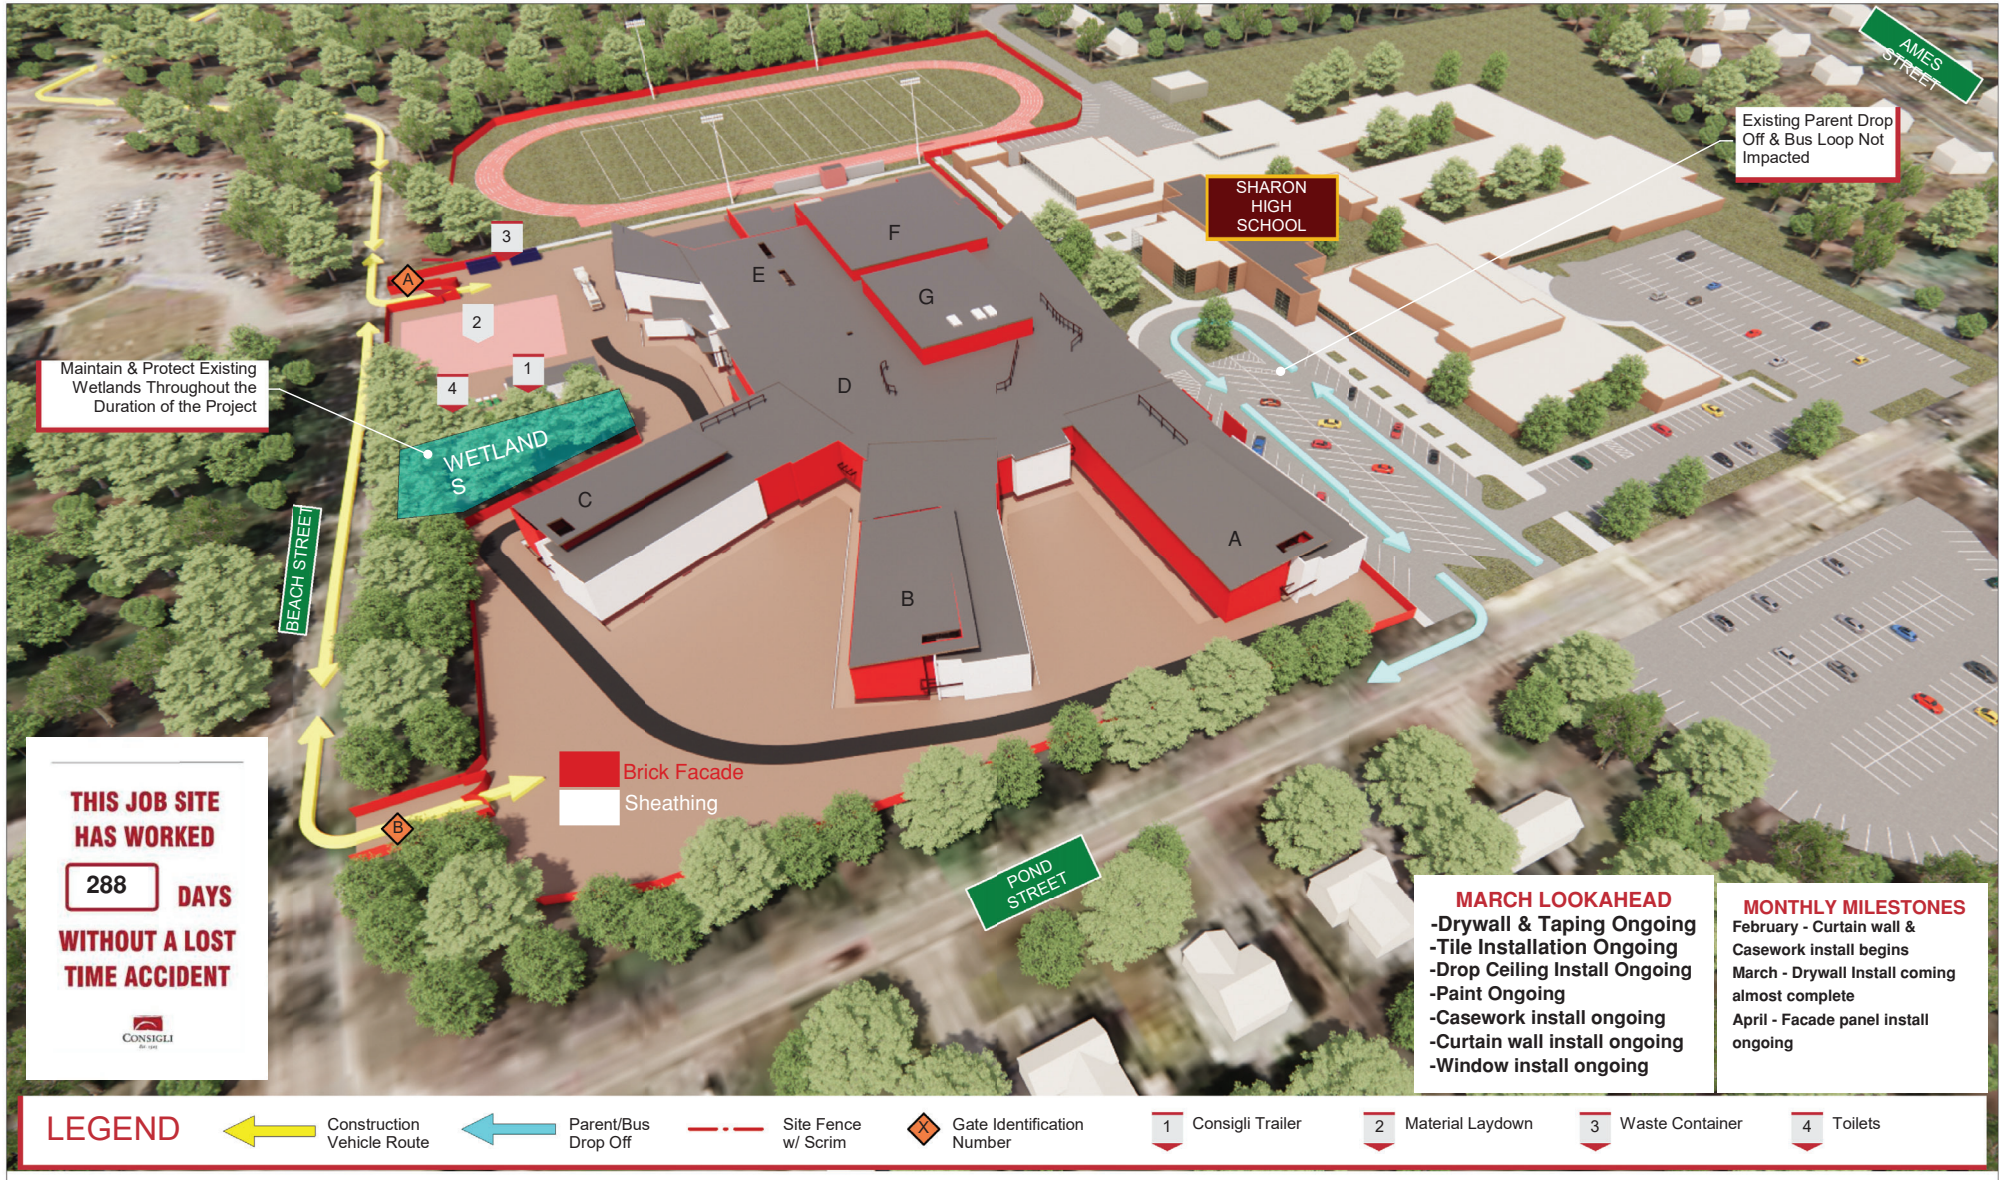

LOOK AHEAD SCHEDULE

2/7/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	2/7	2/8	2/9	2/10	2/11	2/12	2/13	2/14	2/15	2/16	2/17	2/18	2/19	2/20	2/21	2/22	2/23	2/24	2/25	2/26	2/27	2/28	3/1	3/2	3/3	3/4	3/5	3/6					
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S					
Polish Concrete in Main Lobby	First Floor			Kaloutas															X	X	X	X	X														
Building F - GYM																																					
Install OH Ductwork Hangers				Apex	X	X	X																														
Install OH Ductwork	Delivery week of 1-28-22			Apex	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Frame hard ceilings at running track				Century																																	
Tape Walls at running track and gym				Century	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X														
Paint Gym Walls				King																						X	X	X	X	X							
Install Gym Elevated Track Rails	Need Delivery Dates			Berlin Steel																																	
Paint Gym Trusses				King Painting																																	
Building G - North of Auditorium																																					
Install OH & Inwall Electrical Rough	2nd Floor			Griffin	X	X																															
Install OH HVAC Pipe	2nd Floor			NBK	X	X																															
Install OH Duct	2nd Floor			Apex	X	X	X	X	X			X	X	X	X	X																					
In wall inspections complete	2nd Floor			All Trades			X		X																												
Insulate & Board Walls	2nd Floor			Century				X	X			X	X	X	X	X			X	X	X	X	X														
Tape Walls	2nd Floor			Century																						X	X	X	X	X							
Paint Walls	2nd Floor			King																																	
Install Wall Tile	2nd Floor			High Point																																	
Install Ceiling Grid	2nd Floor			K&K																																	
Insulate & Board Walls	1st floor			Century	X	X	X	X	X			X	X	X	X	X																					
Tape Walls	1st floor			Century															X	X	X	X	X			X	X	X	X	X							
Paint Walls	1st floor			King																																	
Install Wall Tile	1st floor			High Point																																	
Install Ceiling Grid	1st floor			K&K																																	
Building G - Auditorium																																					
Install OH ductwork				Apex	X	X	X	X	X			X	X	X	X	X																					
Install OH Electrical Rough				Griffin	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X														
Install Auditorium Rails	Need Delivery Date			Berlin Steel																																	
Insulate and board walls				Century																																	
Tape walls				Century																																	
Building G - Black Box																																					
Install OH ductwork				Apex																																	
Electrical/Fire Alarm/TeIData Inwall Rough				Griffin	X	X	X																														
Install Black box Rails				Berlin Steel																																	
Building A																																					
Install OH & Inwall Plumbing rough	2nd Floor			Grasseschi	X	X	X	X	X			X	X	X	X	X			X	X	X	X															
Install OH Ductwork	2nd Floor			Apex																																	
Install OH & Inwall Electrical Rough	2nd Floor			Griffin				X	X			X	X	X	X	X			X	X	X	X															
Install OH & Inwall HVAC	2nd Floor			NBK	X	X	X	X	X			X	X	X	X	X			X	X	X	X															
Inwall Inspections Complete	2nd Floor			All Trades																																	
Insulate & Board Walls	2nd Floor			Century																																	
Tape Walls	2nd Floor			Century																																	
Paint Walls	2nd Floor			King																																	
Install Wall Tile	2nd Floor			High Point																																	
Install Ceiling Grid	2nd Floor			K&K																																	
Install OH & Inwall Plumbing rough	1st floor			Grasseschi	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Install OH Ductwork	1st floor			Apex																																	
Install OH HVAC Pipe	1st floor			NBK	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Inwall electrical rough	1st floor			Griffin															X	X	X	X	X			X	X	X	X								
Inwall Inspections Complete	1st floor			All Trades																																	
Building B																																					
Install OH & Inwall Plumbing rough	2nd Floor			Grasseschi								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Install OH Ductwork	2nd Floor			Apex																																	
Install OH HVAC Pipe	2nd Floor			NBK															X	X	X	X	X			X	X	X	X	X							
Install OH & Inwall Electrical Rough	2nd Floor			Griffin																						X	X	X	X	X							
Inwall Inspections Complete	2nd Floor 3-16-22			All Trades																																	
Install OH & Inwall Plumbing rough	1st floor			Grasseschi																																	
Install OH Ductwork	1st floor			Apex																																	
Install OH HVAC Pipe	1st floor			NBK																																	
Inwall electrical rough	1st floor			Griffin																																	
Install FP rough	1st floor			JCI	X	X	X	X	X																												
Inwall Inspections Complete	1st floor 3-25-22			All Trades																																	
ROOFING & FAÇADE WORK																																					



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
