

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- Temporary heaters are running. See enclosed notice.
- Major mechanical equipment (RTU's etc.) is stored locally and installation is ongoing.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior light gauge metal framing is nearing completion. In wall inspections are ongoing. Wall close-in is ongoing- targeted to be completed by late March. Drywall finishing is ongoing.
- Finishes including paint, tile, concrete polishing & ceiling grid installation are ongoing.
- Air vapor barrier installation is ongoing but nearing completion. Installation of veneer masonry is ongoing but nearing completion. Installation of exterior panel (sub-girt & insulation) is ongoing.
- Skylight installation is complete.
- Window installation has started & testing is ongoing.
- Casework installation is targeted to begin in late February.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



PMA Consultants




**TAPPÉ
ARCHITECTS**



SHARON HIGH SCHOOL



LOGISTICS UPDATE
February 8, 2022

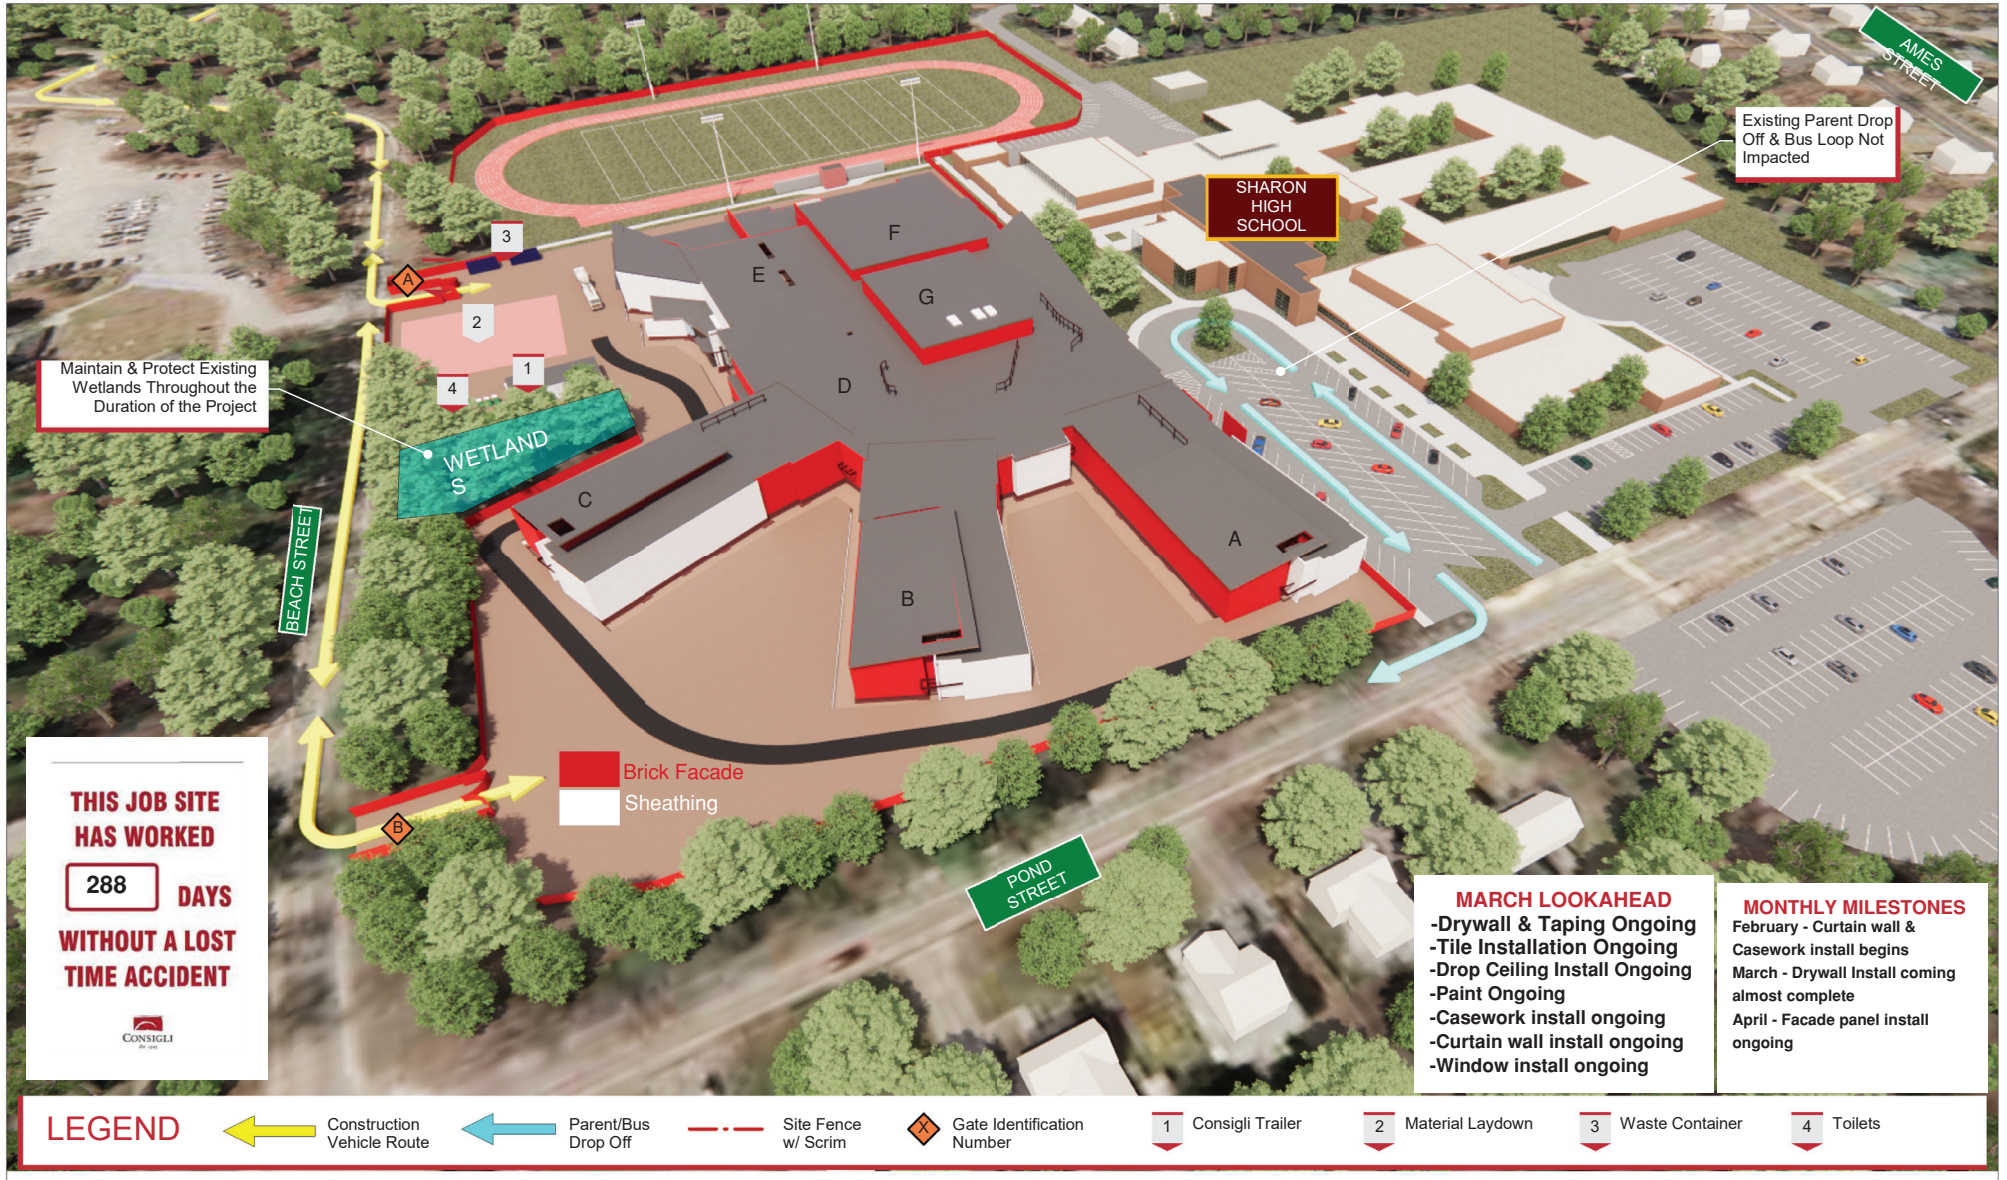

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

Existing Parent Drop Off & Bus Loop Not Impacted

THIS JOB SITE HAS WORKED
288 DAYS
WITHOUT A LOST TIME ACCIDENT

Brick Facade
Sheathing

MARCH LOOKAHEAD
-Drywall & Taping Ongoing
-Tile Installation Ongoing
-Drop Ceiling Install Ongoing
-Paint Ongoing
-Casework install ongoing
-Curtain wall install ongoing
-Window install ongoing

MONTHLY MILESTONES
February - Curtain wall & Casework install begins
March - Drywall Install coming almost complete
April - Facade panel install ongoing

- LEGEND**
- Construction Vehicle Route
 - Parent/Bus Drop Off
 - Site Fence w/ Scrim
 - Gate Identification Number
 - 1 Consigli Trailer
 - 2 Material Laydown
 - 3 Waste Container
 - 4 Toilets

LOOK AHEAD SCHEDULE
2/14/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	2/14	2/15	2/16	2/17	2/18	2/19	2/20	2/21	2/22	2/23	2/24	2/25	2/26	2/27	2/28	3/1	3/2	3/3	3/4	3/5	3/6	3/7	3/8	3/9	3/10	3/11	3/12	3/13	
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
Install Ceiling Grid	2nd Floor			K&K																													
Install OH & Inwall Plumbing rough	1st floor			Grasseschi	X	X	X	X	X			X	X	X	X	X			X	X	X	X											
Install OH Ductwork	1st floor			Apex																													
Install OH HVAC Pipe	1st floor			NBK	X	X	X	X	X			X	X	X	X	X			X	X	X	X											
Inwall electrical rough	1st floor			Griffin								X	X	X	X	X			X	X	X	X											
Inwall Inspections Complete	1st floor			All Trades																		X											
Insulate & Board Walls	1st floor			Century																					X	X	X	X	X				
Tape Walls	1st floor			Century																													
Paint Walls	1st floor			King																													
Install Wall Tile	1st floor			High Point																													
Building B																																	
Install Channels at Stair 9	Delivery 4-4-22			Berlin Steel																													
Install OH & Inwall Plumbing rough	2nd Floor			Grasseschi	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X		
Install OH Ductwork	2nd Floor			Apex																													
Install OH HVAC Pipe	2nd Floor			NBK	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X		
Install OH & Inwall Electrical Rough	2nd Floor			Griffin															X	X	X	X	X				X	X	X	X	X		
Inwall Inspections Complete	2nd Floor 3-16-22			All Trades																													
Install OH & Inwall Plumbing rough	1st floor			Grasseschi	X	X	X	X	X																	X	X	X	X	X			
Install OH Ductwork	1st floor			Apex																													
Install OH HVAC Pipe	1st floor			NBK																						X	X	X	X	X			
Inwall electrical rough	1st floor			Griffin																						X	X	X	X	X			
Inwall Inspections Complete	1st floor 3-25-22			All Trades																													
Polish Concrete in B1 Corridor	1st floor			Kaloutas		X	X	X	X			X	X																				
ROOFING & FAÇADE WORK																																	
Building C																																	
Install Marvin Windows	Pending Testing Results			Chandler Architectural			X	X	X																								
Install Window Caulking				Armani								X																					
Install Clerestory Curtain Wall				Chandler Architectural			X	X	X			X	X	X	X	X																	
Install End of wing Curtain Wall	1st and 2nd Floor			Chandler Architectural																													
Install TAKTL Panels on East and South Facades				Riggs																													
Building D																																	
Complete remaining AVB at south elevation				Armani	X	X	X	X	X																								
Install phenolic panel backup & Insulation				Riggs																						X	X	X	X	X			
Install CW				Chandler Architectural																													
Install peerless windows on south façade D				Chandler Architectural																													
Building E																																	
Install Green roof rails	Delivery 2-28-22			Berlin Steel															X	X	X	X	X										
Install Roofing on South Green Roof - Pending Rail Delivery				Capeway																						X	X	X	X	X			
Install phenolic panel backup & Insulation				Riggs	X	X	X	X	X																								
Install CW				Chandler Architectural																													
Install phenolic panel				Riggs																													
Building F																																	
Install Peerless windows at north elevation	North Façade			Chandler Architectural	X	X	X	X	X																								
Fiber Resin Flashing				Riggs	X	X																											
Fiber Resin Clips/Vertical Rails				Riggs	X	X	X	X	X			X	X																				
Building G																																	
Install Masonry façade				Fernandes	X	X	X	X	X																								
Wash Brick				Fernandes				X	X																								
Caulk Peerless windows in Panels	North Façade			Armani																													
Install Fiber Resin Clips & Vertical Rails				Riggs	X	X	X	X	X																								
Building A																																	
Install Masonry Façade				Fernandes	X	X	X	X	X																								
Wash Brick				Fernandes				X	X																								
Install TAKTL Backup & Insulation				Riggs	X	X	X																										
Install MCM Insulation & Girts				Riggs								X	X	X	X	X																	
Install Clerestory Curtain Wall				Chandler Architectural			X	X	X			X	X	X	X	X																	
Install End of wing Curtain Wall	1st and 2nd Floor			Chandler Architectural																													
Install Marvin Windows	Pending Testing Results			Chandler Architectural																													
Install Window Caulking				Armani																													
Building B																																	



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
