

The Sharon High School Construction Project



4 Week Look Ahead Schedule 03/15/2021

- **Upcoming Activities Include:**

- Structural steel deliveries are ongoing
- Structural steel erection begins next week
- Underground utility work has begun (both site and within building)
- Prep, place, dampproof & insulate foundations is ongoing but nearing completion
- See attached progress update
- See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information:
<https://www.shsbuilding.com/>


Town of
SHARON
Massachusetts



Sharon High School



SHARON HS PROGRESS UPDATE MARCH 2021

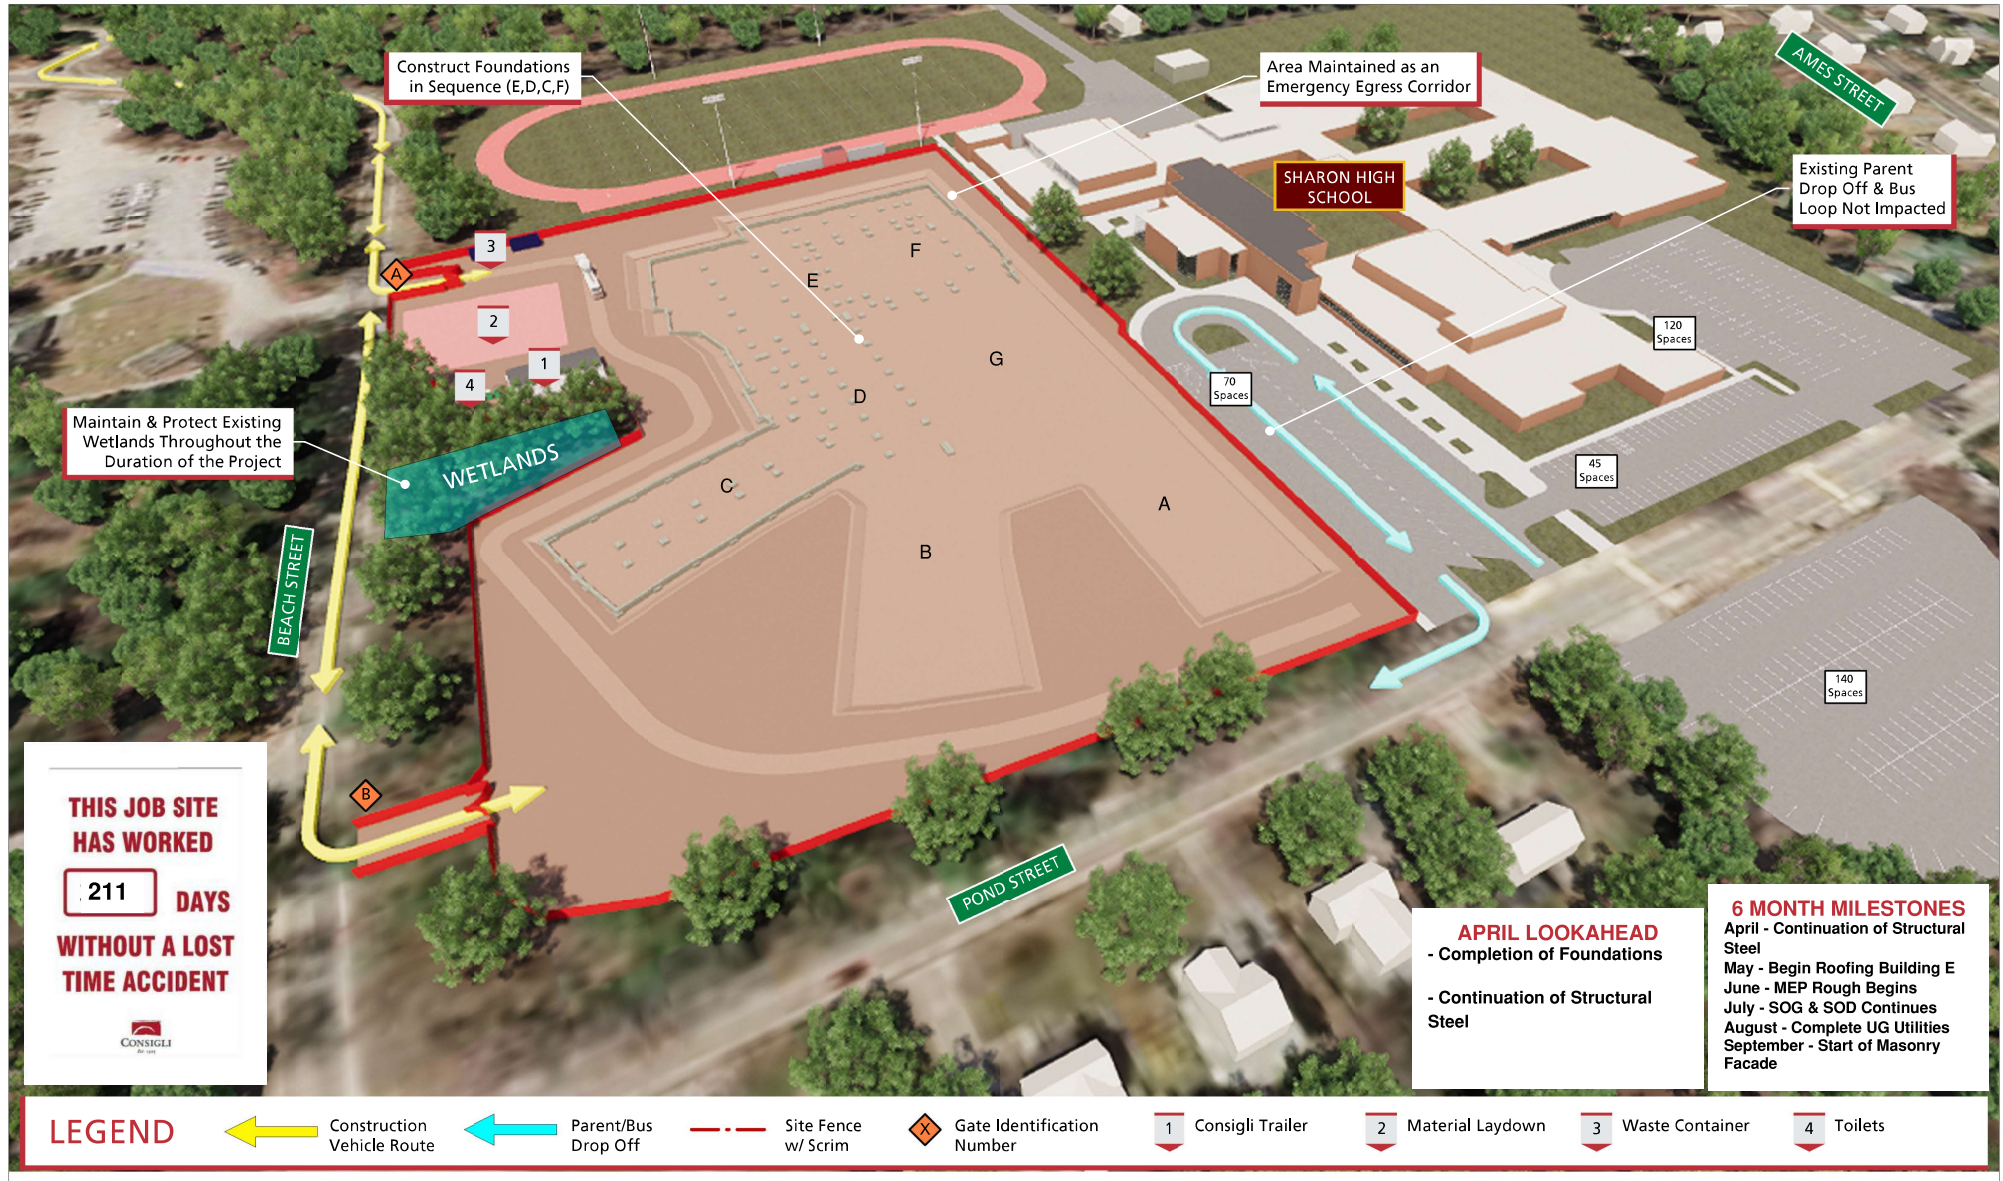

THIS JOB SITE HAS WORKED

211 DAYS

WITHOUT A LOST TIME ACCIDENT



APRIL LOOKAHEAD
 - Completion of Foundations
 - Continuation of Structural Steel

6 MONTH MILESTONES
 April - Continuation of Structural Steel
 May - Begin Roofing Building E
 June - MEP Rough Begins
 July - SOG & SOD Continues
 August - Complete UG Utilities
 September - Start of Masonry Facade

LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets

LOOK AHEAD SCHEDULE

3/15/2021

Description of Work	Notes	P6 Activity Code	Responsibility	3/15	3/16	3/17	3/18	3/19	3/20	3/21	3/22	3/23	3/24	3/25	3/26	3/27	3/28	3/29	3/30	3/31	4/1	4/2	4/3	4/4	4/5	4/6	4/7	4/8	4/9	4/10	4/11
				M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S
				M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S
SCHOOL SCHEDULE																															
Students onsite in school session			SHARON HS	X	X		X	X			X	X		X	X			X	X		X	X			X	X		X	X		
Fully remote day			SHARON HS			X						X							X								X				
Early Release Day			SHARON HS									X																			
Good Friday - No School																						X									
MILESTONES																															
Steel Erection Start Date - Mobilization/Delivery - March 15th 2020			Supermetal/GP East	X																											
HOLIDAYS																															
WEATHER																															
SITework																															
SITE UTILITIES																															
Excavate/Backfill electrical ductbank - Post foundation Backfilling - Pending Weather		A9670	Marois																						X	X	X	X	X		
Install electrical ductbank - Post foundation backfilling - pending weather		A9670	MAK																						X	X	X	X	X		
Install drainage and associated piping - Post Backfilling		A9660	Marois	X																X	X	X			X	X	X	X	X		
Install Domestic Water Service Into building			Marois			X	X	X			X	X	X																		
Install Fire Service Service Into building			Marois			X	X	X			X	X	X																		
Begin design work for gas main to new building			Columbia	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
BUILDING FOUNDATION																															
Dewatering			Marois	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Building E																															
Install remaining footings on K Line - at Acid Pit			Riggs																												
Backfill foundations on K Line			Marois	X																											
Building D																															
Building C																															
Install Foundation Drain and backfill foundation walls			Marois	X	X																										
Building F																															
Install Foundations (footings) for Building F		A9020	Riggs																												
Backfill foundations (footings) Building F			Marois	X	X																										
Install Foundation Walls for Building F		A9020	Riggs	X	X																										
Install Damproofing on F Building Foundations Walls		A10660	Superior									X	X							X	X							X	X		
Building A																															
Excavate foundations Building A		A8820	Marois																												
Install Foundations (footings) for Building A		A9020	Riggs	X	X	X																									
Backfill foundations (footings) Building A			Marois	X	X	X	X																								
Install Foundation Walls for Building A		A9020	Riggs	X	X	X	X	X			X	X	X	X	X			X	X	X											
Steel Erection																															
Building C																															
Steel Delivery C Building		A9120	Supermetal/GP East			X	X	X																							
Crane Mobilization			Supermetal/GP East								X																				
Steel Erection C Building		A9120	Supermetal/GP East									X	X	X	X			X	X	X	X	X									
Deck and Detail C Building		A9190	Supermetal/GP East															X	X	X	X	X			X	X	X	X	X		
Building E																															
Steel Delivery E Building		A9160	Supermetal/GP East										X	X				X	X							X	X	X	X		
Steel Erection E Building		A9160	Supermetal/GP East																	X	X				X	X	X	X	X		
Deck and Detail E Building		A9230	Supermetal/GP East																								X	X	X		
Underground Utilities																															
Building E/D																															
Excavate and backfill for underground utilities			Marois	X	X	X	X	X			X	X	X	X	X																
Underground acid piping (deep runs)			Grasseschi	X	X	X	X	X			X	X	X	X	X																
Building F/G																															
Excavate and backfill for underground utilities			Marois									X	X	X			X	X	X	X	X			X	X	X	X				

				LOOK AHEAD SCHEDULE 3/15/2021																											
Description of Work	Notes	P6 Activity Code	Responsibility	3/15	3/16	3/17	3/18	3/19	3/20	3/21	3/22	3/23	3/24	3/25	3/26	3/27	3/28	3/29	3/30	3/31	4/1	4/2	4/3	4/4	4/5	4/6	4/7	4/8	4/9	4/10	4/11
				M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S	M	T	W	TR	TR	1	S
Underground acid piping (deep runs)			Grasseschi									X	X	X			X	X	X	X	X			X	X	X	X				
