The Sharon High School Construction Project

4 Week Look Ahead Schedule

- Temporary heaters are running. See enclosed notice.
- The majority of mechanical equipment (RTU's etc.) has been set in place. Team is working towards equipment start up.
- Electrical switchgear is being assembled on-site and team is working towards permanent power.
- Sheetrock completion (including taping) is on the radar for early April.
- Finishes including paint, tile, epoxy flooring, concrete polishing & ceiling grid are ongoing.
- Exterior panel systems installation is ongoing.
- Window & curtainwall installation-including installation of glazing- is ongoing.
- Casework installation is ongoing.
- Work at the athletic facility- including installation of concrete slabs- has resumed.
- Specialty installations such as gymnasium equipment & wood floor are on the radar for the next month.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/

Town of

SHARON












SHARON HIGH SCHOOL



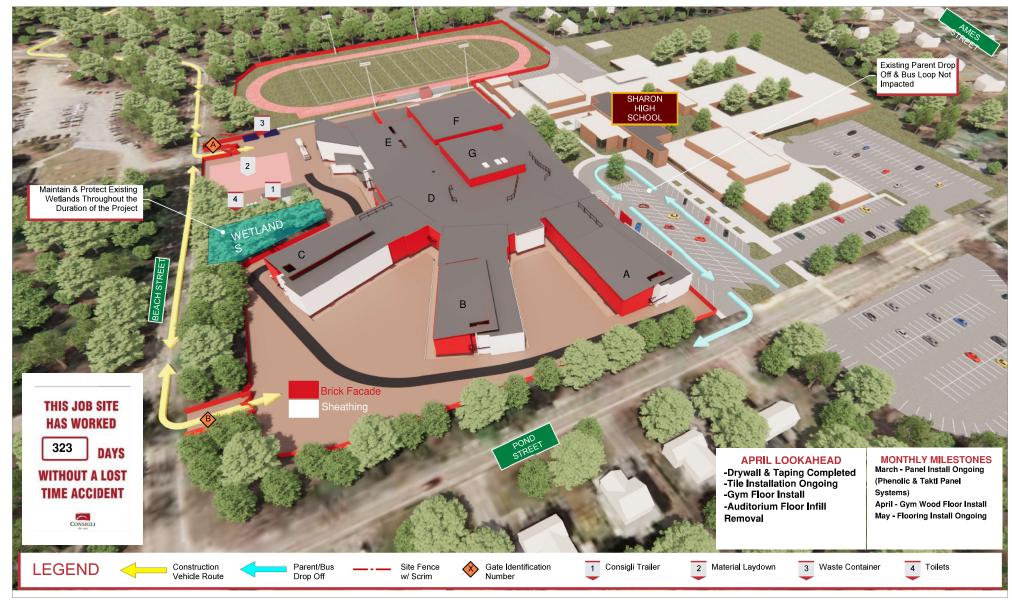

Schedule	Consigli Construction - Sharon Hi	iah School F	Project																											
3212022 More More More More	-	igir concorr				-																								
Description of Nork Mote Origination Support of Nork Support <																														
Deck Deck <thdeck< th=""> Deck Deck <</thdeck<>	3/21/2022																													
Description Description <thdescription< th=""> <thdescription< th=""></thdescription<></thdescription<>		Notes		ROCK	ponsibility	3/21 M	3/22 T	3/23 W	3/24 TR	3/25 FR	3/26 3/2 S S	27 3/28 M	3/29 T	3/30 W	3/31 TR	4/1 FR	4/2 4/3 S S	4/4 M	4/5 T	4/6 W	4/7 TR	4/8 /	4/9 4/9	/10 4/11 S M		4/13 W	4/14 TR	4/15 FR	4/16 4 S	//17 4/18 S M
Normal-participants Image: Participant set of the set																														
Non-Non-Non-Non-Non-Non-Non-Non-Non-Non-																														
WEAKE Control Market Delete Delet		12-Apr-22																							Х					
Note:	HOLIDAYS																													
Series of lating 22 and 32 Series of 32	WEATHER																													
Set to the set of the se	MOCK UP/THIRD PARTY ENVELOPE TESTING																													
Set Market Autures NU. Grim NU. Grim NU. Grim NU. Set Market Autor	Peerless Window Testing on Buildings E2 and G2			C	CC/PMA							Х																		
State State <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>																														
Incluit Production optic for larges Image: Procession optic for larges				W.	J Griffin																									
Status																														
Prom antial riskar for pressors bordings Pressors bor																														
Blace pressobio forings Image Im																												_		
From Prior a) president bootings From Prior a) president booting a) president booting a) president booting a) president bootings																												-		
Back Biorshox Dan Clayton Dan Clayton <td>Form Piers at pressbox footings</td> <td></td> <td></td> <td></td> <td>Riggs</td> <td></td>	Form Piers at pressbox footings				Riggs																									
Intal ProcessorIntel ContonIntel Cont																												-		
ATH ETIC FACILITY BUILDINGS Image: Arrows of the set																														
Install Red members n AF Install Root Parsing																														
Install Root Trusses Image				Fe	rnandes																									
Install Roof Framing Install Roof Framing <th< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>_</td><td></td><td>V</td><td>v</td><td>v</td><td>v</td><td>v</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></th<>																_		V	v	v	v	v								
Install proving																		^	^	^	~	<u> </u>								
Prep floor drains in AF slab Imaki Vago Grasseschi X	Install Roofing			C	apeway																									
Instal Moyor Barrier Instal Moyor Barrier <th< td=""><td></td><td></td><td></td><td></td><td></td><td>X</td><td>x</td><td></td><td></td><td>_</td><td></td><td></td><td></td><td></td><td></td><td>_</td><td></td><td></td><td></td><td></td><td></td><td>-</td><td></td><td></td><td></td><td></td><td></td><td>-</td><td></td><td></td></th<>						X	x			_						_						-						-		
Instal Mesh & Rebar Instal Mesh & Rebar<								Х	Х	Х																		-		
Install Masony Façade Install Masony Fa												Х	Х	Х	X	X														
Sulding C - 2nd Floor Image: Solution of the second of				_											X	X														
Install APEX Duct drops in ACT Media Media Apex X </td <td>INTERIOR FITOUT/OH ROUGH/FINISHES</td> <td></td>	INTERIOR FITOUT/OH ROUGH/FINISHES																													
Install Light Fixtures in classrooms Pending missing light fixtures WJ Griffin Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures WJ Griffin Image: Complete Electrical/LV drops Drops in ACT Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops in ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops In ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops In ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops In ACT Pending missing light fixtures Image: Complete Electrical/LV drops Drops					-																									
· · · · · · · · · · · · · · · · · · ·	P					X	X	Х	Х	X		X																		
Pending missing light fixtures Pending missing light fixtures K&K K		fixtures																-										-		
Install Toilet FinishesInstall Toilet FinishesInstall CollingInstall Colling <t< td=""><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td>~</td><td>~</td><td>~</td><td>~</td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td><td></td></t<>													~	~	~	~														
Install Ceiling grid in high hallway ceilings Install Channels at Stair 10 Install Stair 1		Intures												Х	Х	Х														
Install Channels at Stair 10	_											X	Х			-						-						-		
Install Stair 10 Berlin Steel Image: C + 1 to transformed by the t																				Х	Х	Х								
Building C - 1st Floor 6 1 St F															X	X												-		
	Building C - 1st Floor			Del										~	~	~		~	~											
Install APEX Duct drops in ACT Apex X	Install APEX Duct drops in ACT					Х	Х	Х	Х	Х		Х																		
Complete Electrical/LV drops Drops in ACT WJ Griffin WJ Griffin X<		Pending missing light																												
instal Light Fixtures in classrooms fixtures		fixtures											X	Х	X	X		X	X	Х	X	X								
	Flood Cellings in Classrooms											v	~											X	X	Х	Х	X		
Prime & First Coat Hard Ceilings King King <td></td> <td>X</td> <td>X</td> <td>Х</td> <td>х</td> <td>X</td> <td></td>												X	X	Х	х	X														

Considi Construction Sharor	- High School F	Project																							
Consigli Construction - Sharor														_											
3/21/2022																									
Description of Work	Notes	P6 Activity % Code Comp	<u>Responsibility</u>	3/21 M	-		1					/31 4/1 FR FR				4/7 TR			4/11 M		4/13 W			/16 4/1 S S	
Frame/Board/Tape/Sand soffit around stair 10 channel Board soffit around stair 10 channel			Century Century													x	X		Х	x	х				
Tape & Sand soffit around stair 10 channel			Century													~			~	~	X	Х	X		Х
Prime & First Coat Soffit around stair 10 channel			Century																						
Install wood slat ceiling in hallway			K&K																						
Building C - IDF Room 2519			W I Criffin																						
Build Out Building D - 2nd Floor			WJ Griffin																						
Prime & First Coat Hard Ceilings			King				X	X	Х	X															
Install Toilet Finishes			Grasseschi				~	~		~	X	х х	>	X	Х	Х	Х								
Install MEP Drops to ACT grid			MEP Trades							Х		х х	>			Х									
Complete MEP Drops in ACT			MEP Trades														Х								
Install electrical devices and light fixtures in ACT	Pending missing light fixtures		WJ Griffin							х	X	x x	>	Х	Х	Х	Х								
Install Casework in Science Rooms	Post Window Install		NEIS Casework						 																
Flood ACT Ceilings	Pending missing light fixtures		K&K																Х	Х	Х	Х	x		
Install Pipe grid in Steam room			Berlin Steel																						
Building D - 1st floor																									
Complete Duct Drops in ACT Grid			Арех																						
Complete HVAC Drops in ACT Grid			NBK													_									
Install light fixtures in ACT ceilings Flood ACT Ceilings	Pending missing light fixtures		WJ Griffin K&K																						
Install light fixtures in hard ceilings	Pending missing light fixtures		WJ Griffin														-								
Prime & First Coat Hard Ceilings			King				Х	X																	
Install Toilet Finishes			Grasseschi						Х	Х	X	х х	>	X	Х	Х	Х								
Complete tile in Hallway			High Point	Х	Х	Х																			
Install tile at stair 3 wall			High Point										>	X	Х	Х	Х								
Install Casework in Science Rooms	Post Window Install		NEIS Casework						 X	X		× ×													
Install Pipe grid in Steam room Building D - Electrical Closet 1268			Berlin Steel						X	X	X .	X X	>												
Install Electric Tubs			WJ Griffin	X	X	Х	X	X																	
Install OH Conduits			WJ Griffin					X																	
Pull Feeders/Branch Wire			WJ Griffin						Х	Х	X	х х	>	X	Х	Х									
Install Panel Interiors			WJ Griffin						Х	Х	X	х х	>	Х	Х	Х	Х								
Terminate & Test Panels			WJ Griffin						 																
Start Up & Test Building D - MDF Room 1269			WJ Griffin																						
Build Out			WJ Griffin	X	X	Х	X	X																	
Building E - 2nd Floor/Media Center				~	~																				
Install MEP Drops to ACT grid			MEP Trades						Х	Х	X	х х	>	X	Х										
Install light fixtures in ACT ceilings	Pending missing light fixtures		WJ Griffin						Х	Х	X	х х	>	Х	Х										
Flood ACT Ceilings			K&K	-						+						X			Х	Х	Х	Х	Х		
Install light fixtures in soffits Board Soffits in media center	Pending missing light fixtures		WJ Griffin Century				+			+			>		X	X	Х								
Tape & Sand Soffits			Century	X	X	Х	X	X	X	Х	x														
Prime & First Coat Soffits			King									x x													
Building E - 1st Floor/Dining Commons																									
Install Stair 4			Berlin Steel										>	X	Х	Х	Х		Х	Х	Х				
Place Stair Pans at Stair 4			Riggs		V			X			~				_	_						Х	Х		
Polish Concrete in Dining Commons			Kaloutas	X	X	X	Х	X	X	Х	X														
Building E - Kitchen Install Epoxy Floor in Kitchen			NE Decks & Floors	Y	Y	Y	X	X																	
Install Epoxy Floor in Ritchen			Kitteridge	^	^	^		X	Х	X															
Install Coiling Doors			Overhead Doors																Х	Х	Х	Х	Х		
Install ACT Ceiling Grid			K&K								X	х х													
MEP Drops to ACT grid			MEP Trades	_								Х	>	Х	Х	Х	Х								
Install Light Fixtures in ACT			WJ Griffin							+		Х	>	X	Х	Х	Х		V	~	~				
Flood ACT Ceilings Install kitchen equipment			K&K Kitteridge				+			+				_	_	_			Х	X	X				
Install kitchen equipment			Kitteridge				+		-	+												Х	X		X
Building E - Electrical Room 1139			- Attendge																			~	~		

Consigli Construction - Sharon	High School P	Project																						
Lookahead Schedule																								
3/21/2022	-																							
Description of Work	Notes	P6 Activity % Code Comp	<u>Responsibility</u>	3/21 M		3/23 W		/25 3/26 FR S		+		31 4/1 R FR			4/5 T			4/8 FR	 	11 4/12 1 T		4/14 TR		4/17 4/18 S M
Install Electrical Tubs Install OH Conduits			WJ Griffin WJ Griffin	Х	Х	Х	Х	Х		X	X X	<u>к х</u>												
Pull Feeders/Branch Wire			WJ Griffin						^					Х	Х	Х	Х	Х	>	x x	Х	Х	Х	
Install Panel Interiors			WJ Griffin																	X X		Х	X	Х
Terminate & Test Panels			WJ Griffin																					
Start Up & Test Building E - Emergency Electrical Room 1140			WJ Griffin																					
Install Electrical Tubs			WJ Griffin	X	Х	Х	Х	X																
Install OH Conduits			WJ Griffin			~	~	~	Х	Х	X X	< X												
Pull Feeders/Branch Wire			WJ Griffin								ХХ	< X		Х	Х	Х	Х	Х	>	(X	Х	Х	Х	
Install Panel Interiors			WJ Griffin																 >	(X	Х	Х	Х	 Х
Terminate & Test Panels Start Up & Test			WJ Griffin WJ Griffin																					
Building E - MDF Room 1145			wy Grinni																					
Build out			WJ Griffin																					
Building F - Lockerooms & Community Education																								
OH Building Inspection in Hard Ceilings			000									Х												
Board Hard Ceilings			Century											Х	Х									
Tape Hard Ceilings			Century													Х	Х	Х						
Pime & First coat Hard Ceilings			King																>	(X	Х			
Install Casework in misc. Building F1 Rooms			NEIS Casework		Х																			
MEP Drops to ACT ceiling grid West of gym			MEP Trades	Х				Х	Х			K X												
MEP Drops to ACT ceiling grid in community education			MEP Trades	Х	Х	Х	Х	Х	Х	Х	X X	K X												
Install light fixtures in community education	Pending missing light fixtures		WJ Griffin																 					
Flood ACT Ceilings			K&K																					
Building F - GYM Prep & Paint Gym Elevated track rails			King	X	Х	X	Х	X	Х	X														
Complete electrical rough OH Gym			WJ Griffin				X		X		X X	< X		Х	х	Х	Х	Х						
Tape & sand east wall of gym			Century		Х																			
Prime & First coat east wall of gym			King			Х	Х	Х	Х															
Paint Underside of elevated track deck			King						Х	Х		X X							 					
Install Corners Gym Elevated Track Rails Install Gym Equipment	Need Delivery Date		Berlin Steel Pappas						X	X		X X		х	x	X	Х	X						
Install Gym Floor	Delivery 4-12-22		Kenvo						^	^	^ ^			^	~	~	~	^						
Building F - Main Lobby																								
Tape and Sand wall west of lobby			Century						Х	Х	ХХ	< X												
Prime and first coat wall west of main lobby			King									_		Х	Х	Х		_						
Building F - IDF Room 1113			W L Criffin	V	V	V	V	V	V	×	× ×	< X												
Build out Building F - Stair 6			WJ Griffin	~	~	~	Х	^	~	^	<u>^ X</u>													
Board Stairwell Walls			Century			Х	Х	X	Х	Х	Х													
Tape/Sand Stairwell Walls			Century								X X	< X												
Prime/First Coat Walls			King		<u> </u>					[_]				Х										
Install ACT grid Install Light Fixtures			K&K WJ Griffin		+					+				Х	Х	X X	Y			_	-			
Install Light Fixtures Install MEP Drops to Grid			MEP Trades														X							
Flood ACT Ceilings			K&K		1												X	Х				-		
Remove Staging on/over Stair 6			Century																>	(
Install Handrails			Berlin Steel							<u> </u>														
Clean Stair risers and treads Install Rubber treads			Riggs Capital Carpet							+														
Building F - Stair 1			Capital Carpet																					
Erect Staging on/over Stair 1			Century								X X	<												
Board Stairwell Walls			Century									X		Х	Х	Х								
Tape/Sand Stairwell Walls			Century														Х	Х						
Install interior phenolic panel at stairwell wall			Riggs																>	(X	_			
Prime/First Coat Walls Install ACT grid			King K&K		-					+											_			
Install Light Fixtures			WJ Griffin							+														
Install MEP Drops to Grid			MEP Trades		1																			
Flood ACT Ceilings			K&K																					

Consigli Construction - Sharon	High School P	Project																											٦
Lookahead Schedule		юјест																											_
3/21/2022																													
		P6 Activity	%		3/21	3/22 3	3/23 3/24	3/25	3/26	3/27 3	/28 3/2	9 3/30	3/31	4/1	4/2	4/3	4/4	4/5 4/	6 4/7	7 4/8	4/9	4/10	4/11 4	/12 4/	/13 4/14	4/15	4/16 4	1/17 4/1	18
Description of Work	Notes	Code	Comp	<u>Responsibility</u>	M		W TR				M T			FR						R FR		S			W TR			S N	Λ
Remove Staging on/over Stair 6 Install Handrails				Century Berlin Steel																						-		_	_
Clean Stair risers and treads				Riggs																									
Install Rubber treads				Capital Carpet																									_
Install Zen garden under stair 1 Building G North of Auditorium - 2nd Floor																													
Install Wall Tile in Hallway				High Point							х х	Х	Х	Х						X									
Install Wall Tile in Bathrooms Install Ceiling Grid in hallway				High Point	V	v	x x	v			X X	Х	Х	Х			Х	X X	(
Install Sprinkler Drops to ACT Grid				K&K JCI	~	~	<u> </u>	^																					
Install Duct Drops to ACT Grid				Арех																									_
Install HVAC Drops to ACT grid Install Light Fixtures in ACT	Des dies Liebt Sixtee Delivere			NBK WJ Griffin	_																								_
Complete MEP Drops in ACT	Pending Light Fixture Delivery			MEP Trades																									
Building G North of Auditorium - 1st Floor																													
Install Epoxy Floors				NE Decks & Floors			~				X X	Х	Х	Х			Х	Х											\square
Install Casework in misc. Building G1 Rooms Install MEP Drops to ACT Grid				NEIS Casework MEP Trades	Х	Х	х	-				_														+ +			-
Install Light Fixtures	Pending Light Fixture Delivery			WJ Griffin																									
Flood ACT Ceilings	Pending Light Fixture Delivery			MEP Trades																									
Install Pipe Grid in Innovation Lab				Berlin Steel													Х	X X	(X	X									_
Building G - Auditorium & Mezzanine Layout Clouds and install air craft cable				K&K	X	Х	X X	Х			ХХ	X	X	Х															_
Install OH Electrical Rough to boxes above clouds	House lights/AV/Theatrical			WJ Griffin	X		x x							X															
Install OH ductwork drops				Apex					Х		x x	Х	Х	Х			Х	X X	(
Install OH Clouds				K&K															Х	X					х х				Х
Drop Sprinkler Heads in Clouds Install light fixtures at cloud level				JCI WJ Griffin																X			X		X X X X	X		×	
Tape & Sand walls at stage and diffusers				Century	Х	X	X X	X											^				^	<u> </u>	^ ^	^			<u>`</u>
Complete in-wall rough in mezzaine walls				WJ Griffin	Х	Х																							
Board & Insulate mezzainine walls Complete in-wall rough in walls below mezzaine				Century WJ Griffin			X X	X			X X	X	Х	Х												-			_
Board & Insulate walls below mezzainine				Century							x x	Х	Х	Х															
Install Block Filler at stage				King				Х			х х	Х																	
Paint OH Structure Counterweight rigging installation - Phase 1	Start 5/3/22			King Texas Scenic													Х	X X	X	X						-			_
Counterweight rigging installation - Phase 1	Start 5/17/22			Texas Scenic																									
Counterweight rigging installation - Phase 3	Start 5/31/22			Texas Scenic																									
Motorized rigging installation - Phase 1 Track Installation	Start 6/14/2022 Start 4/28/2			Texas Scenic Texas Scenic																						-			_
Drapery Installation	Start 4/28/2 Start 7/18/22			Texas Scenic																									\neg
Install Stage Flooring	Start 6/21/22			Kenvo																									
Install Light Fixtures Install Auditorium Rails at Mezzanine	Start 7/20/22 Need Delivery Date			Texas Scenic Berlin Steel																						-			_
Install Auditorium Rails at Catwalks	Need Delivery Date			Berlin Steel																									
Install Stair 7	Need Delivery Date			Berlin Steel																									
Install Spiral Stair Building G - Black Box	Pending re-design			Berlin Steel																									
Insulate & Board Walls				Century	Х	Х	Х																						
Tape & Sand Walls				Century				Х			Х																		
Prime & First Coat Walls Tension Wire Grid Installation Phase 1	Start 4/5/2022			King Texas Scenic							X	X	X					v v		X									-
Tension Wire Grid Installation Phase 1 Tension Wire Grid Installation Phase 2	Start 4/5/2022 Start 4/19/22			Texas Scenic Texas Scenic								^	^	^						. ^									\neg
Install Blackbox wood flooring				Kenvo																									
Building G - Electrical Closet 2217				W(10-!!!!																									
Build out Building G - Stair 2				WJ Griffin																									
Complete Electrical Rough in Stair 2				WJ Griffin																									
Inwall Electrical inspection				WJ Griffin																									
Erect Staging on/over Stair 2 Board Stairwell Walls				Century Century																									-
		1		Century		1																							

Consigli Construction - Sharon	High School P	Project																					
Lookahead Schedule																							
3/21/2022																							_
Description of Work	Notes	P6 Activity % Code Comp	Responsibility	3/21 M	1	3/23 3/ W 1		 3/27 S	3/28 M			l 4/1 FR	4/2 4	/3 4/4 S M	4/5 T		4/7 TR			1 4/12 I T	4/13 W		/17 4/18 S M
Tape/Sand Stairwell Walls			Century																			 	
Prime/First Coat Walls Install ACT grid			King K&K																				
Install Light Fixtures			WJ Griffin																				
Install MEP Drops to Grid			MEP Trades K&K																				
Flood ACT Ceilings Remove Staging on/over Stair 2			Century																				
Install Handrails			Berlin Steel																				
Clean treads and risers Install Rubber treads			Riggs																			-	
Building A - 2nd Floor																							
Install Channels at Stair 8	Delivery 3-28-22		Berlin Steel	~																			
Install OH Ductwork Tape and sand Walls			Apex Century	Х	Х	X	X X		X	Х	X X	X											
Prime & First Coat Walls			King	Х	Х	Х	x x																
Install Wall Tile in Bathrooms			High Point	Х	Х	Х	X X		V	V	VV	V											
Install Wall Tile in Hallway Install ACT Ceiling Grid Classrooms & Science Rooms			High Point K&K						X X	X X		X		X	x	x	Х	x		_			
Install ACT Grid in high hallway ceilings			K&K							X		~		X									
Install MEP Drops to ACT Ceiling Grid			MEP Trades																				
Install Light Fixtures in ACT ceilings Flood ACT Ceilings	Pending Light Fixture Delivery		WJ Griffin K&K																				
Frame Hard Ceilings			Century						Х	Х													
Install MEP Drops to hard ceilings			MEP Trades								X X			X									
Install Light fixtures in hard ceilings Board Hard Ceilings			WJ Griffin Century								X X	Х		X	Х	Х	Х						
Tape & Sand Hard Ceilings			Century															Х					
Install Epoxy Floors			NE Decks & Floors						-														
Install Casework Building A - 1st Floor			NEIS Casework																				
Install OH Ductwork			Apex				х х		Х	Х	х х	Х											
Insulate & Board Walls Tape and sand Walls			Century Century	X			X X X X		v	X													
Prime & First Coat Walls			King	^	^		<u>^ ^</u> X X		X		x x	X										-	
Install Wall Tile in Bathrooms			High Point				Х		Х	Х	х х	Х											
Install Epoxy Floors in Bathrooms Install Wall Tile in Hallway			NE Decks & Floors High Point											X		x	Х	x					
Install ACT Ceiling Grid Classrooms & Science Rooms			K&K											X	X	X	X					-	
Install ACT Grid in high hallway ceilings			K&K																				
Install MEP Drops to ACT Ceiling Grid Install Light Fixtures in ACT ceilings	Pending Light Fixture Delivery		MEP Trades WJ Griffin																				
Flood ACT Ceilings	- enang Light Fixture Delivery		K&K																				
Frame Hard Ceilings			Century																				
Install MEP Drops to hard ceilings Install Light fixtures in hard ceilings			MEP Trades WJ Griffin																				
Board Hard Ceilings			Century																				
Tape & Sand Hard Ceilings			Century																				
Install Casework Frame soffit at stair 8 opening			NEIS Casework Century												-	+				-			
Building A - IDF Room 2319																							
Build out Building B - 2nd Floor			WJ Griffin																				
Install Channels at Stair 9	Delivery 4-4-22		Berlin Steel											X									
Install OH & Inwall Plumbing rough in science rooms &			Grasseschi	х																			
bathrooms Install OH Ductwork			Apex		X	x	x v		x	X	X Y	×		Y	×	Y	Х	x					
Install OH HVAC Pipe in science rooms & bathrooms			NBK	X		<u></u>										^							
Install OH & Inwall Electrical Rough in science rooms &			WJ Griffin	х																			
bathrooms MEP complete inwall install & insulation in science rooms &																							
bathrooms			MEP Trades	Х																			
Inwall Inspections Complete in science rooms & bathrooms			All Trades		X	V																	
Insulate & Board Walls in classrooms only			Century	Х	Х	Х																	

Consigli Construction - Sharon	High School	Project																						
Lookahead Schedule																								-+-
3/21/2022																								
Description of Work	Notes	P6 Activity Code	% Comp	<u>Responsibility</u>	3/21 M		3/23 3/24 W TR							4/3 S							¥/11 4/12 M T			4/17 4/18 S M
Insulate & Board Walls in science rooms & bathrooms			-	Century			ХХ	Х		ХХ	X X												 	•
Tape and sand Walls				Century			Х	Х		ХХ		X	Х	 										
Prime & First Coat Walls Install Wall Tile in Bathrooms				King High Point								X	X		X	X X	X X	X						
Install Wall Tile in Hallway				High Point							^		^		X	X	X	X	Х					
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K											Х	Х	Х	Х	Х					
Install ACT Grid in high hallway ceilings				K&K MEP Trades																				
Install MEP Drops to ACT Ceiling Grid Install Light Fixtures in ACT ceilings	Pending Light Fixture Deliver			WLP Trades WJ Griffin																				
Flood ACT Ceilings	T ending Light Fixture Deriver	y		K&K																				
Frame Hard Ceilings				Century																				
Install MEP Drops to hard ceilings				MEP Trades										 										
Install Light fixtures in hard ceilings Board Hard Ceilings				WJ Griffin Century																				
Tape & Sand Hard Ceilings				Century																				
Install Epoxy Floors				NE Decks & Floors																				
Install Casework				NEIS Casework																				
Install Stair 9				Berlin Steel																				
Building B - 1st Floor Install OH & Inwall Plumbing rough				Grasseschi	Х																			
Install OH Ductwork				Apex						X X	x x	X	Х		Х	Х	Х	Х	Х					
Install OH HVAC Pipe				NBK	Х																			
Inwall electrical rough				WJ Griffin	X																			
MEP complete inwall install & insulation Inwall Inspections Complete				MEP Trades All Trades	Х	X																		
Insulate & Board Walls				Century			X X	Х		X X	x x	x	Х		-									
Tape and sand Walls				Century				~							Х	Х	Х	Х	Х					
Prime & First Coat Walls				King																				
Install Wall Tile in Bathrooms				High Point																				
Install Wall Tile in Hallway Install ACT Ceiling Grid Classrooms & Science Rooms				High Point K&K										 										
Install ACT Grid in high hallway ceilings				K&K																				
Install MEP Drops to ACT Ceiling Grid				MEP Trades																				
Install Light Fixtures in ACT ceilings	Pending Light Fixture Deliver	у		WJ Griffin																				
Flood ACT Ceilings Frame Hard Ceilings				K&K Century											-									
Install MEP Drops to hard ceilings				MEP Trades											-									
Install Light fixtures in hard ceilings				WJ Griffin																				
Board Hard Ceilings				Century																				
Tape & Sand Hard Ceilings				Century																				
Install Epoxy Floors Frame soffit at stair 9 opening				NE Decks & Floors Century							_	_	-									-		
Board Soffit at Stair 8				Century																		1		
Tape & Sand Soffit at Stair 8				Century																				
Prime & First Coat Soffit at stair 8				King										 										
Install Casework Building B - IDF Room 2419				NEIS Casework																				
Build out				WJ Griffin																				
ROOFING & FAÇADE WORK																								
Building C																								
Install Remainder of Rooftop equipment				NBK	X																			
Test Marvin Windows in Building C				PMA/CCC																				
Install Marvin Windows 1st floor	Pending Testing Results			Chandler Architectural	Х	Х	X X	Х		ХХ														
Install Marvin Windows 2nd floor	Pending Testing Results	•		Chandler Architectural						X X	< X	X	Х		Х	X	X	Х	X			_		
Install Window Caulking				Armani						ХХ	X X	X	X		X	X	X X	X	X					
Install Drywall Returns at Marvin Windows on 1st Floor Install Drywall Returns at Marvin Windows on 2nd Floor				Century Century											~	^	^	^	~					
Install Clerestory Glass				Chandler Architectural									-											
First TAKTL Delivery				Riggs			Х	Х																
Install TAKTL Panels on East and South Facades				Riggs						X X	< X	X	X		X	X	X	X	X					
Install TAKTL Panels on Roof Clerestory				Riggs						X X	K X	. Х	Х		Х	Х	Х	Х	Х					

Constall Constantion Charan	Lligh Cabaal D)raia at																											
Consigli Construction - Sharon	n High School P	roject																											
Lookahead Schedule																													
					-										_														
3/21/2022																													
		P6 Activity	%		3/21	3/22	3/23	3/24	3/25	3/26	3/27 3	/28 3/2	9 3/3	30 3/3	4/1	4/2 4/3	3 4/4	4/5	4/6	4/7	4/8	4/9 4	/10 4/11	4/12	4/13	4/14	4/15	4/16 4/	17 4/18
Description of Work	Notes		Comp	<u>Responsibility</u>	M	T	W	TR	FR			M T				S S		Т	W	TR			<u>s</u> м		W				S M
Building D																													
Install phenolic Panel				Riggs	Х	Х	Х	Х	Х			х х	X X	(X	Х														
Install CW 11				Chandler Architectural								X X	X X	(X	Х		X	Х	Х	Х	Х								
Install Marvin Windows 1st floor	Pending Testing Results			Chandler Architectural	Х	Х	Х	Х	Х			X X	X X	(X	Х														
Install Marvin Windows 2nd floor	Pending Testing Results			Chandler Architectural								x x	x x	(X	Х		Х	Х	Х	Х	Х								
Caulk Marvin Windows				Armani								x x					Х	Х											
Install Drywall Returns at Marvin Windows on 1st Floor				Century															Х	Х	х								
Install Drywall Returns at Marvin Windows on 2nd Floor				Century															X	X	X								
Building E																													
Install Green roof rails	Delivery pushed from 2-28- 22			Berlin Steel	X																								
Install Roofing on South Green Roof				Capeway		Х																							
Complete remaining AVB at south elevation				Armani			Х	Х	Х																				
Install Phenollic Panel on South and west green roofs				Riggs								X X	X	(X	Х		Х	Х	Х		Х								
Install Phenolic Panel over CW 20				Riggs								X X	X	(X	Х		Х	Х	Х	Х	Х								
Install CW 07 & 14	Post Rail install on Green roof			Chandler Architectural								x x	x	x x	Х														
Install CW 20 Frame & Glass		**		Chandler Architectural	Х	Х	Х																						
Install silicone strip at CW 20				Armani				Х	Х			× ×	<hr/>	/ X/	X		_												
Install Clerestory above Dining Commons CW 03 Building F				Chandler Architectural								X X	X	(X	X														
Install P Windows				Chandler Architectural																									
Caulk P Windows				Armani																									
Install Drywall Returns on P Windows				Century													-												
Install phenolic panel at North Façade				Riggs	X	x	Х	Х	x																				
Adjust steel at curtain wall 06				Berlin Steel	X			X	X																				
Install CW 06 & CW 01				Chandler Architectural													X	Х	Х	Х	х								
Install CW 27 & CW 23				Chandler Architectural																									
Caulk Windows around the gym				Armani	X	Х																							
Building G																													
Install Roof at G North Canopy				Capeway		Х	Х																						
Caulk H & I Windows				Armani	Х	Х	Х	Х	Х																				
Install CW 22 & CW 12				Chandler Architectural																									

Consigli Construction - Sharon	High School P	roject																															
Lookahead Schedule	-	-	Ĩ	1																													
3/21/2022																																	
Description of Work	Notes	P6 Activity	%	Responsibility	3/21	3/22	3/23	3/24	3/25	3/26	3/27	3/28	3/29	3/30	3/31	4/1	4/2	4/3	4/4	4/5	4/6	4/7	4/8	4/9	4/10	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18
Description of Work	Notes	Code	Comp	Responsibility	м	т	w	TR	FR	S	S	М	т	w	TR	FR	S	S	м	т	w	TR	FR	S	S	м	т	w	TR	FR	S	S	м
Install CW 18 & CW 13				Chandler Architectural																													
Building A																																	
Install TAKTL Panels on North and east elevations				Riggs																													
Install TAKTL Panels on Roof clerestory				Riggs																													
Install Marvin Windows	Pending Testing Results			Chandler Architectural																													
Install Window Caulking				Armani																													
Building B																																	
Install TAKTL Backup & Insulation				Riggs																													
Install TAKTL Panels on North and East elevations				Riggs																													
Install TAKTL Panels on Roof clerestory				Riggs																													
Install Marvin Windows	Pending Testing Results			Chandler Architectural																													
Install Window Caulking				Armani																													



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at https://www.shsbuilding.com/

Best Regards,

Matthew Gulino

Matthew Gulino Associate | Owner's Project Manager PMA Consultants mgulino@pmaconsultants.com
