

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- Temporary heaters are running on an as needed basis. See enclosed notice.
- The majority of mechanical equipment (RTU's etc.) has been set in place. Team is working towards equipment start up.
- Electrical switchgear is being assembled on-site and team is working towards permanent power.
- Sheetrock (including taping) will be complete in the coming weeks
- Finishes including paint, tile, epoxy flooring, concrete polishing, casework & ceiling grid are ongoing.
- Exterior panel systems installation (including metal & concrete) is ongoing.
- Window & curtainwall installation- including installation of glazing- is ongoing.
- Installation of kitchen equipment has started.
- Work at the athletic facility- including installation of concrete slabs- has resumed.
- Installation of gymnasium equipment -which will be followed by wood floor- has started.
- Installation of luxury vinyl tile (at classrooms) will begin in the coming weeks.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



PMA Consultants




TAPPÉ
ARCHITECTS



SHARON HIGH SCHOOL



LOGISTICS UPDATE
March 15, 2022

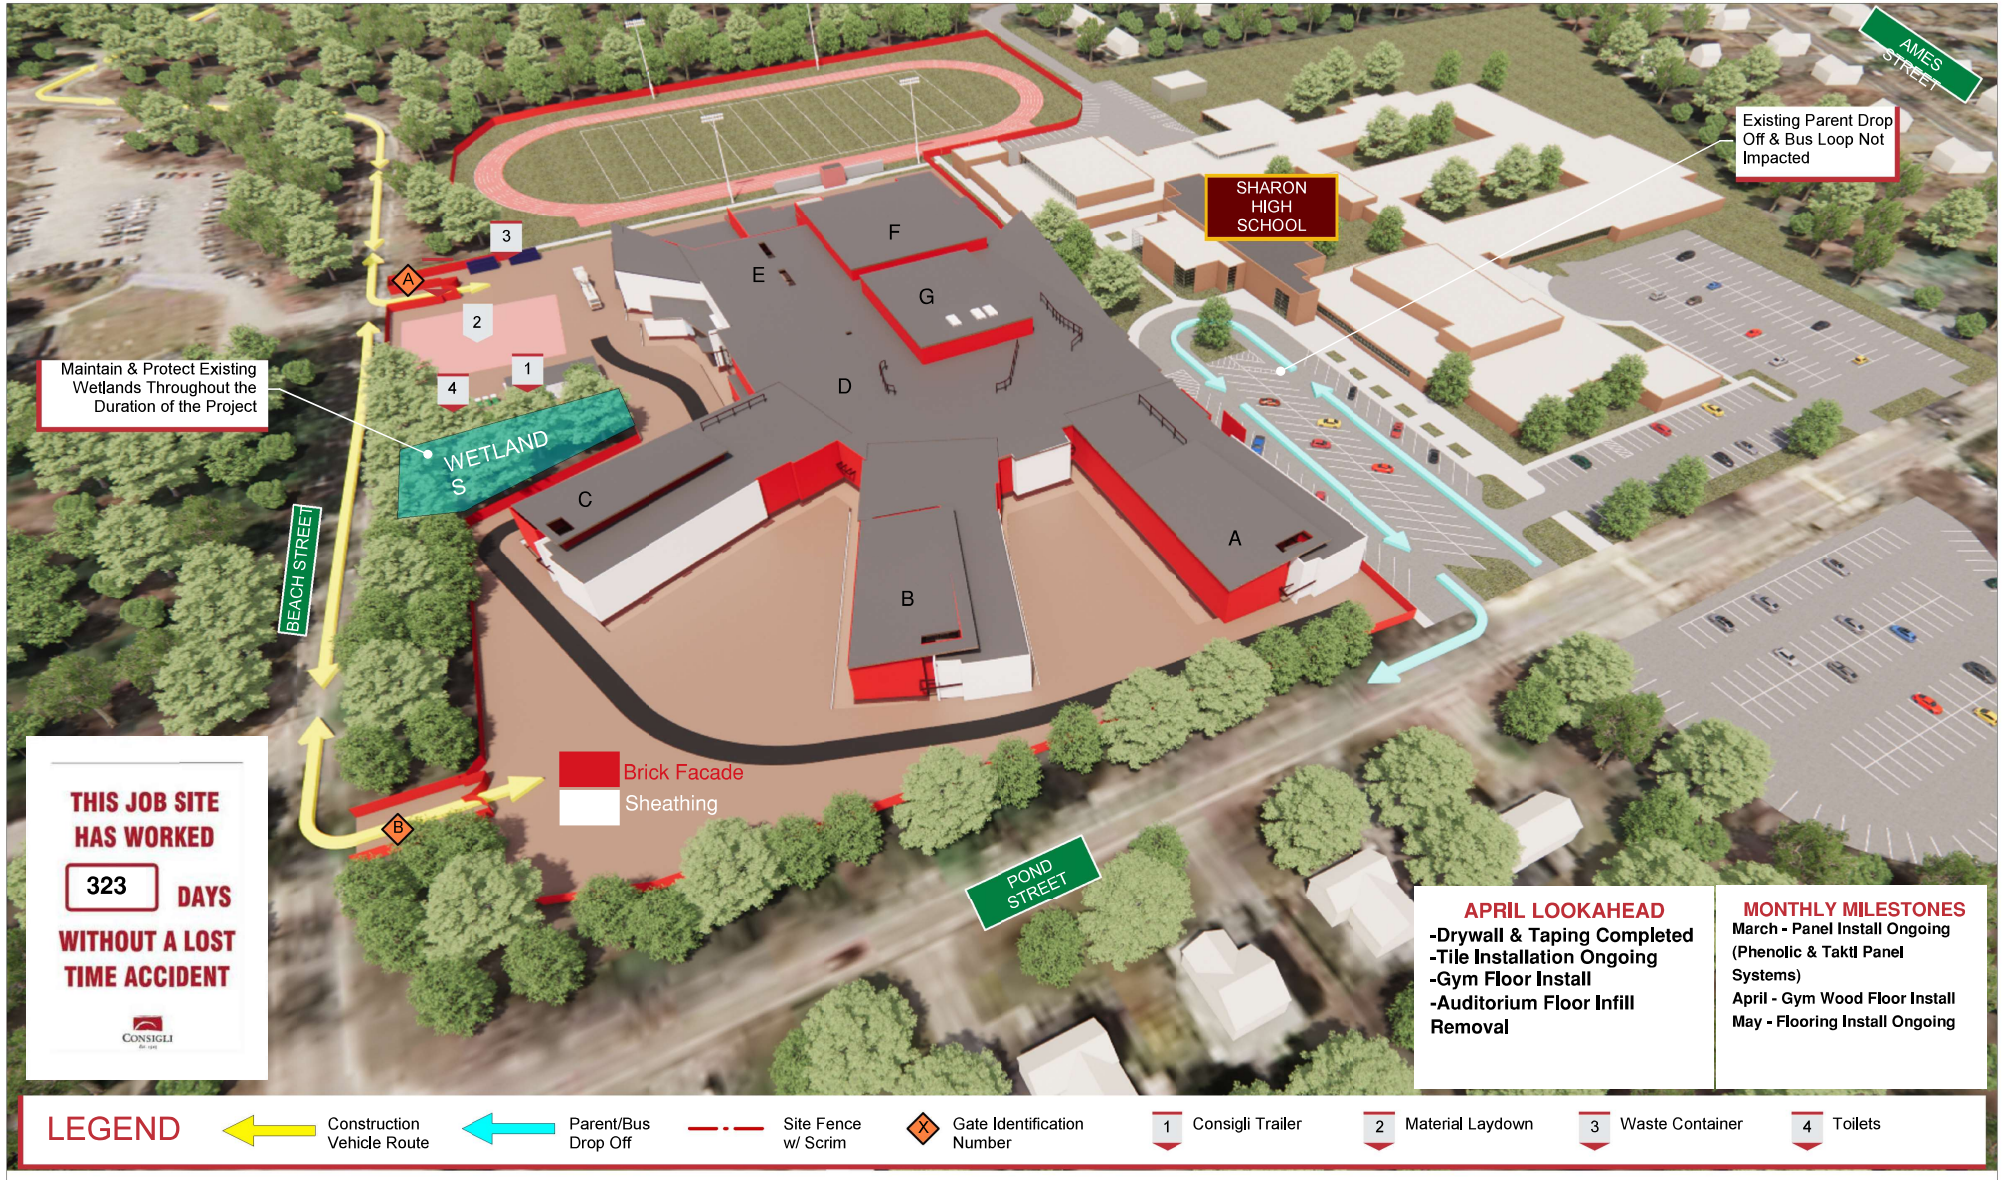

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

Existing Parent Drop Off & Bus Loop Not Impacted

THIS JOB SITE HAS WORKED
323 DAYS
WITHOUT A LOST TIME ACCIDENT

Brick Facade
 Sheathing

APRIL LOOKAHEAD
 -Drywall & Taping Completed
 -Tile Installation Ongoing
 -Gym Floor Install
 -Auditorium Floor Infill Removal

MONTHLY MILESTONES
 March - Panel Install Ongoing (Phenolic & Taktl Panel Systems)
 April - Gym Wood Floor Install
 May - Flooring Install Ongoing

- LEGEND**
- Construction Vehicle Route
 - Parent/Bus Drop Off
 - Site Fence w/ Scrim
 - Gate Identification Number
 - 1 Consigli Trailer
 - 2 Material Laydown
 - 3 Waste Container
 - 4 Toilets

Consigli Construction - Sharon High School Project

Lookahead Schedule

4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8				
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S				
SCHOOL SCHEDULE																																				
MILESTONES																																				
Dancefloor removal in Auditorium																																				
Install Gym Wood Floor	Pushed from 4-12 due to gym equipment deliery dates											X																								
HOLIDAYS																																				
WEATHER																																				
MOCK UP/THIRD PARTY ENVELOPE TESTING																																				
SITWORK & UTILITIES																																				
Install conduit & transformer pads				WJ Griffin																																
Install Remaining conduit for athletic facility				MAK																																
FOOTBALL FIELD																																				
Potential Re-Design of Pressbox Footings				CCC/Tappe																																
Form and install rebar for pressbox footings				Riggs																																
Place pressbox footings				Riggs																																
Form Piers at pressbox footings				Riggs																																
Place piers at pressbox footings				Riggs																																
Back fill pressbox footings				Vinagro																																
Install Press Box				Dant Clayton																																
ATHLETIC FACILITY BUILDINGS																																				
Install Roof Trusses				Century					X			X	X	X	X																					
Install Roof Framing				Century										X	X	X																				
Install Roofing				Capeway																X	X															
Install spray applied AVB on CMU Walls				Armani																	X	X						X	X							
Place Slabs	Pushed due to rain			Riggs				X														X	X					X	X							
Install Masonry Façade				Fernandes																			X										X			
INTERIOR FITOUT/OH ROUGH/FINISHES																																				
Building C - 2nd Floor																																				
Install Channels at Stair 10				Berlin Steel	X	X	X	X	X																											
Install Stair 10				Berlin Steel	X	X	X	X	X																											
Skim Patching in Classrooms				Silverback	X	X	X	X	X																											
Install Light Fixtures in classrooms				WJ Griffin								X	X	X	X	X																				
Complete Electrical/LV drops Drops in ACT				WJ Griffin								X	X	X	X	X																				
Install Ceiling grid in high hallway ceilings				K&K															X	X	X	X	X				X	X	X	X	X					
Returns at Clerestory - End of Bld				Century				X	X																											
Install APEX Duct drops in ACT	Awaiting delivery			Apex				X	X			X	X	X	X	X																				
Install Drywall returns at Marvins				Century				X	X			X	X	X																						
Flood Ceilings in Classrooms				K&K								X	X	X																						
Tape & Sand Drywall returns at Marvins				Century										X	X																					
Prep & Install LVT in Classrooms				Capital Carpet															X	X	X	X	X													
Building C - 1st Floor																																				
Install APEX Duct drops in ACT	Awaiting delivery			Apex				X	X			X	X	X	X	X																				
Complete Electrical/LV drops Drops in ACT				WJ Griffin								X	X	X	X	X																				
Install Light Fixtures in classrooms				WJ Griffin								X	X	X	X	X																				
Frame soffit around stair 10 channel				Century								X	X																							
Board soffit around stair 10 channel				Century										X																						
Tape & Sand soffit around stair 10 channel				Century											X	X																				
Prime & First Coat Soffit around stair 10 channel				King											X	X																				
Install Drywall returns at Marvins				Century				X	X			X	X	X																						
Tape & Sand Drywall returns at Marvins				Century										X	X																					
Flood Ceilings in Classrooms				K&K										X	X																					
Install wood slat ceiling in hallway				K&K								X	X	X	X	X			X	X	X	X	X													
Prep & Install LVT in Classrooms				Capital Carpet																			X	X					X	X	X					

Consigli Construction - Sharon High School Project
Lookahead Schedule
4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8				
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S				
Building C - IDF Room 2519																																				
Build Out				WJ Griffin																																
Building D - 2nd Floor																																				
Install Toilet Finishes				Grasseschi		X	X	X	X																											
Install MEP Drops to ACT grid				MEP Trades								X	X	X	X	X																				
Install electrical devices and light fixtures in ACT				WJ Griffin								X	X	X	X	X																				
Install Fumehoods				NEIS Casework	X	X																														
Install Casework in Science Rooms				NEIS Casework				X	X			X	X																							
Complete dywall returns at marvin woods in science rooms				Century				X																												
Tape returns at marvin windows				Century				X	X																											
Complete ACT grid in science rooms at Marvin windows				K&K					X																											
Flood ACT Ceilings				K&K								X	X																							
Skim Patching in Classrooms				Silverback	X	X	X																													
Prep & Install LVT in Classrooms				Capital Carpet														X	X	X	X	X														
Install Pipe grid in Steam room	Awaiting delivery			Berlin Steel																																
Building D - 1st floor																																				
Complete Duct Drops in ACT Grid				Apex																																
Install light fixtures in ACT ceilings				WJ Griffin								X	X	X	X	X																				
Flood ACT Ceilings				K&K																																
Install tile at stair 3 wall				High Point																																
Install Fumehoods				NEIS Casework	X	X																														
Install Casework in Science Rooms				NEIS Casework				X	X			X	X																							
Complete dywall returns at marvin woods in science rooms				Century				X																												
Tape returns at marvin windows				Century				X	X																											
Complete ACT grid in science rooms at Marvin windows				K&K					X																											
Install Casework in Science Rooms				NEIS Casework								X	X																							
Prep & Install LVT in Classrooms				Capital Carpet																		X	X				X	X	X							
Install Pipe grid in Steam room	Awaiting delivery			Berlin Steel																																
Building D - Electrical Closet 1268																																				
Install OH Conduits				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Pull Feeders/Branch Wire				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Install Panel Interiors				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Terminate & Test Panels				WJ Griffin																																
Start Up & Test				WJ Griffin																																
Building D - MDF Room 1269																																				
Build Out				WJ Griffin	X	X	X	X	X																											
Building E - 2nd Floor/Media Center																																				
Install MEP Drops to ACT grid				MEP Trades								X	X	X	X	X																				
Install light fixtures in ACT ceilings				WJ Griffin								X	X	X	X	X																				
Install light fixtures in soffits				WJ Griffin																																
Prime & First Coat Soffits & OH MEPs				King	X	X	X																													
Install K-13 on OH Sturcture				H.Carr																																
Flood ACT Ceilings				K&K																																
Building E - 1st Floor/Dining Commons																																				
Install Stair 4				Berlin Steel									X	X	X	X			X	X	X	X														
Place Stair Pans at Stair 4				Riggs																			X													
Building E - Kitchen																																				
Install Coiling Doors				Overhead Doors								X	X	X	X	X																				
Install ACT Ceiling Grid				K&K	X	X	X	X	X																											
MEP Drops to ACT grid				MEP Trades								X	X	X	X	X																				
Install Light Fixtures in ACT				WJ Griffin								X	X	X	X	X																				
Flood ACT Ceilings				K&K															X	X	X	X	X				X	X	X	X	X					
Install 2 remaining panels in kitchen	Pending Delivery			WJ Griffin																																
Install kitchen equipment				Kitteridge																							X	X	X	X	X					
Install walk-ins				Kitteridge																																
Building E - Electrical Room 1139																																				
Pull Feeders/Branch Wire				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Install Panel Interiors				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Terminate & Test Panels				WJ Griffin																																
Start Up & Test				WJ Griffin																																

Consigli Construction - Sharon High School Project
 Lookahead Schedule
 4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8				
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S				
Building E - Emergency Electrical Room 1140																																				
Install OH Conduits				WJ Griffin																																
Pull Feeders/Branch Wire				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Install Panel Interiors				WJ Griffin	X	X	X	X	X			X	X	X	X	X																				
Terminate & Test Panels				WJ Griffin																																
Start Up & Test				WJ Griffin																																
Building E - MDF Room 1145																																				
Build out				WJ Griffin																																
Building F - Lockerooms & Community Education																																				
Tape Hard Ceilings				Century			X	X	X																											
Prime & First coat Hard Ceilings				King								X	X	X																						
MEP Drops to ACT ceiling grid West of gym				MEP Trades																																
MEP Drops to ACT ceiling grid in community education				MEP Trades																																
Install light fixtures in community education				WJ Griffin																																
Flood ACT Ceilings				K&K																																
Building F - GYM																																				
Install Gym Equipment				Pappas	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X													
Install Gym Floor	Delivery 4/21			Kenvo										X	X			X	X	X	X	X					X	X	X	X	X					
Building F - Main Lobby																																				
Install Wall tile in main lobby				High Point								X	X	X	X	X																				
Tape and Sand main lobby walls for paint				Century				X	X			X	X	X	X	X																				
Prime and first coat wall west of main lobby				King										X	X	X																				
Building F - IDF Room 1113																																				
Build out				WJ Griffin																																
Building F - Stair 6																																				
Install Handrails				Berlin Steel																																
Clean Stair risers and treads				Riggs																																
Install Rubber treads				Capital Carpet																																
Building F - Stair 1																																				
Board Stairwell Walls				Century			X	X	X																											
Tape/Sand Stairwell Walls				Century								X	X																							
Install interior phenolic panel at stairwell wall				Riggs										X	X	X																				
Prime/First Coat Walls				King															X	X	X															
Install ACT grid				K&K																		X	X													
Install Light Fixtures				WJ Griffin																			X	X			X	X								
Install MEP Drops to Grid				MEP Trades																																
Flood ACT Ceilings				K&K																																
Remove Staging on/over Stair 6				Century																																
Install Handrails				Berlin Steel																																
Clean Stair risers and treads				Riggs																																
Install Rubber treads				Capital Carpet																																
Install Zen garden under stair 1																																				
Building G North of Auditorium - 2nd Floor																																				
Install Ceiling Grid in hallway				K&K	X	X	X	X	X																											
Install Sprinkler Drops to ACT Grid				JCI								X	X																							
Install Duct Drops to ACT Grid				Apex																																
Install HVAC Drops to ACT grid				NBK																																
Install Light Fixtures in ACT				WJ Griffin																																
Complete MEP Drops in ACT				MEP Trades																																
Rm 2218 Install Panel & Fit out				WJ Griffin	X	X	X	X	X																											
Building G North of Auditorium - 1st Floor																																				
Installing Elevator 2				Delta Beckwith	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X					
Install MEP Drops to ACT Grid				MEP Trades																																
Install Light Fixtures				WJ Griffin																																
Flood ACT Ceilings				MEP Trades																																
Install Pipe Grid in Innovation Lab	Need delivery date			Berlin Steel																																
Building G - Auditorium & Mezzanine																																				
Complete paint on stage side wall to allow for cloud install				King	X	X																														
Install OH ductwork drops				Apex			X	X	X			X	X	X	X	X			X	X	X	X	X													
Install OH Clouds				K&K			X	X	X			X	X	X	X	X			X	X	X	X	X													

Consigli Construction - Sharon High School Project
 Lookahead Schedule
 4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8	
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
Drop Sprinkler Heads in Clouds				JCI			X	X	X			X	X	X	X	X			X	X	X	X	X										
Install light fixtures at cloud level				WJ Griffin	X	X	X	X	X			X	X	X	X	X																	
Tape & Sand Walls Under Mezzanine				Century	X	X	X	X																									
Paint OH Structure at stage				King					X																								
Counterweight rigging installation - Phase 1	Start 5/3/22			Texas Scenic																													
Counterweight rigging installation - Phase 2	Start 5/17/22			Texas Scenic																													
Counterweight rigging installation - Phase 3	Start 5/31/22			Texas Scenic																													
Motorized rigging installation - Phase 1	Start 6/14/2022			Texas Scenic																													
Track Installation	Start 4/28/2			Texas Scenic																													
Drapery Installation	Start 7/18/22			Texas Scenic																													
Install Stage Flooring	Start 6/21/22			Kenvo																													
Install Light Fixtures	Start 7/20/22			Texas Scenic																													
Install Auditorium Rails at Mezzanine	Need Delivery Date			Berlin Steel																													
Install Auditorium Rails at Catwalks	Need Delivery Date			Berlin Steel																													
Install Stair 7	Need Delivery Date			Berlin Steel																													
Install 2 Ships ladders to catwalks on stage	Need Delivery Date			Berlin Steel																													
Building G - Black Box																																	
Install OH Duct off catwalk & 1st floor slab				Apex	X	X																											
Install House Lights				WJ Griffin	X	X	X	X	X																								
Paint OH Structure in Black box				King						X																							
Prep & Paint black box theatre rails				King				X	X	X																							
Tension Wire Grid Installation Phase 1				Texas Scenic								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Tension Wire Grid Installation Phase 2				Texas Scenic																													
Protect Tension wire grid																																	
Install theatrical lights at tension wire grid				WJ Griffin																													
Install Blackbox wood flooring				Kenvo																													
Building G - Electrical Closet 2217																																	
Build out				WJ Griffin																													
Building G - Stair 2																																	
Erect Staging on/over Stair 2				Century																													
Board Stairwell Walls				Century																													
Tape/Sand Stairwell Walls				Century																													
Prime/First Coat Walls				King																													
Install ACT grid				K&K																													
Install Light Fixtures				WJ Griffin																													
Install MEP Drops to Grid				MEP Trades																													
Flood ACT Ceilings				K&K																													
Remove Staging on/over Stair 2				Century																													
Install Handrails				Berlin Steel																													
Clean treads and risers				Riggs																													
Install Rubber treads																																	
Building A - 2nd Floor																																	
Install Casework				NEIS Casework	X	X	X	X	X																								
Install Wall Tile in Bathrooms				High Point	X	X	X	X	X			X	X	X	X	X																	
Install Wall Tile in Hallway				High Point	X	X	X	X	X																								
Install Channels at Stair 8				Berlin Steel																													
Board Hard Ceilings				Century								X																					
Tape & Sand Hard Ceilings				Century									X	X																			
Install Epoxy Floors				NE Decks & Floors											X	X		X	X	X	X	X											
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K																													
Install ACT Grid in high hallway ceilings				K&K																													
Install MEP Drops to ACT Ceiling Grid				MEP Trades																													
Install Light Fixtures in ACT ceilings				WJ Griffin																													
Flood ACT Ceilings				K&K																													
Install MEP Drops to hard ceilings				MEP Trades																													
Building A - 1st Floor																																	
Install OH Ductwork				Apex	X	X	X	X	X																								
Prime & First Coat Walls				King	X	X	X	X	X																								
Install Wall Tile in Bathrooms				High Point								X	X	X	X	X																	
Install Wall Tile in Hallway				High Point								X	X	X	X	X																	
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K			X	X	X			X	X	X	X	X																	

Consigli Construction - Sharon High School Project
 Lookahead Schedule
 4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8		
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S		
Install ACT Grid in high hallway ceilings				K&K																														
Install MEP Drops to ACT Ceiling Grid				MEP Trades																														
Install Light Fixtures in ACT ceilings				WJ Griffin																														
Flood ACT Ceilings				K&K																														
Install MEP Drops to hard ceilings				MEP Trades																														
Install Light fixtures in hard ceilings				WJ Griffin																														
Board Hard Ceilings				Century									X																					
Tape & Sand Hard Ceilings				Century									X	X	X																			
Install Epoxy Floors				NE Decks & Floors																														
Install Casework				NEIS Casework											X	X			X	X	X													
Frame soffit at stair 8 opening				Century																														
Building A - IDF Room 2319																																		
Tape & Sand IDF Room				Century	X	X	X																											
Prime & First Coat IDF Room				King				X	X																									
Install Plywood in IDF Room				Century	X	X	X																											
Install Cable Tray				WJ Griffin								X	X																					
Pull cable to tray				WJ Griffin								X	X	X	X	X																		
Install Split HVAC Unit				NBK																														
Install Ceiling				K&K																														
Building B - 2nd Floor																																		
Install Channels at Stair 9				Berlin Steel																														
Install OH Ductwork				Apex	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X			
Tape and sand Walls				Century	X	X	X	X	X																									
Prime & First Coat Walls				King								X	X	X	X	X																		
Install Wall Tile in Bathrooms				High Point															X	X	X	X	X											
Install Wall Tile in Hallway				High Point															X	X	X	X	X											
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K															X	X	X	X	X			X	X	X	X	X				
Install ACT Grid in high hallway ceilings				K&K																														
Install MEP Drops to ACT Ceiling Grid				MEP Trades																														
Install Light Fixtures in ACT ceilings				WJ Griffin																														
Flood ACT Ceilings				K&K																														
Frame Hard Ceilings				Century																														
Install MEP Drops to hard ceilings				MEP Trades																														
Install Light fixtures in hard ceilings				WJ Griffin																														
Board Hard Ceilings				Century																														
Tape & Sand Hard Ceilings				Century																														
Install Epoxy Floors				NE Decks & Floors								X	X	X	X																			
Install Casework				NEIS Casework																														
Install Stair 9				Berlin Steel																														
Building B - 1st Floor																																		
Install OH Ductwork				Apex	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X			
Install OH HVAC Pipe				NBK	X	X	X	X	X																									
MEP complete inwall install & insulation				MEP Trades																														
Tape and sand Walls				Century	X	X	X	X	X			X	X	X																				
Prime & First Coat Walls				King															X	X	X	X	X				X	X	X	X	X			
Install Wall Tile in Bathrooms				High Point																							X	X	X	X	X			
Install Wall Tile in Hallway				High Point																							X	X	X	X	X			
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K																														
Install ACT Grid in high hallway ceilings				K&K																														
Install MEP Drops to ACT Ceiling Grid				MEP Trades																														
Install Light Fixtures in ACT ceilings				WJ Griffin																														
Flood ACT Ceilings				K&K																														
Frame Hard Ceilings				Century																														
Install MEP Drops to hard ceilings				MEP Trades																														
Install Light fixtures in hard ceilings				WJ Griffin																														
Board Hard Ceilings				Century																														
Tape & Sand Hard Ceilings				Century																														
Install Epoxy Floors				NE Decks & Floors										X	X	X			X															
Frame soffit at stair 9 opening				Century																														
Board Soffit at Stair 9				Century																														
Tape & Sand Soffit at Stair 9				Century																														

Consigli Construction - Sharon High School Project
 Lookahead Schedule
 4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Prime & First Coat Soffit at stair 9				King																												
Install Casework				NEIS Casework																												
Building B - IDF Room 2419																																
Install Plywood at IDF Room				Century	X	X	X																									
Paint Plywood				King				X	X																							
Install Cable Tray				WJ Griffin								X	X	X	X	X																
Pull Cable to IDF				WJ Griffin			X	X	X			X	X	X	X	X										X	X	X	X	X		
ROOFING & FAÇADE WORK																																
Building C																																
Install Marvin Windows 1st floor @ Science Room				Chandler Architectural		X	X																									
Install Marvin Windows 2nd floor @ Science Room				Chandler Architectural		X	X																									
Install Window Caulking				Armani	X	X	X																									
Install Drywall Returns at Marvin Windows on 1st Floor				Century	X	X	X	X	X																							
Install Drywall Returns at Marvin Windows on 2nd Floor				Century	X	X	X	X	X									X	X	X	X	X				X	X	X	X	X		
Install TAKTL Panels on East and South Facades				Riggs	X	X	X	X	X																							
Install TAKTL Panels on Roof Clerestory				Riggs								X	X	X	X	X																
Building D																																
Install CW 11 Frame & Glass				Chandler Architectural				X	X																							
Building E																																
Install Phenolic Panel on South and west green roofs				Riggs	X	X	X																									
Install MCM Panel over CW 20				Riggs																												
Install CW 07 & 14 glass				Chandler Architectural	X	X	X																									
Install CW 20 Glass				Chandler Architectural								X	X	X	X	X																
Install silicone strip at CW 20				Armani																												
Building F																																
Caulk P Windows				Armani		X																										
Complete AVB at CW 06 Opening				Armani	X	X																										
Install Drywall Returns on P Windows				Century																												
Complete sheathing at CW 06 Opening				Century	X	X	X	X	X																							
Install phenolic panel at North Façade				Riggs	X	X	X	X	X			X	X																			
Install CW 06				Chandler Architectural														X	X	X	X	X										
Install CW 01				Chandler Architectural																						X	X	X	X	X		
Install CW 27 & CW 23				Chandler Architectural																					X	X	X	X	X			
Building G																																
Install CW 22 & CW 12				Chandler Architectural								X	X	X	X	X																

Consigli Construction - Sharon High School Project
 Lookahead Schedule
 4/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	4/11	4/12	4/13	4/14	4/15	4/16	4/17	4/18	4/19	4/20	4/21	4/22	4/23	4/24	4/25	4/26	4/27	4/28	4/29	4/30	5/1	5/2	5/3	5/4	5/5	5/6	5/7	5/8
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Install CW 18 & CW 13				Chandler Architectural								X	X	X	X	X																
Building A																																
Install TAKTL Panels on North and east elevations				Riggs																												
Install TAKTL Panels on Roof clerestory				Riggs																												
Install Marvin Windows				Chandler Architectural	X	X	X	X	X																							
Install Window Caulking				Armani								X	X	X	X	X																
Building B																																
Install TAKTL Panels on North and East elevations				Riggs																						X	X	X	X	X		
Install TAKTL Panels on Roof clerestory				Riggs																												
Install Marvin Windows				Chandler Architectural								X	X	X	X	X																
Install Window Caulking				Armani															X	X	X	X	X									



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
