The Sharon High School Construction Project

4 Week Look Ahead Schedule 05/03/2021

- Upcoming Activities Include:
 - Concrete foundations are substantially complete
 - \circ Structural steel erection, decking, detailing & associated deliveries are ongoing
 - Placement of our first concrete slab is scheduled to occur in the next two weeks. Preparation of concrete slabs will continue to follow steel erection
 - $\circ~$ Roofing and associated prep activities are scheduled to begin during this period
 - Underground plumbing work is ongoing
 - \circ Construction at the track and football field is beginning on 4/26- see enclosed notice for details
 - See attached progress update
 - $\circ~$ See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/















Sharon High School: Upcoming Closure of Track & Football Field

Notice Date: April 5, 2021

Sharon High School Community:

In the coming weeks Consigli Construction will be moving to their next phase of construction which includes beginning work at the Sharon High School track & football field. This work will require that these areas are closed to public use/access. The phased closing of this area is as detailed below:

- <u>April 26th</u> Erosion Control will be installed (no impact to field use)
- <u>May 3rd</u> We will begin temp fencing surrounding the perimeter of the existing fencing (no impact to field use. Once the fencing is installed there will only be field access from the Ames Court side of the site)
- <u>May 17th</u> Site work will start, track and field will be off limits to all staff/ student/ public, gates will be locked

The project team would also like to take the opportunity to thank you for your continued support throughout this project.

For the latest on Sharon High School construction please visit the project's website at https://www.shsbuilding.com/


Best Regards,

Matthew Gulino

Matthew Gulino Associate | Owner's Project Manager PMA Consultants <u>mgulino@pmaconsultants.com</u>

Sharon High School



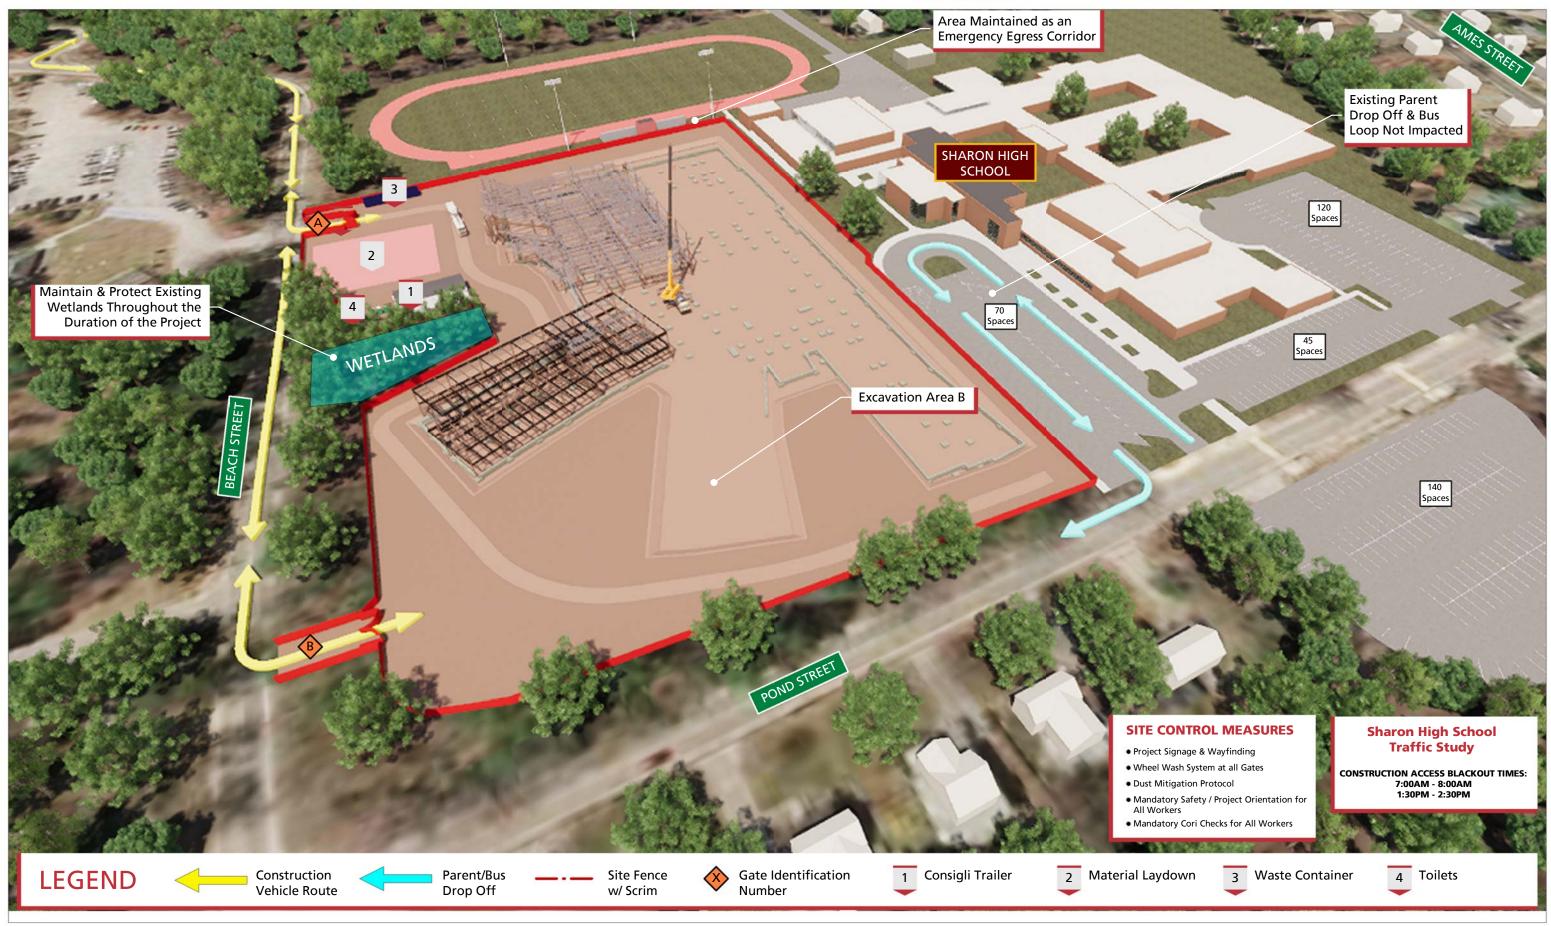

																			,							
		LOOK AHEAD SC 5/3/2021	HEDULE																	 						
Description of Work Not	es P6 Act Coc		ility 5/3 M		5/5 W	5/6 TR	5/7 FR	5/8 1	5/9 S			5/12 W		5/15 5/1 1 S			1		5/21 5/ FR ²						5/28 5 FR	5/29 5/30 1 S
School Schedule		SHADON				V	V			V	V	V	X X				X	V	V		V	X	V	V	× I	
Students onsite in school session		SHARON SHARON		X	X	X	X			X	X	X	X X		X	X	X	X	<u> </u>		X	X	X	<u> </u>	X	
Fully remote day Early Release Day		SHARON																	-							
MILESTONES		SHARON																								
Foundation Placement Complete 4/30/21		Riggs																								
HOLIDAYS																										
WEATHER																										
SITEWORK																										
SITE UTILITIES																										
Excavate/Backfill electrical ductbank - Post steel Pending N	otes from	70																								
erection/coordination meeting with Eversource Arch En																										
Install electrical ductbank - Post steel Pending N	otes from	70																								
erection/coordination meeting with Eversource Arch En																										
Begin design work for gas main to new building		Columbi	a X	X	X	Х	Х			X	Х	Х	X X		X	Х		Х	Х			X	Х	Х	Х	
BUILDING FOUNDATION																										
Dewatering		Marois	Х	X	X	Х	Х	Х	X																	
Building E																										
Building D																										
Building C						_																				
Building F						_																				
Building A						_																				
Building G																										
Building B																										
Install Foundations (footings) for Building B	A902																									
Backfill foundations (footings) Building B		Marois	X							\vdash									_							
Install Foundations walls Building B		Riggs	Х	X																						
Install Damproofing on B Building Foundations Walls		Superio	r			X	X			X									-							
Backfill foundations (Walls) Building B		Marois									X	X	X X		X	X	X	Х			X	x	Х	X		
Underground Utilities																										
Building C																										
Layout install underground utiliities		Grasseso	hi																							
Excavate and backfill for underground utilities		Marois		X	X	X	X			X	x															
Install underground utiliities		Grasseso									X								-							
Subgrade for SOG		Marois										v	v v			v					V	\mathbf{v}		<u> </u>		
Subgrade for SOG Steel Erection/Concrete Slab on Deck											^	^	∧ Å		X	~					<u>∧</u> .	^				
Building C																										
Deck and Detail C Building Include	Studs A91	90 Supermetal/G	PEast																							
Install rebar and mesh on SOD	A913			X	X																					
Install MEP sleeves	A93					Х	Х			X	X															
Place Concrete Deck	A93												X													
Install Fire Proofing															Х	Х	Х	Х	Х		X	X	Х	Х	Х	
Building E																										
Steel Erection E Building	A91																									
Deck and Detail E Building Include	Studs A92	30 Supermetal/G	P East X	Х	Х	Х	Х			Х	Х	Х	X X		Х	Х	Х									
Building D																										
Steel Erection D Building	A91:			X																						
Deck and Detail D Building Include	Studs A92	00 Supermetal/G	P East		X	X	X			X	X	Х	X X		X	X	X	Х	X		x	X	X	X	X	
Building F						N/	V					V						V			V	V				
Steel Erection F Building	A91	50 Supermetal/G	PEast			X	X			X	X	Х	X X		X	Х		X	X			X				
Roofing																										
Building C											V	V	V V													
Install Roof Blocking and High/Low Wall Framing Install Roofing		Century		X	X	X	X			X	Х	X	X X			X	Y	Y	×			x	X	X	X	
		Capewa	y				1									^		^	^			X	~	<u>^</u>	^	
