

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- Team is working with Eversource on the final stages of permanent power. Equipment start up and commissioning will be coordinated in conjunction with this milestone.
- Sheetrock finishing is ongoing nearing completion.
- Finishes including paint, tile, epoxy flooring, concrete polishing, casework & ceilings are ongoing.
- Flooring including vinyl tile & carpet will begin in the coming weeks.
- Exterior panel systems installation (including metal & concrete) is ongoing.
- Window & curtain wall installation- including installation of glazing- is ongoing.
- Installation of gym wood flooring is ongoing.
- Theater specialty equipment installation is ongoing
- Sitework & preparation for hardscape & landscape is ongoing.
- Track resurfacing is scheduled to occur in the coming weeks.
- Work at the athletic facility - including roof installation- is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



PMA Consultants




TAPPÉ
ARCHITECTS



SHARON HIGH SCHOOL



LOGISTICS UPDATE

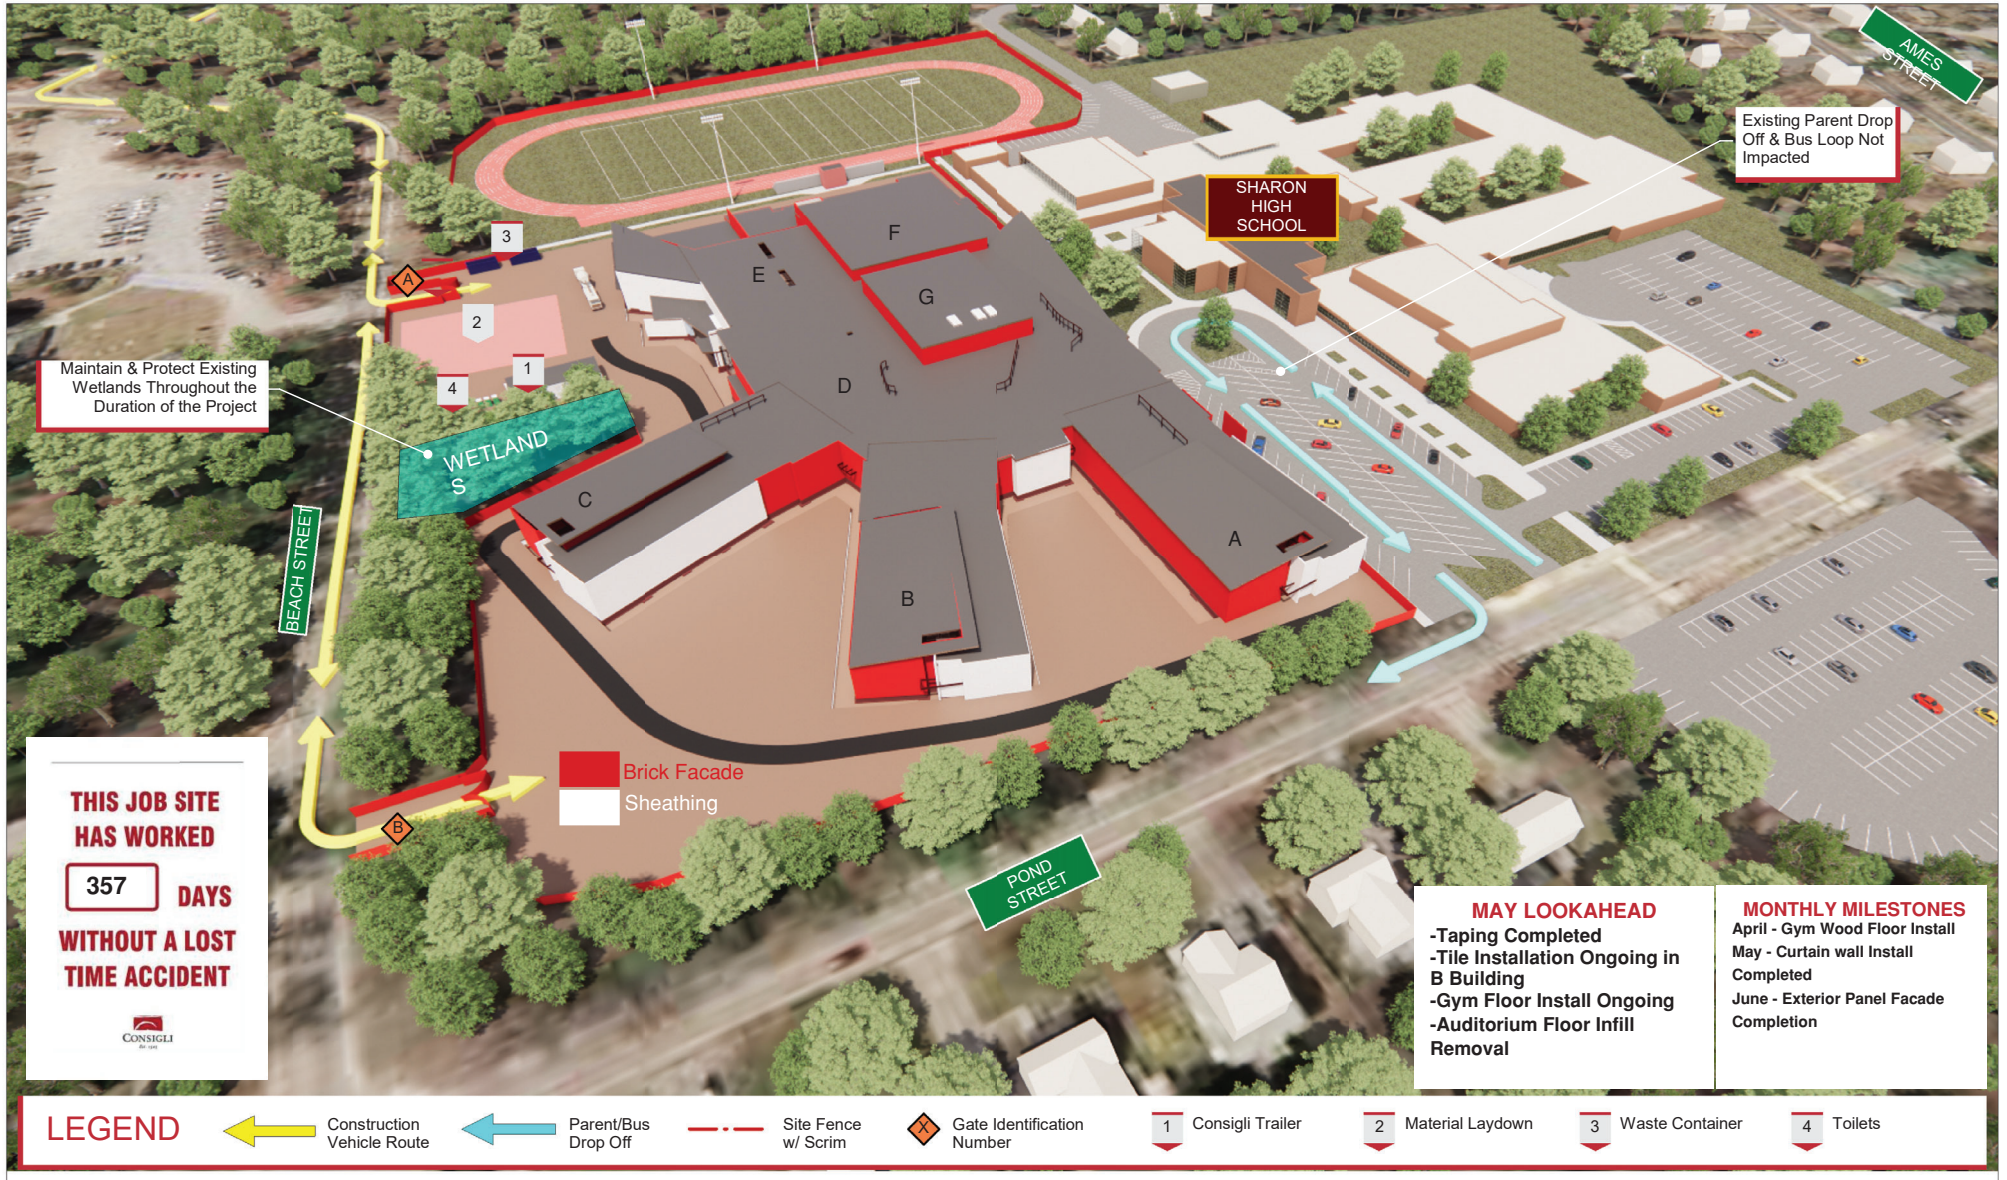

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/9/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/9	5/10	5/11	5/12	5/13	5/14	5/15	5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5		
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S		
SCHOOL SCHEDULE																																		
MILESTONES																																		
Dancefloor removal in Auditorium																																		
HOLIDAYS																																		
WEATHER																																		
MOCK UP/THIRD PARTY ENVELOPE TESTING																																		
CW Testing				INTERTEK/PMA			X																											
SITWORK & UTILITIES																																		
Install Remaining conduit for athletic facility				MAK																														
FOOTBALL FIELD																																		
Potential Re-Design of Pressbox Footings				CCC/Tappe																														
Form and install rebar for pressbox footings				Riggs																														
Place pressbox footings				Riggs																														
Form Piers at pressbox footings				Riggs																														
Place piers at pressbox footings				Riggs																														
Back fill pressbox footings				Vinagro																														
Install Press Box				Dant Clayton																														
ATHLETIC FACILITY BUILDINGS																																		
Install Roof Trusses and Framing				Century	X	X	X	X	X			X	X	X																				
Install Roofing				Capeway										X	X	X			X	X														
Install spray applied AVB on CMU Walls				Armani				X	X	X																								
Install Masonry Façade				Fernandes								X	X	X																				
Install Consession Sliders				Chandler Architectural																														
INTERIOR FITOUT/OH ROUGH/FINISHES																																		
Building C - 2nd Floor																																		
Flood Ceilings in Classrooms				K&K	X	X	X	X	X																									
Install Classroom Doors				Thompson Door			X	X	X			X																						
Prep & Install LVT in Classrooms				Capital Carpet								X	X	X	X	X																		
Building C - 1st Floor																																		
Flood Ceilings in Classrooms				K&K	X	X	X	X	X																									
Install wood slat ceiling in hallway				K&K								X	X	X	X	X			X	X														
Install Classroom Doors				Thompson Door								X	X	X	X																			
Prep & Install LVT in Classrooms				Capital Carpet											X	X			X	X	X													
Building C - IDF Room 2519																																		
Build Out				WJ Griffin																														
Building D - 2nd Floor																																		
Interior Caulk Joint @ CW21				Armani			X																											
RFI 190 Soffit Boarding @ 2293				Century			X																											
Install Fumehoods	Pending Mock-up approval			NEIS Casework																														
Install Countertops				NEIS Casework			X	X																										
Install Fixtures/Finishes in Science Rooms				Grasseschi			X	X																										
Install Classroom Doors				Thompson Door			X	X	X			X																						
Prep & Install LVT in Classrooms				Capital Carpet								X	X	X	X	X																		
Flood ACT Ceilings				K&K																														
Install Pipe grid in Steam room				Berlin Steel																														
Building D - 1st floor																																		
Flood ACT Ceilings				K&K																														
Install tile at stair 3 wall				High Point			X	X	X			X	X	X	X	X																		
Install Fumehoods	Pending Mock-up approval			NEIS Casework																														
Install Countertops				NEIS Casework			X	X																										
Install Fixtures/Finishes in Science Rooms				Grasseschi			X	X																										
Install Classroom Doors				Thompson Door			X	X				X	X	X	X																			
Prep & Install LVT in Classrooms				Capital Carpet											X	X			X	X	X													

Consigli Construction - Sharon High School Project Lookahead Schedule

5/9/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/9	5/10	5/11	5/12	5/13	5/14	5/15	5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5							
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S							
Install Motorized shades at CW11				Walker Specialties																																			
Install Pipe grid in Steam room				Berlin Steel																																			
Building D - Electrical Closet 1268																																							
Install Door and Hardware				Thompson Door		X																																	
Pull Feeders/Branch Wire				WJ Griffin	X	X	X	X	X																														
Install Panel Interiors				WJ Griffin	X	X	X	X	X																														
Terminate & Test Panels				WJ Griffin																																			
Start Up & Test				WJ Griffin																																			
Building D - MDF Room 1269																																							
Install Door and Hardware				Thompson Door		X																																	
Build Out				WJ Griffin																																			
Building E - 2nd Floor/Media Center																																							
Install MEP Drops to ACT grid				Apex	X	X	X	X	X																														
Install light fixtures in ACT ceilings				WJ Griffin	X	X	X	X	X																														
Install light fixtures in soffits				WJ Griffin	X	X	X	X	X																														
Flood ACT Ceilings				K&K																																			
Building E - 1st Floor/Dining Commons																																							
Install ceiling grid over Stair 4				K&K																																			
Place Stair Pans at Stair 4				Riggs				X	X		X																												
Install Int glass store fronts at wellness/weight rooms				Chandler Architectural	X																																		
Install Mirrors in wellness/weight rooms				Chandler Architectural																																			
Install wall pads in wellness/weight rooms				Pappas																																			
Install Motorized Shades at CW20				Walker Specialties																																			
Prep & Install LVT				Capital Carpet																	X	X	X	X															
Prep & Install RAF in 1129 & 1131				Capital Carpet																X	X	X	X																
Building E - Kitchen																																							
Install Coiling Doors				Overhead Doors	X	X	X	X	X																														
MEP Drops to ACT grid				Apex	X	X	X	X	X																														
Install Light Fixtures in ACT				WJ Griffin							X	X	X	X	X																								
Flood ACT Ceilings				K&K																																			
Install kitchen equipment				Kitteridge	X	X	X	X	X		X	X																											
Install walk-ins				Kitteridge	X	X	X	X	X		X	X																											
Building E - Electrical Room 1139																																							
Install Door and Hardware				Thompson Door		X																																	
Pull Feeders/Branch Wire				WJ Griffin	X	X	X	X	X																														
Install Panel Interiors				WJ Griffin	X	X	X	X	X																														
Terminate & Test Panels				WJ Griffin																																			
Start Up & Test				WJ Griffin																																			
Building E - Emergency Electrical Room 1140																																							
Install Door and Hardware				Thompson Door		X																																	
Pull Feeders/Branch Wire				WJ Griffin	X	X	X	X	X																														
Install Panel Interiors				WJ Griffin	X	X	X	X	X																														
Terminate & Test Panels				WJ Griffin																																			
Start Up & Test				WJ Griffin																																			
Building E - IDF Room 1145																																							
Install Door and Hardware				Thompson Door		X																																	
Pull cable to IDF room				WJ Griffin	X	X	X	X	X																														
Build out				WJ Griffin																																			
Building F - Lockerrooms & Community Education																																							
Install Coiling Doors in community education				Overhead Doors							X	X	X	X	X			X	X	X	X	X					X	X	X	X	X								
Install Drywall Returns at P windows				Century																																			
Tape & Sand Drywall Returns				Century																																			
Flood ACT Ceilings				K&K																																			
Install Flooring in Community Education				Capital Carpet																							X	X	X	X									
Building F - GYM																																							
Install Gym Floor				Kenvo	X	X	X	X	X		X	X	X	X	X																								
Protect Gym Floor																																							
Install Remainder of gym equipment				Pappas															X	X	X	X	X																
Wire gym equipment				WJ Griffin														X	X	X	X	X																	
Install wall panels on elev track walls				K&K	X	X	X	X	X		X	X	X	X	X																								

Consigli Construction - Sharon High School Project
Lookahead Schedule
 5/9/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/9	5/10	5/11	5/12	5/13	5/14	5/15	5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Install elevated track rubber flooring				Capital Carpet																						X	X	X	X			
Protect rubber track flooring				Capital Carpet																						X	X	X	X			
Building F - Main Lobby																																
Install Wall tile in main lobby				High Point								X	X	X	X	X			X	X	X	X	X									
Install Veg green wall																																
Install int glass storefronts				Chandler Architectural																												
Building F - IDF Room 1113																																
Install Door and Hardware				Thompson Door		X																										
Build out				WJ Griffin	X	X	X	X	X																							
Building F - IDF Room 1279																																
Install Door and Hardware				Thompson Door		X																										
Install Cable trays				WJ Griffin	X	X	X	X	X																							
Pull cable to IDF room				WJ Griffin	X	X	X	X	X																							
Build out				WJ Griffin																												
Building F - Stair 6																																
Install Handrails				Berlin Steel																												
Clean Stair risers and treads				Riggs																												
Install Rubber treads				Capital Carpet																												
Building F - Stair 1																																
Install interior phenolic panel at stairwell wall				Riggs																												
Install Handrails				Berlin Steel																												
Clean Stair risers and treads				Riggs																												
Install Rubber treads				Capital Carpet																												
Install Zen garden under stair 1																																
Building G North of Auditorium - 2nd Floor																																
Install Sprinkler Drops to ACT Grid				JCI	X	X	X	X	X			X	X	X	X	X																
Install Duct Drops to ACT Grid				Apex								X	X	X	X	X																
Install Light Fixtures in ACT				WJ Griffin								X	X	X	X	X																
Flood ACT Ceilings				K&K																												
Install int glass storefronts				Chandler Architectural																												
Building G North of Auditorium - 1st Floor																																
Install Elevator 2				Delta Beckwith	X	X	X	X	X																							
Install MEP Drops to ACT Grid				Apex																												
Install Light Fixtures				WJ Griffin																												
Flood ACT Ceilings				K&K																												
Install Pipe Grid in Innovation Lab	Need delivery date			Berlin Steel																												
Install int glass storefronts				Chandler Architectural																												
Building G - Auditorium & Mezzanine																																
Install light fixtures at cloud level	Pending Delivery			WJ Griffin																												
Install speakers over Auditorium seating off of catwalk				PRO AV			X	X	X																							
Tape & Sand Walls Under Mezzanine				Century	X	X	X	X	X																							
Frame and Board Added Chicago Grid Under Mezzanine				Century			X	X	X			X																				
Tape and Sand Ceiling and Soffit under Mezzanine				Century								X	X																			
Prime & First Coat Walls under mezzanine				King										X	X																	
Counterweight rigging installation - Phase 1				Texas Scenic								X	X	X	X	X			X	X	X	X	X			X						
Counterweight rigging installation - Phase 2				Texas Scenic																							X	X	X	X		
Counterweight rigging installation - Phase 3	Start 6/13/2022			Texas Scenic																												
Motorized rigging installation - Phase 1	Start 6/27/2022			Texas Scenic																												
Track Installation	Start 5/11/2022			Texas Scenic																												
Drapery Installation	Start 5/13/2022			Texas Scenic																												
Install Stage Flooring				Kenvo																X	X	X	X	X		X	X	X	X	X		
Install Light Fixtures																																
Install Auditorium Rails at Mezzanine & Catwalks				Berlin Steel	X	X	X	X	X																							
Install conduit and boxes on catwalk rails				WJ Griffin								X	X	X	X	X																
Theatrical Equipment install on catwalk rails				PRO AV								X	X	X	X	X																
Install Stair 7	Need Delivery Date			Berlin Steel																												
Install 2 Ships ladders to catwalks on stage	Need Delivery Date			Berlin Steel																												
Building G - Auditorium Storage 1281A																																
Frame & Board 10' Wall				Century			X	X	X																							
Tape & Sand 10' Wall				Century					X			X																				
Prime/First Coat Walls				King									X																			

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/9/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/9	5/10	5/11	5/12	5/13	5/14	5/15	5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5					
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S					
Install & Build Out panels				WJ Griffin										X	X	X			X	X	X	X	X														
Building G - Black Box																																					
Install theatrical & House lights/AV at tension wire grid				WJ Griffin	X	X	X	X	X			X	X	X	X	X																					
Install AV Equipment at Tension wire grid				PRO AV	X	X	X	X	X			X	X	X	X	X																					
Install electrical wall devices				WJ Griffin								X	X	X	X	X																					
Install Blackbox wood flooring				Kenvo															X	X	X	X	X			X	X	X	X	X							
Install Bleachers	Start 6-17-22																																				
Building G - Electrical Closet 2217																																					
Build out				WJ Griffin	X	X	X	X	X																												
Install Door and Hardware				Thompson Door		X																															
Building G - Stair 2																																					
Tape/Sand Stairwell Walls				Century King			X	X	X			X	X																								
Prime/First Coat Walls				WJ Griffin										X	X	X																					
Install Light Fixtures				WJ Griffin																																	
Install Handrails				Berlin Steel																																	
Clean treads and risers				Riggs																																	
Install Rubber treads																																					
Building A - 2nd Floor																																					
Install ACT Grid in high hallway ceilings				K&K																																	
Install MEP Drops to ACT Ceiling Grid				MEP Trades								X	X	X	X	X			X	X	X	X	X														
Install Light Fixtures in ACT ceilings				WJ Griffin															X	X	X	X	X														
Flood ACT Ceilings				K&K																																	
Building A - 1st Floor																																					
Board Hard Ceilings				Century								X																									
Tape & Sand Hard Ceilings				Century									X	X	X																						
Prime/First Coat Ceilings				King											X	X																					
Install Epoxy Floors				NE Decks & Floors	X	X	X	X	X																												
Install Wall Tile in Bathrooms				High Point								X	X	X	X	X			X	X						X	X										
Install ACT Grid in high hallway ceilings				K&K																																	
Install MEP Drops to ACT Ceiling Grid				MEP Trades								X	X	X	X	X			X	X	X	X	X														
Install Light Fixtures in ACT ceilings				WJ Griffin															X	X	X	X	X														
Flood ACT Ceilings				K&K																																	
Install Casework				NEIS Casework																																	
Frame soffit at stair 8 opening				Century																																	
Building A - IDF Room 2319																																					
Install Door and Hardware				Thompson Door		X																															
Install Cable Tray				WJ Griffin																																	
Pull cable to tray				WJ Griffin																																	
Flood ACT Ceiling				K&K																																	
Building B - 2nd Floor																																					
Install Channels at Stair 9				Berlin Steel																																	
Install OH Ductwork				Apex	X	X	X	X	X			X	X	X	X	X																					
Install Wall Tile in Bathrooms				High Point															X	X	X	X	X				X	X									
Install Wall Tile in Hallway				High Point															X	X	X	X	X				X	X									
Install ceiling grid over stair 9				K&K					X	X																											
Install MEP Drops to ACT Ceiling Grid				MEP Trades																																	
Install Light Fixtures in ACT ceilings				WJ Griffin																																	
Flood ACT Ceilings				K&K																																	
Frame Hard Ceilings				Century																																	
Install MEP Drops to hard ceilings				MEP Trades																																	
Install Light fixtures in hard ceilings				WJ Griffin																																	
Board Hard Ceilings				Century																																	
Tape & Sand Hard Ceilings				Century																																	
Install Epoxy Floors				NE Decks & Floors																																	
Install Casework				NEIS Casework																																	
Install Stair 9				Berlin Steel																																	
Building B - 1st Floor																																					
Install OH Ductwork				Apex	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X						
Tape and sand B2 Hallway wall				Century			X	X	X																												
Tape & sand walls				Century																																	
Prime & First Coat Walls				King																																	
Install Wall Tile in Bathrooms				High Point																							X	X	X	X	X						

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/9/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/9	5/10	5/11	5/12	5/13	5/14	5/15	5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Install Wall Tile in Hallway				High Point																						X	X	X	X	X		
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K																												
Install ACT Grid in high hallway ceilings				K&K																												
Install MEP Drops to ACT Ceiling Grid				MEP Trades																												
Install Light Fixtures in ACT ceilings				WJ Griffin																												
Flood ACT Ceilings				K&K																												
Frame Hard Ceilings				Century																												
Install MEP Drops to hard ceilings				MEP Trades																												
Install Light fixtures in hard ceilings				WJ Griffin																												
Board Hard Ceilings				Century																												
Tape & Sand Hard Ceilings				Century																												
Install Epoxy Floors				NE Decks & Floors																												
Frame soffit at stair 9 opening				Century																												
Board Soffit at Stair 9				Century																												
Tape & Sand Soffit at Stair 9				Century																												
Prime & First Coat Soffit at stair 9				King																												
Install Casework				NEIS Casework																												
Building B - IDF Room 2419																																
Install Door and Hardware				Thompson Door		X																										
Install Cable Tray				WJ Griffin	X	X																										
Pull Cable to IDF				WJ Griffin			X	X	X																							
ROOFING & FAÇADE WORK																																
Building C																																
Exterior Marvin Caulking @ Brick Façade				Armani	X	X	X	X	X																							
Exterior Marvin Caulking @ TAKTL Façade				Armani	X	X	X	X	X																							
Install TAKTL Panels on East and South Facades				Riggs								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
Install TAKTL Panels on Roof Clerestory				Riggs								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
Building D																																
Install perimeter roof edge				Capeway																												
Exterior Recaulk & Silicone of CW21	Done After Rework			Armani		X	X																									
Building E																																
Install MCM Panel over CW 20				Riggs																												
Install CW 07 & 14 glass				Chandler Architectural																												
Building F																																
Install Drywall Returns on P Windows				Century							X	X																				
Tape & Sand P window returns				Century									X	X	X																	
Install CW 06				Chandler Architectural							X	X	X	X	X				X	X	X	X	X			X	X	X	X	X		
Install CW 01				Chandler Architectural																												
Install CW 27 & CW 23				Chandler Architectural																												
Building G																																
Install CW 22 & CW 12 @ Stair 2				Chandler Architectural																												
Building A																																
Install TAKTL Panels on North and east elevations				Riggs																												
Install TAKTL Panels on Roof clerestory				Riggs																												
Exterior Marvin Caulking @ Brick Façade				Armani	X	X	X	X	X																							
Exterior Marvin Caulking @ TAKTL Façade				Armani	X	X	X	X	X																							
Install CW 13				Chandler Architectural																												
Building B																																
Install TAKTL Panels on North and East elevations				Riggs																												
Install TAKTL Panels on Roof clerestory				Riggs																												
Interior Window Caulking				Armani	X	X	X																									
Install CW 13				Chandler Architectural																												
