

The Sharon High School Construction Project



4 Week Look Ahead Schedule 05/10/2021


- **Upcoming Activities Include:**

- Structural steel erection, decking, detailing & associated deliveries are ongoing
- Placement of our first concrete slab is scheduled to occur in the next two weeks. Preparation & placement of concrete slabs will continue to follow steel erection. Once placed, slabs will enable MEP trades to begin rough in.
- Roofing and associated prep activities are scheduled to begin during this period
- Underground plumbing work is ongoing
- Construction at the track and football field has begun- see enclosed notice for details
- See attached progress update
- See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information:
<https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



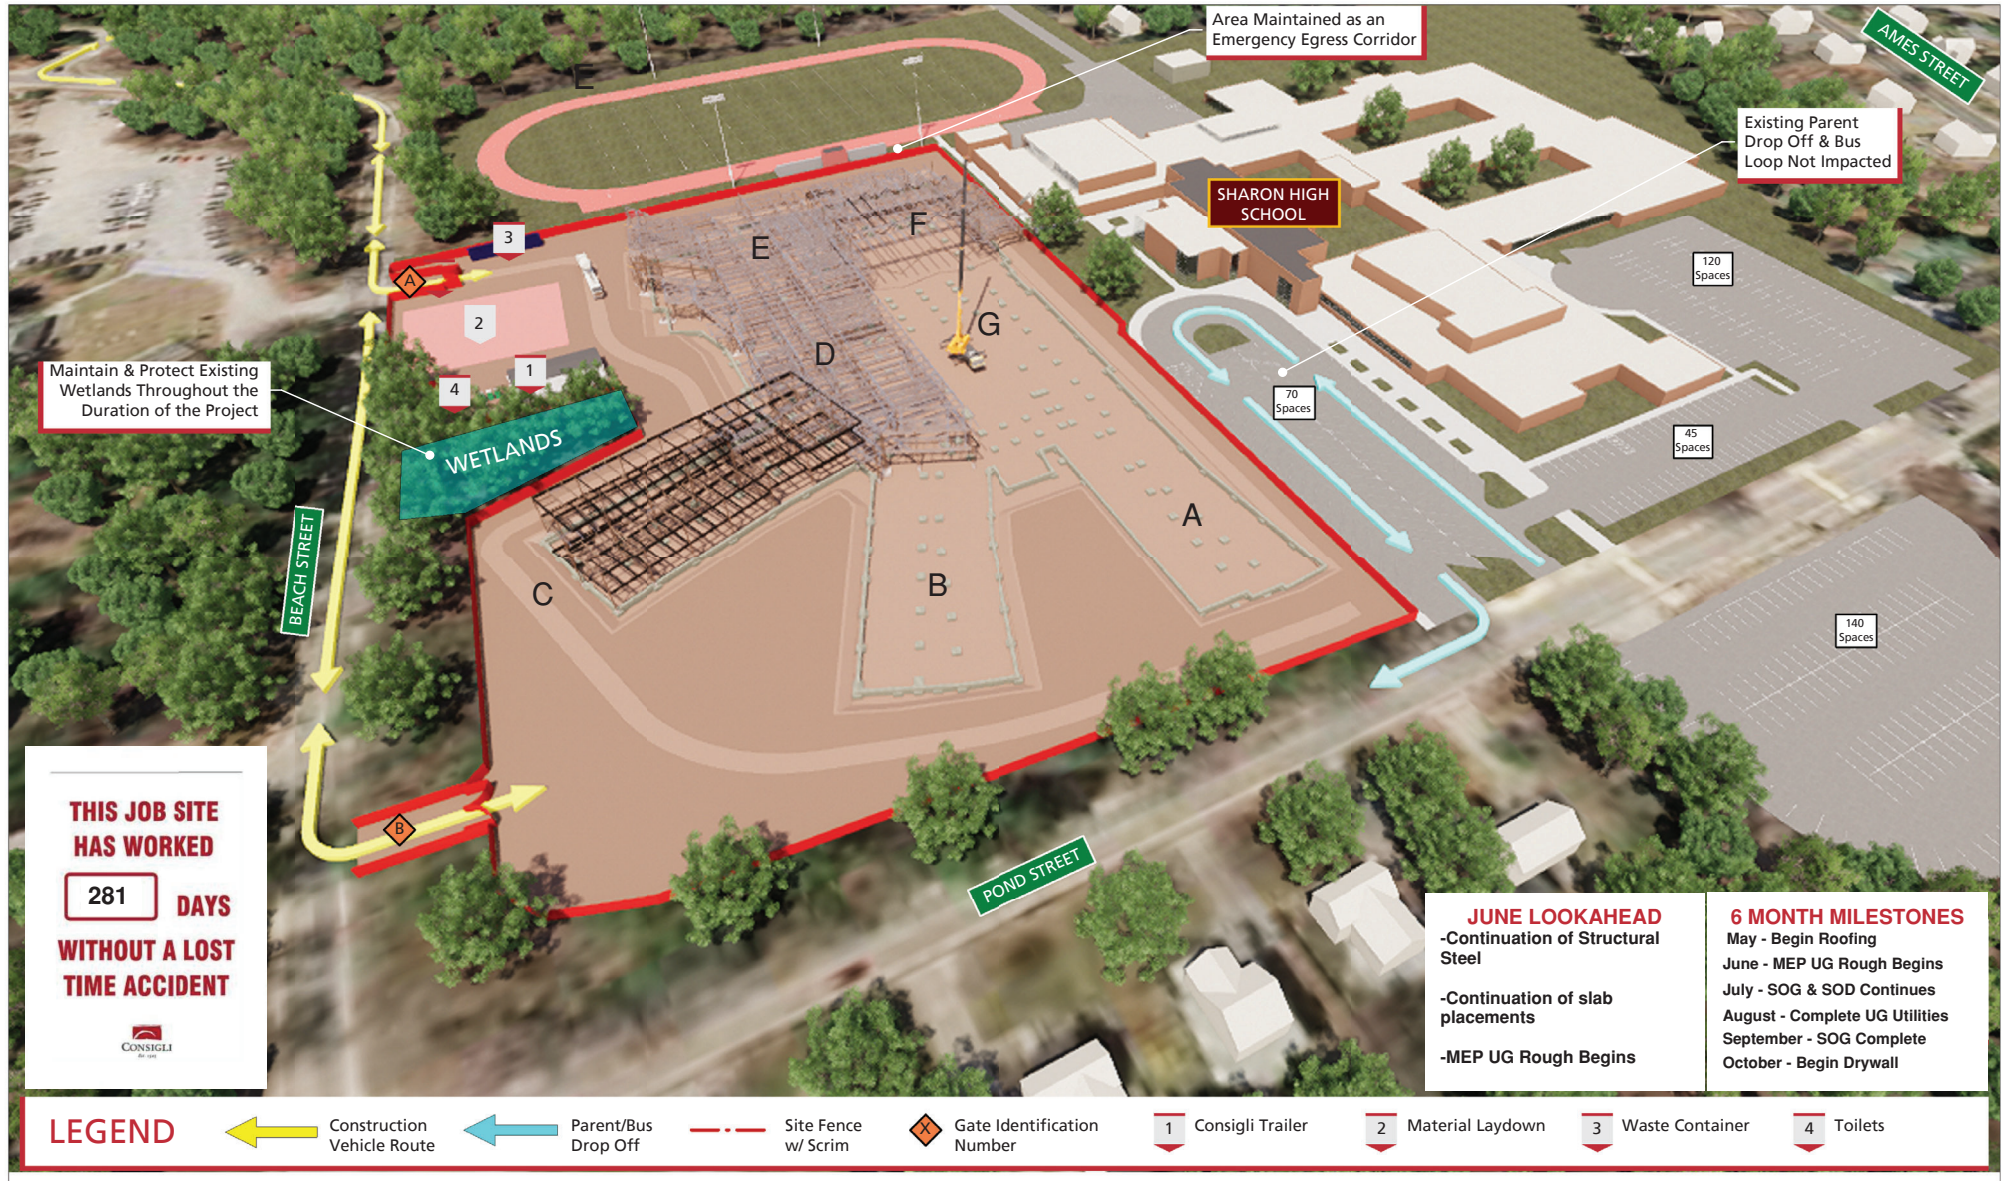



Sharon High School: Upcoming Closure of Track & Football Field

Notice Date: April 5, 2021

Sharon High School Community:

In the coming weeks Consigli Construction will be moving to their next phase of construction which includes beginning work at the Sharon High School track & football field. This work will require that these areas are closed to public use/access. The phased closing of this area is as detailed below:

- **April 26th** – Erosion Control will be installed (no impact to field use)
- **May 3rd** – We will begin temp fencing surrounding the perimeter of the existing fencing (no impact to field use. Once the fencing is installed there will only be field access from the Ames Court side of the site)
- **May 17th** – Site work will start, track and field will be off limits to all staff/ student/ public, gates will be locked

The project team would also like to take the opportunity to thank you for your continued support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com

LOOK AHEAD SCHEDULE
5/10/2021

Description of Work	Notes	P6 Activity Code	Responsibility	5/10	5/11	5/12	5/13	5/14	5/15	5/16	5/17	5/18	5/19	5/20	5/21	5/22	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6
				M	T	W	TR	FR	1	S	M	T	W	TR	FR	1	S	M	T	W	TR	FR	1	S	M	T	W	TR	FR	1	S
SCHOOL SCHEDULE																															
Students onsite in school session			SHARON HS	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X					X	X	X	X	X
Fully remote day			SHARON HS																												
Early Release Day			SHARON HS																												
MILESTONES																															
Foundation Placement Complete 4/30/21			Riggs																												
HOLIDAYS																															
Memorial Day																											X				
WEATHER																															
SITWORK																															
SITE UTILITIES																															
Excavate/Backfill electrical ductbank - Post steel erection/coordination meeting with Eversource	Pending Notes from Arch Engineers	A9670																													
Install electrical ductbank - Post steel erection/coordination meeting with Eversource	Pending Notes from Arch Engineers	A9670																													
Begin design work for gas main to new building			Columbia	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X				X	X	X	X	X	
BUILDING FOUNDATION																															
Building B																															
Install Damproofing on B Building Foundations Walls	Moved to Tuesday Due to Rain		Superior		X																										
Backfill foundations (Walls) Building B			Marois		X	X	X	X			X	X																			
Underground Utilities																															
Building C																															
Form/Place/Strip Column Collars			Riggs			X	X	X																							
Fine Grade - Southern Half			Marois								X	X	X	X	X																
Install Underground Conduit Run			Wayne J Griffin										X	X	X																
Excavate and Backfill for underground sanitary piping			Marois			X	X	X			X	X																			
Building A																															
Excavate and Backfill for underground storm piping			Marois	X	X	X	X	X																							
Install Storm underground			Grasseschi	X	X	X																									
Building B																															
Excavate and Backfill for underground storm piping			Marois	X	X	X	X	X																							
Install Storm underground			Grasseschi			X	X	X																							
Steel Erection/Concrete Slab on Deck																															
Building C																															
Install rebar and mesh on SOD		A9330	Riggs																												
Install MEP sleeves		A9330	MEP TRADES	X	X																										
Place Concrete Deck		A9330	Riggs								X																				
Install Fire Proofing - Exterior structure			H Carr														X	X	X	X	X										
Building E																															
Install rebar and mesh on SOD		A9330	Riggs				X	X			X	X	X	X	X			X	X	X											
Steel Erection E Building		A9160	Supermetal/GP East																												
Deck and Detail E Building	Include Studs	A9230	Supermetal/GP East	X	X	X	X	X			X	X	X																		
Building D																															
Steel Erection D Building		A9130	Supermetal/GP East																												
Deck and Detail D Building	Include Studs	A9200	Supermetal/GP East	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X									
Building F																															
Steel Delivery F Building		A14470	Supermetal/GP East	X	X	X	X	X																							
Steel Erection F Building		A9150	Supermetal/GP East	X	X	X	X	X			X	X	X	X	X			X	X												
Deck and Detail F Building	Include Studs	A9200	Supermetal/GP East	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X									
Building A																															
Steel Delivery A Building		A14470	Supermetal/GP East	X	X	X	X	X																							
Steel Erection A Building		A9150	Supermetal/GP East	X	X	X	X	X			X	X	X	X	X			X	X												
Roofing & Façade																															
Building C																															
Install Roof Blocking			Century	X	X	X	X	X																							
Install LGMF at Low/High Roofing Wall			Century										X	X			X	X	X	X	X					X	X	X	X		
Install Exterior Framing Clips			Century								X	X	X	X	X			X	X	X	X	X									
Install Roofing			Capeway																								X	X	X	X	
Building D																															
Install Roof Blocking			Century								X	X	X	X	X			X	X	X	X	X					X	X	X	X	
