

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- The transformer has been set and the team is working with Eversource on the final stages of permanent power. Equipment start up and commissioning will be coordinated accordingly.
- Sheetrock finishing is ongoing nearing completion.
- Finishes including paint, tile, epoxy flooring, concrete polishing, casework & ceilings are ongoing.
- Flooring including vinyl tile & carpet will begin in the coming weeks.
- Exterior panel systems installation (including metal & concrete) is ongoing.
- Window & curtain wall installation- including installation of glazing- is ongoing.
- Installation of gym wood flooring is ongoing. Bleacher installation is also upcoming.
- Installation of auditorium seating is on the radar for mid-June. Theater specialty equipment installation is ongoing.
- Sitework & preparation for hardscape & landscape is ongoing.
- Work at the athletic facility - including roof installation- is ongoing. Track resurfacing is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



PMA Consultants




TAPPÉ
ARCHITECTS



SHARON HIGH SCHOOL



LOGISTICS UPDATE
May 25, 2022

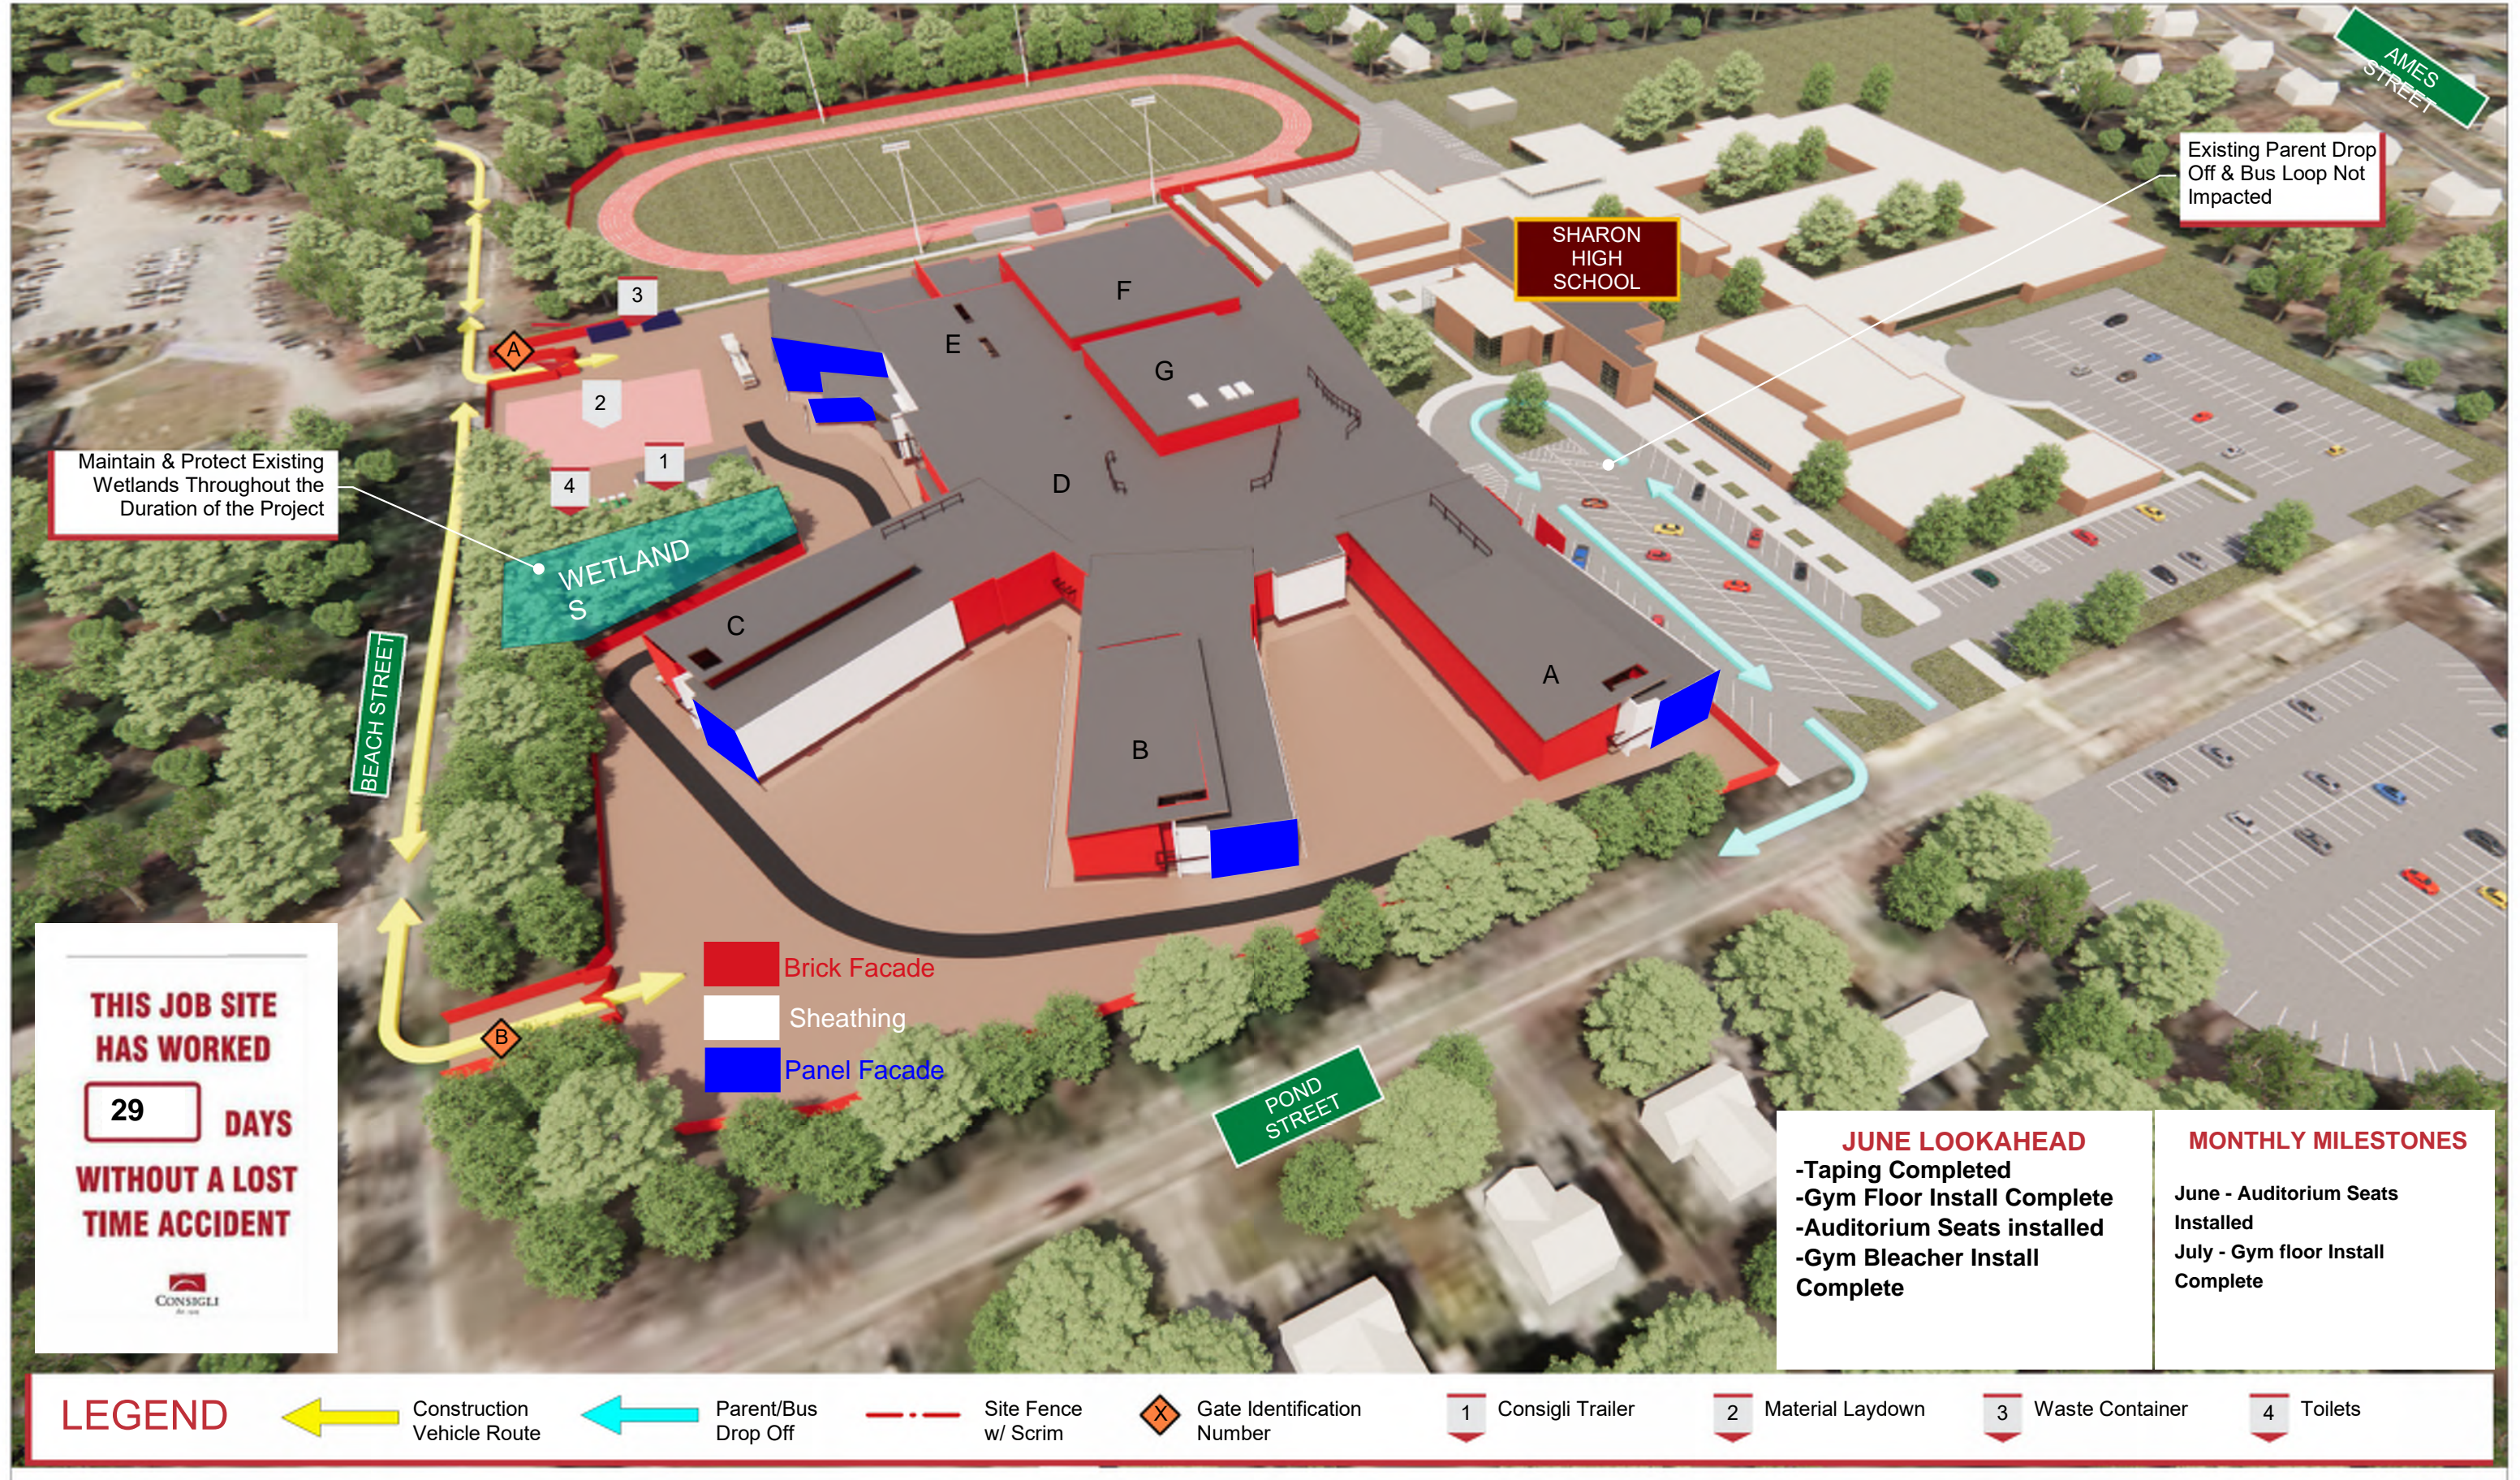

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/23/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
SCHOOL SCHEDULE																																
MILESTONES																																
Dancefloor removal in Auditorium				Commonwealth	X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X	X		X	X	X	X	X	X	
Installation of Auditorium Seats	Start 6/13/22			Highland Seating																												
Installation of Gym Bleachers				Corbin Seating			X	X	X			X	X	X	X	X																
HOLIDAYS																																
WEATHER																																
MOCK UP/THIRD PARTY ENVELOPE TESTING																																
SITWORK & UTILITIES																																
Install Remaining conduit for athletic facility				MAK																												
FOOTBALL FIELD																																
Potential Re-Design of Pressbox Footings				CCC/Tappe																												
Form and install rebar for pressbox footings				Riggs																												
Place pressbox footings				Riggs																												
Form Piers at pressbox footings				Riggs																												
Place piers at pressbox footings				Riggs																												
Back fill pressbox footings				Vinagro																												
Install Press Box				Dant Clayton																												
ATHLETIC FACILITY BUILDINGS																																
Install Roof Trusses and Framing				Century																												
Install Roofing				Capeway	X	X	X																									
Install spray applied AVB on CMU Walls				Armani			X	X	X																							
Install Masonry Façade				Fernandes								X	X	X	X	X			X	X					X	X						
Install Concession Sliders				Chandler Architectural																X	X	X										
Install OH Duct				Apex																												
INTERIOR FITOUT/OH ROUGH/FINISHES																																
Building C - 2nd Floor																																
Electrical Inspection OH in C wing				WJ Griffin																												
Building inspection OH in C wing to flood ceilings	Pending elec insp			CONSIGLI																												
Flood Ceilings in Classrooms				K&K															X	X	X	X	X									
Install Manual Shades in classrooms				Walker Specialties								X	X	X	X	X																
Prep & Install LVT in Classrooms				Capital Carpet								X	X	X	X	X																
Installing Corridor Millwork				Riggs	X	X	X	X	X			X	X																			
Install P-Lam Window Sills in Classrooms				Riggs	X	X	X	X	X																							
Install lockers in classroom wing	Delivery 7/11/22			NEIS Specialties																												
Building C - 1st Floor																																
Electrical Inspection OH in C wing				WJ Griffin																												
Building inspection OH in C wing to flood ceilings	Pending elec insp			CONSIGLI																												
Install Manual Shades in classrooms				Walker Specialties								X	X	X	X	X																
Flood Ceilings in Classrooms				K&K															X	X	X	X	X									
Install wood slat ceiling in hallway				K&K	X	X	X	X	X																							
Sand and Paint stair 10				King	X	X																										
Prep & Install LVT in Classrooms				Capital Carpet								X	X	X	X	X			X	X	X	X	X									
Install Marker Boards				NEIS Specialties																												
Install P-Lam Window Sills in Classrooms				Riggs	X	X	X	X	X																							
Install lockers in classroom wing	Delivery 7/11/22			NEIS Specialties																												
Building C - IDF Room 2519																																
Install racks on slab				WJ Griffin																												
Terminations				WJ Griffin	X	X	X	X	X																							
Building D - 2nd Floor																																
RFI 190 Soffit Taping @ 2293				Century																												

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/23/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19					
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S					
Install Coiling Doors in community education				Overhead Doors								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Install Operable partions/glass folding doors				Corbin Hufcor																						X	X	X	X	X							
Flood ACT Ceilings				K&K																																	
Install Doors				Thompson Door															X	X	X	X	X			X											
Install Flooring in Community Education				Capital Carpet																						X	X	X	X	X							
Building F - GYM																																					
Install Gym Floor				Kenvo	X	X																															
Install Gym Bleachers				Corbin Seating			X	X	X			X	X	X	X	X																					
Install Remainder of gym equipment				Pappas				X	X			X	X	X	X	X																					
Wire gym equipment				WJ Griffin								X	X	X	X	X																					
Complete Gym Floor				Kenvo														X	X	X	X	X				X	X	X	X	X							
Install elevated track rubber flooring				Capital Carpet																						X	X	X	X	X							
Protect rubber track flooring				Capital Carpet																												X					
Building F - Main Lobby																																					
Install Veg green wall	Delivery 6/27/22			Xquisite																																	
Install int glass storefronts				Chandler Architectural																																	
Install wood benches in main lobby				Riggs														X	X	X	X	X				X	X	X	X	X							
Building F - IDF Room 1113																																					
Terminate				WJ Griffin	X	X	X	X	X			X	X	X	X	X																					
Building F - IDF Room 1279																																					
Terminate				WJ Griffin	X	X	X	X	X			X	X	X	X	X																					
Building F - Stair 6																																					
Install Handrails	Delivery 6/6/22			Berlin Steel														X	X	X	X	X				X	X	X	X	X							
Clean Stair risers and treads				Riggs																																	
Install Rubber treads				Capital Carpet																																	
Building F - Stair 1																																					
Install interior phenolic panel at stairwell wall				Riggs																																	
Install Handrails	Delivery 6/6/22			Berlin Steel														X	X	X	X	X				X	X	X	X	X							
Clean Stair risers and treads				Riggs																																	
Install Rubber treads				Capital Carpet																																	
Install Zen garden under stair 1																																					
Building G North of Auditorium - 2nd Floor																																					
Install Light Fixtures in ACT				WJ Griffin																																	
Flood ACT Ceilings				K&K																																	
Install int glass storefronts				Chandler Architectural																																	
Install markerboards				NEIS Specialties								X	X	X	X	X																					
Install doors				Thompson Door	X	X	X	X	X																												
Building G North of Auditorium - 1st Floor																																					
Install Elevator 2				Delta Beckwith																																	
Install Light Fixtures				WJ Griffin																																	
Flood ACT Ceilings				K&K																																	
Install Pipe Grid in Innovation Lab	Need delivery date			Berlin Steel																																	
Paint and prime teacher planing				King																																	
Install markerboards				NEIS Specialties								X	X	X	X	X																					
Install int glass storefronts				Chandler Architectural																																	
Install Doors				Thompson Door	X	X	X	X	X			X																									
Building G - Auditorium & Mezzanine																																					
Install light fixtures at cloud level	Pending Delivery			WJ Griffin																																	
REMOVAL OF AUDITORIUM PLYWOOD INFILL																																					
Install AV Equipment under mezzanine				PRO AV	X																																
Tape & Sand Walls Under Mezzanine				Century																																	
Frame and Board Added Chicago Grid Under Mezzanine				Century																																	
Tape and Sand Ceiling and Soffit under Mezzanine				Century																																	
Prime & First Coat Walls under mezzanine				King	X	X																															
Counterweight rigging installation				Texas Scenic	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Motorized rigging installation - Phase 1	Start 6/27/2022			Texas Scenic																																	
Track Installation				Texas Scenic								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X							
Drapery Installation				Texas Scenic								X	X	X	X	X																					
Install Stage Flooring				Kenvo														X	X	X	X	X				X	X	X	X	X							
Install P-52 Light Fixtures				WJ Griffin																																	

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/23/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Install Auditorium Rails at Mezzanine & Catwalks				Berlin Steel																												
Install conduit and boxes on catwalk rails				WJ Griffin																												
Theatrical Equipment install on catwalk rails				PRO AV																												
Install Stair 7	Need Delivery Date			Berlin Steel																												
Install 2 Ships ladders to catwalks on stage	Need Delivery Date			Berlin Steel																												
Prime and First Coat Auditorium hallway				King																												
Building G - Auditorium Storage 1281A																																
Tape & Sand 10' Wall				Century																												
Prime/First Coat Walls				King																												
Install & Build Out panels				WJ Griffin	X	X	X	X	X																							
Building G - Black Box																																
Install theatrical & House lights/AV at tension wire grid				WJ Griffin	X	X	X	X	X																							
Install AV Equipment at Tension wire grid				PRO AV	X	X	X	X	X																							
Install electrical wall devices				WJ Griffin																												
Install Blackbox wood flooring				Kenvo				X	X			X	X	X	X	X			X	X	X											
Protect Blackbox wood flooring																																
Install Bleachers	Start 6-17-22																													X		
Building G - Electrical Closet 2217																																
Install Panel Interiors				WJ Griffin	X	X	X	X	X																							
Terminate & Test Panels				WJ Griffin								X	X	X	X	X																
Start Up & Test				WJ Griffin																												
Building G - Stair 2																																
Tape/Sand Stairwell Walls				Century	X	X	X																									
Prime/First Coat Walls				King	X	X	X	X	X																							
Install Light Fixtures				WJ Griffin																												
Install Handrails				Berlin Steel															X	X	X	X	X			X	X	X	X	X		
Clean treads and risers				Riggs																												
Install Rubber treads				Capital Carpet																												
Building A - 2nd Floor																																
Install ACT Grid in high hallway ceilings				K&K																												
Install MEP Drops to ACT Ceiling Grid				MEP Trades	X	X	X	X	X			X	X	X	X	X																
Install PRO AV Speaker Drops in ACT				PRO AV								X	X	X	X	X																
Flood ACT Ceilings				K&K																												
Building A - 1st Floor																																
Board Hard Ceilings				Century																												
Tape & Sand Hard Ceilings				Century																												
Prime/First Coat Ceilings				King																												
Install Wall Tile in Bathrooms				High Point				X	X			X	X	X																		
Install ACT Grid in high hallway ceilings				K&K																												
Install MEP Drops to ACT Ceiling Grid				MEP Trades	X	X	X	X	X			X	X	X	X	X																
Install Light Fixtures in ACT ceilings				WJ Griffin	X	X	X	X	X																							
Install PRO AV Speaker Drops in ACT				PRO AV								X	X	X	X	X																
Flood ACT Ceilings				K&K																												
Install Casework				NEIS Casework																												
Frame soffit at stair 8 opening				Century																												
Install Marker Boards				NEIS Specialties	X	X	X	X	X																							
Building A - IDF Room 2319																																
Terminate				WJ Griffin	X	X	X	X	X			X	X	X	X	X																
Building B - 2nd Floor																																
Install Channels at Stair 9				Berlin Steel								X	X	X	X	X																
Install OH Ductwork				Apex																												
Install Wall Tile in Bathrooms				High Point	X	X	X	X	X			X	X						X	X						X	X					
Install Wall Tile in Hallway				High Point	X	X	X	X	X			X	X						X	X						X	X					
Install ceiling grid over stair 9				K&K																												
Install MEP Drops to ACT Ceiling Grid				MEP Trades	X																											
Install Light Fixtures in ACT ceilings				WJ Griffin	X																											
Install PRO AV Speaker Drops in ACT				PRO AV								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
Install Wall Tile at Stair 9				High Point	X	X	X	X	X																							
Flood ACT Ceilings				K&K																												
Frame Hard Ceilings				Century																												
Install MEP Drops to hard ceilings				MEP Trades																												
Install Light fixtures in hard ceilings				WJ Griffin																												

Consigli Construction - Sharon High School Project

Lookahead Schedule

5/23/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	5/23	5/24	5/25	5/26	5/27	5/28	5/29	5/30	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19	
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
Board Hard Ceilings				Century																													
Tape & Sand Hard Ceilings				Century																													
Install Epoxy Floors				NE Decks & Floors																													
Install Casework				NEIS Casework																													
Paint ceilings				King																													
Install Stair 9				Berlin Steel																													
Building B - 1st Floor																																	
Install OH Ductwork				Apex	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Tape and sand B2 Hallway wall				Century																													
Tape & sand walls				Century																													
Prime & First Coat Walls				King																	X	X	X					X	X	X			
Install Wall Tile in Bathrooms				High Point								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Install Wall Tile in Hallway				High Point								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K																													
Install ACT Grid in high hallway ceilings				K&K																													
Install MEP Drops to ACT Ceiling Grid				MEP Trades																													
Install Light Fixtures in ACT ceilings				WJ Griffin																													
Install PRO AV Speaker Drops in ACT				PRO AV																X	X	X	X	X			X	X	X	X	X		
Flood ACT Ceilings				K&K																													
Frame Hard Ceilings				Century																													
Install MEP Drops to hard ceilings				MEP Trades																													
Install Light fixtures in hard ceilings				WJ Griffin																													
Board Hard Ceilings				Century																													
Tape & Sand Hard Ceilings				Century																													
Install Epoxy Floors				NE Decks & Floors																													
Frame soffit at stair 9 opening				Century																													
Board Soffit at Stair 9				Century																													
Tape & Sand Soffit at Stair 9				Century																													
Prime & First Coat Soffit at stair 9				King															X	X	X	X											
Install Casework				NEIS Casework																													
Building B - IDF Room 2419																																	
Install Cable Tray				WJ Griffin	X																												
Pull Cable to IDF				WJ Griffin		X	X	X	X																								
ROOFING & FAÇADE WORK																																	
Building C																																	
Exterior Marvin Caulking @ Brick Façade				Armani																													
Exterior Marvin Caulking @ TAKTL Façade				Armani																													
Install TAKTL Panels on East and South Facades				Riggs	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Install TAKTL Panels on Roof Clerestory				Riggs	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Building D																																	
Install perimeter roof edge				Capeway																													
Exterior Recaulk & Silicone of CW21	Done After Rework			Armani																													
Building E																																	
Install MCM Panel over CW 20				Riggs																													
Install CW 07 & 14 glass				Chandler Architectural																													
Building F																																	
Install Drywall Returns on P Windows				Century																													
Tape & Sand P window returns				Century																													
Install CW 06				Chandler Architectural	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Install CW 01				Chandler Architectural																													
Install CW 27 & CW 23				Chandler Architectural																													
Building G																																	
Install CW 22 & CW 12 @ Stair 2				Chandler Architectural																													
Building A																																	
Install TAKTL Panels on North and east elevations				Riggs																													
Install TAKTL Panels on Roof clerestory				Riggs																													
Exterior Marvin Caulking @ Brick Façade				Armani																													
Exterior Marvin Caulking @ TAKTL Façade				Armani																													
Install CW 13				Chandler Architectural																													

