

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule

- Permanent power is targeting completion this week. Equipment start up and commissioning is being coordinated accordingly.
- Finishes including paint, tile, epoxy flooring, vinyl tile, carpet, concrete polishing, millwork, casework & ceilings are ongoing.
- Exterior panel systems installation (including metal & concrete) is ongoing.
- Window & curtain wall installation- including installation of glazing- is ongoing.
- Gymnasium floor finishing is ongoing.
- Installation of auditorium seating is complete. Theater specialty equipment installation is ongoing.
- Sitework & preparation for hardscape & landscape is ongoing. Paving around the site is complete.
- Work at the athletic facility is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of  
**SHARON**  
Massachusetts



**PMA Consultants**




**TAPPÉ**  
ARCHITECTS



# SHARON HIGH SCHOOL



## LOGISTICS UPDATE

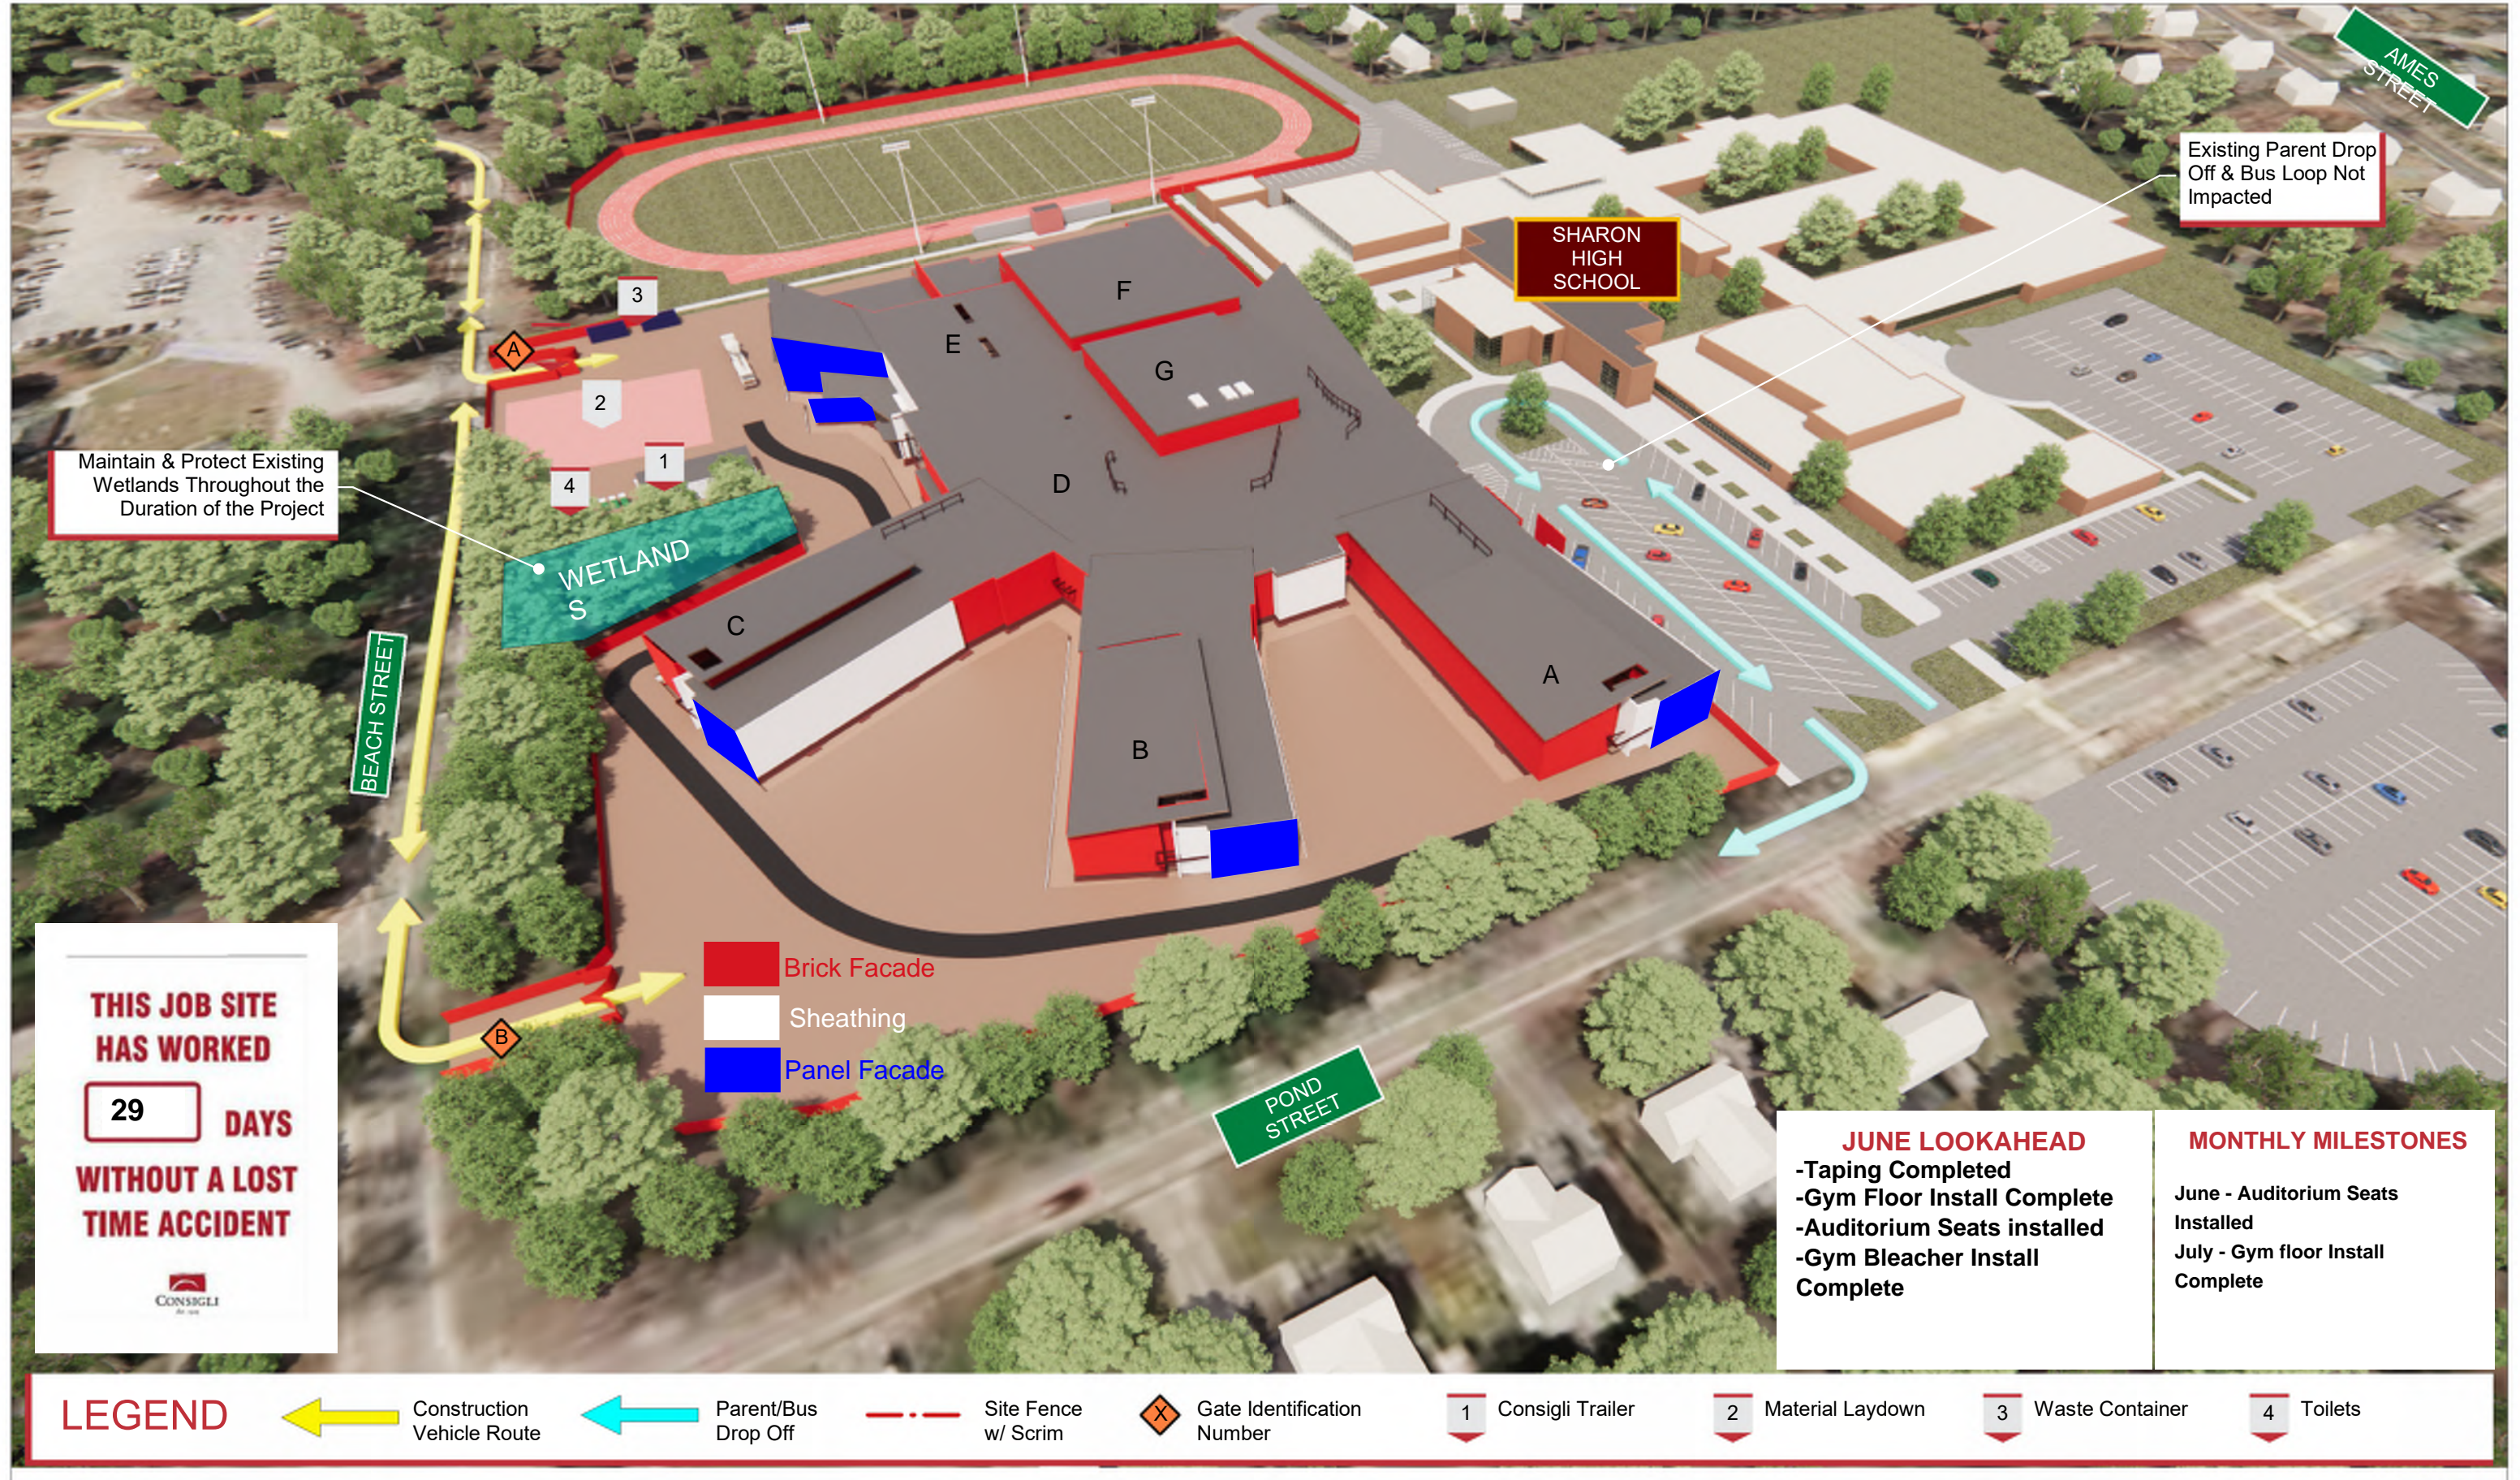

**THIS JOB SITE HAS WORKED**  
**29** DAYS  
**WITHOUT A LOST TIME ACCIDENT**



- Brick Facade
- Sheathing
- Panel Facade

**JUNE LOOKAHEAD**  
 -Taping Completed  
 -Gym Floor Install Complete  
 -Auditorium Seats installed  
 -Gym Bleacher Install Complete

**MONTHLY MILESTONES**  
 June - Auditorium Seats Installed  
 July - Gym floor Install Complete

### LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets

**Consigli Construction - Sharon High School Project**  
**4 Week Lookahead Schedule**  
 6/27/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	6/27	6/28	6/29	6/30	7/1	7/2	7/3	7/4	7/5	7/6	7/7	7/8	7/9	7/10	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25	
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	
<b>SCHOOL SCHEDULE</b>																																		
<b>MILESTONES</b>																																		
Waste Water Treatment Plant Scope Complete	29-Jul-22			CONSIGLI																														
TCO	25-Jul-22			CONSIGLI																														X
<b>HOLIDAYS</b>																																		
July 4th - SITE CLOSED											X																							
<b>WEATHER</b>																																		
<b>MOCK UP/THIRD PARTY ENVELOPE TESTING</b>																																		
Marvin Window Testing				Marvin/Optimize			X	X																										
<b>SITework &amp; UTILITIES</b>																																		
Form Misc. Sidewalks around the site				Riggs				X	X				X	X																				
Place Misc. Sidewalks around the site				Riggs											X																			
Install UG Piping and Pond between B & C				Vinagro																														
Form and Place Chalkboard & Benches at outdoor classroom				Riggs										X																				
Backfill outdoor classroom				Vinagro																														
Excavate for pump station at Gate D				Vinagro	X	X										X	X																	
Install Pump station at gate D				Vinagro			X	X	X				X																					
Backfill pump station at Gate D				Vinagro										X	X																			
<b>FOOTBALL FIELD &amp; PRESSBOX</b>																																		
Form and install rebar for pressbox footings				Riggs																														
Place pressbox footings				Riggs																														
Form Piers at pressbox footings				Riggs																														
Place piers at pressbox footings				Riggs																														
Back fill pressbox footings				Vinagro																														
Install Press Box				Dant Clayton																														
<b>ATHLETIC FACILITY BUILDINGS</b>																																		
Install Consession Sliders				Chandler Architectural									X	X	X	X																		
Install Metal panel Façade				Riggs									X	X	X	X			X															
Install OH Duct				Apex									X	X	X	X			X	X	X	X	X											
Install OH Electric Heaters				NBK		X	X	X																										
Paint Walls & OH Trusses/Plywood				King				X	X				X	X																				
<b>WASTE WATER TREATMENT PLANT</b>																																		
<b>INTERIOR FITOUT/OH ROUGH/FINISHES</b>																																		
<b>Building C - 2nd Floor</b>																																		
Install lockers in classroom wing				NEIS Specialties															X	x	x	x	x											
Install Wall Graphic				BlueBird									X	X	X	X																		
Install Toilet Partitons	Delivery TBD			NEIS Specialties																														
Final polish				Kaloutas			X	X	X																									
Install calking on countertops				NEIS Casework																														
<b>Building C - 1st Floor</b>																																		
Final Paint				King	X	X	X																											
Install Toilet Partitons	Delivery TBD			NEIS Specialties																														
Final polish				Kaloutas																														
Install lockers in classroom wing				NEIS Specialties															X	X	X	X	X											
Install calking on countertops				NEIS Casework																														
<b>Building C - IDF Room 2519</b>																																		
Terminations				WJ Griffin																														
<b>Building D - 2nd Floor</b>																																		
Tape Soffit in 2500 @ Folding Partitons				Century		X	X						X	X	X	X																		
Paint Soffit in 2500				King				X										X	X															
Install ceiling grid in D2 Resource Room				K&K					X				X																					
Wire fumehoods				WJ Griffin																														



Consigli Construction - Sharon High School Project  
 4 Week Lookahead Schedule  
 6/27/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	6/27	6/28	6/29	6/30	7/1	7/2	7/3	7/4	7/5	7/6	7/7	7/8	7/9	7/10	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25						
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Install Vinyl wall graphic & signage				BlueBird															X	X	X																		
Install int glass storefronts				Chandler Architectural			X	X	X																														
Install wood benches in main lobby				Riggs															X	X	X	X	X																
<b>Building F - IDF Room 1113</b>																																							
Terminate				WJ Griffin	X	X	X	X	X																														
<b>Building F - IDF Room 1279</b>																																							
Terminate				WJ Griffin	X	X	X	X	X																														
<b>Building F - Stair 6</b>																																							
Clean Stair risers and treads				Riggs																																			
Install Rubber treads				Capital Carpet									X	X	X	X			X	X	X	X	X																
<b>Building F - Stair 1</b>																																							
Install interior phenolic panel at stairwell wall				Riggs			X	X	X				X	X																									
Clean Stair risers and treads				Riggs																																			
Install Rubber treads				Capital Carpet															X	X	X	X	X																
Install Zen garden under stair 1				Xquisite																						X	X	X	X	X									
<b>Building G North of Auditorium - 2nd Floor</b>																																							
OH Elec inspection				WJ Griffin																																			
OH Building Inspection				CONSIGLI																																			
Flood ACT Ceilings				K&K																																			
Install interior glass at HM Door Frames				Chandler Architectural									X	X	X	X			X	X	X																		
Install int glass storefronts				Chandler Architectural															X	X	X	X	X																
<b>Building G North of Auditorium - 1st Floor</b>																																							
OH Elec inspection				WJ Griffin																																			
OH Building Inspection				CONSIGLI																																			
Flood ACT Ceilings				K&K																																			
Install Carpet				Alleghaney																																			
Install Pipe Grid in Innovation Lab	Berlin Sub			Berlin Steel																																			
Install interior glass				Chandler Architectural																																			
Install interior phenolic panel at stairwell wall				Riggs															X	X																			
Install int glass storefronts				Chandler Architectural															X	X																			
<b>Building G - Auditorium &amp; Mezzanine</b>																																							
Run Rope				Texas Scenic	X	X	X	X																															
Install Arbors + Counterweights				Texas Scenic																																			
Install Arbor Stops				Texas Scenic																																			
Mount Motors				Texas Scenic	X	X	X	X																															
Install Locking Rail				Texas Scenic					X	X			X	X																									
Install Floor Mounts				Texas Scenic																																			
Drapery Installation at 2nd floor mezzanine				Texas Scenic										X	X	X			X	X	X	X																	
Install Stage Flooring				Kenvo															X	X	X	X	X																
Install Carpet in Aisle ways in Aud and mezzanine				Alleghaney															X	X	X	X	X																
Install conduit and boxes on catwalk rails				WJ Griffin																																			
Theatrical Equipment install on catwalk rails				PRO AV																																			
Install 2 Ships ladders to catwalks on stage	Need Delivery Date			Berlin Steel																																			
<b>Building G - Black Box</b>																																							
Install theatrical & House lights/AV at tension wire grid				WJ Griffin	X	X	X	X	X				X	X	X	X																							
Install AV Equipment at Tension wire grid				PRO AV	X	X	X	X	X				X	X	X	X																							
Install Bleachers				Corbin Seating	X	X	X																																
Install HM int glass				Chandler Architectural				X	X				X																										
<b>Building G - Electrical Closet 2217</b>																																							
Terminate & Test Panels				WJ Griffin																																			
Start Up & Test				WJ Griffin																																			
<b>Building G - Stair 2</b>																																							
Install Light Fixtures				WJ Griffin																																			
Install Rubber treads				Capital Carpet									X	X	X	X																							
<b>Building A - 2nd Floor</b>																																							
Flood ACT ceilings				K&K	X	X	X																																
Wire Fumehoods				WJ Griffin																																			
Install FR Door assembly at stair 2				Chandler Architectural																						X	X	X	X										
<b>Building A - 1st Floor</b>																																							
Flood ACT Ceilings				K&K	X	X	X	X	X																														
Wire Fumehoods				WJ Griffin																																			
HM Glass in Door Frames				Chandler Architectural																																			
Install FR Door assembly at stair 2				Chandler Architectural																						X	X	X	X										

Consigli Construction - Sharon High School Project  
 4 Week Lookahead Schedule  
 6/27/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	6/27	6/28	6/29	6/30	7/1	7/2	7/3	7/4	7/5	7/6	7/7	7/8	7/9	7/10	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M
<b>Building A - IDF Room 2319</b>																																	
Terminate				WJ Griffin																													
<b>Building B - 2nd Floor</b>																																	
Install Wall Tile in Bathrooms				High Point	X	X	X	X	X																								
Install Wall Tile in Hallway				High Point															X														
Install MEP Drops to ACT Ceiling Grid				MEP Trades																													
Install Light Fixtures in ACT ceilings				WJ Griffin																													
Install PRO AV Speaker Drops in ACT				PRO AV																													
OH Electrical Inspection				WJ Griffin																													
OH Building Inspection				CONSIGLI																													
Flood ACT Ceilings				K&K																													
Install Casework				NEIS Casework	X	X	X	X	X																								
Install Countertops				NEIS Casework			X	X	X																								
Install interior glass at end of wing study rooms				Chandler Architectural											X	X																	
<b>Building B - 1st Floor</b>																																	
Install ACT Ceiling Grid Classrooms & Science Rooms				K&K	X	X	X																										
Install MEP Drops to ACT Ceiling Grid				MEP Trades	X	X	X	X	X																								
Install PRO AV Speaker Drops in ACT				PRO AV				X	X				X	X	X	X																	
OH Electrical Inspection				WJ Griffin															X														
OH Building Inspection				CONSIGLI															X														
Flood ACT Ceilings				K&K															X	X	X	X											
Install Elec wall devices in Building B				WJ Griffin	X	X	X	X	X																								
Install Mech wall devices in Building B				Mann Electric	X	X	X	X	X																								
Prime & First Coat Soffit at stair 9				King			X	X																									
Install Casework				NEIS Casework	X	X	X	X	X																								
Install Countertops				NEIS Casework			X	X	X																								
Install interior glass at end of wing study rooms				Chandler Architectural											X	X																	
<b>Building B - IDF Room 2419</b>																																	
Pull Cable to IDF				WJ Griffin																													
Terminations				WJ Griffin																													
<b>ROOFING &amp; FAÇADE WORK</b>																																	
<b>Building C</b>																																	
Install TAKTL Panels on East and South Facades				Riggs	X	X	X	X	X				X	X	X	X																	
<b>Building E</b>																																	
Install MCM Panel over CW 20				Riggs	X	X	X																										
Install CW 07 & 14 glass				Chandler Architectural																													
<b>Building F</b>																																	
Install Silicone Strip at CW 06				Armani																													
Install CW 01				Chandler Architectural																													
Install CW 27 & CW 23				Chandler Architectural																													
<b>Building A</b>																																	
Install TAKTL Panels on North and east elevations				Riggs	X	X	X	X	X				X	X	X																		
<b>Building B</b>																																	
Install TAKTL Panels on North and East elevations				Riggs	X	X	X	X	X				X	X	X	X																	
