

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- Permanent power was brought to the building this week. Lighting, system & equipment start up and commissioning are ongoing. Final stages of coordination with Internet utility are also ongoing.
- Jobsite logistics are being adjusted to prepare for the next phase of construction. Coordination with key stakeholders is ongoing.
- Finishes including paint, tile, epoxy flooring, vinyl tile, carpet, concrete polishing, millwork, casework & ceilings are ongoing. Substantial ceiling installation is anticipated now that permanent lighting can be turned on.
- Exterior panel systems installation (including metal & concrete) is ongoing.
- Window & curtain wall installation- including installation of glazing- is ongoing.
- Gymnasium floor finishing is ongoing.
- Installation of interior signage has started.
- Installation of auditorium seating is complete. Theater specialty equipment installation is ongoing.
- Sitework & preparation for hardscape & landscape is ongoing. Paving around the site is complete.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuiding.com/>


Town of
SHARON
Massachusetts



Sharon High School



PROJECT LOGISTICS UPDATE JULY 2022

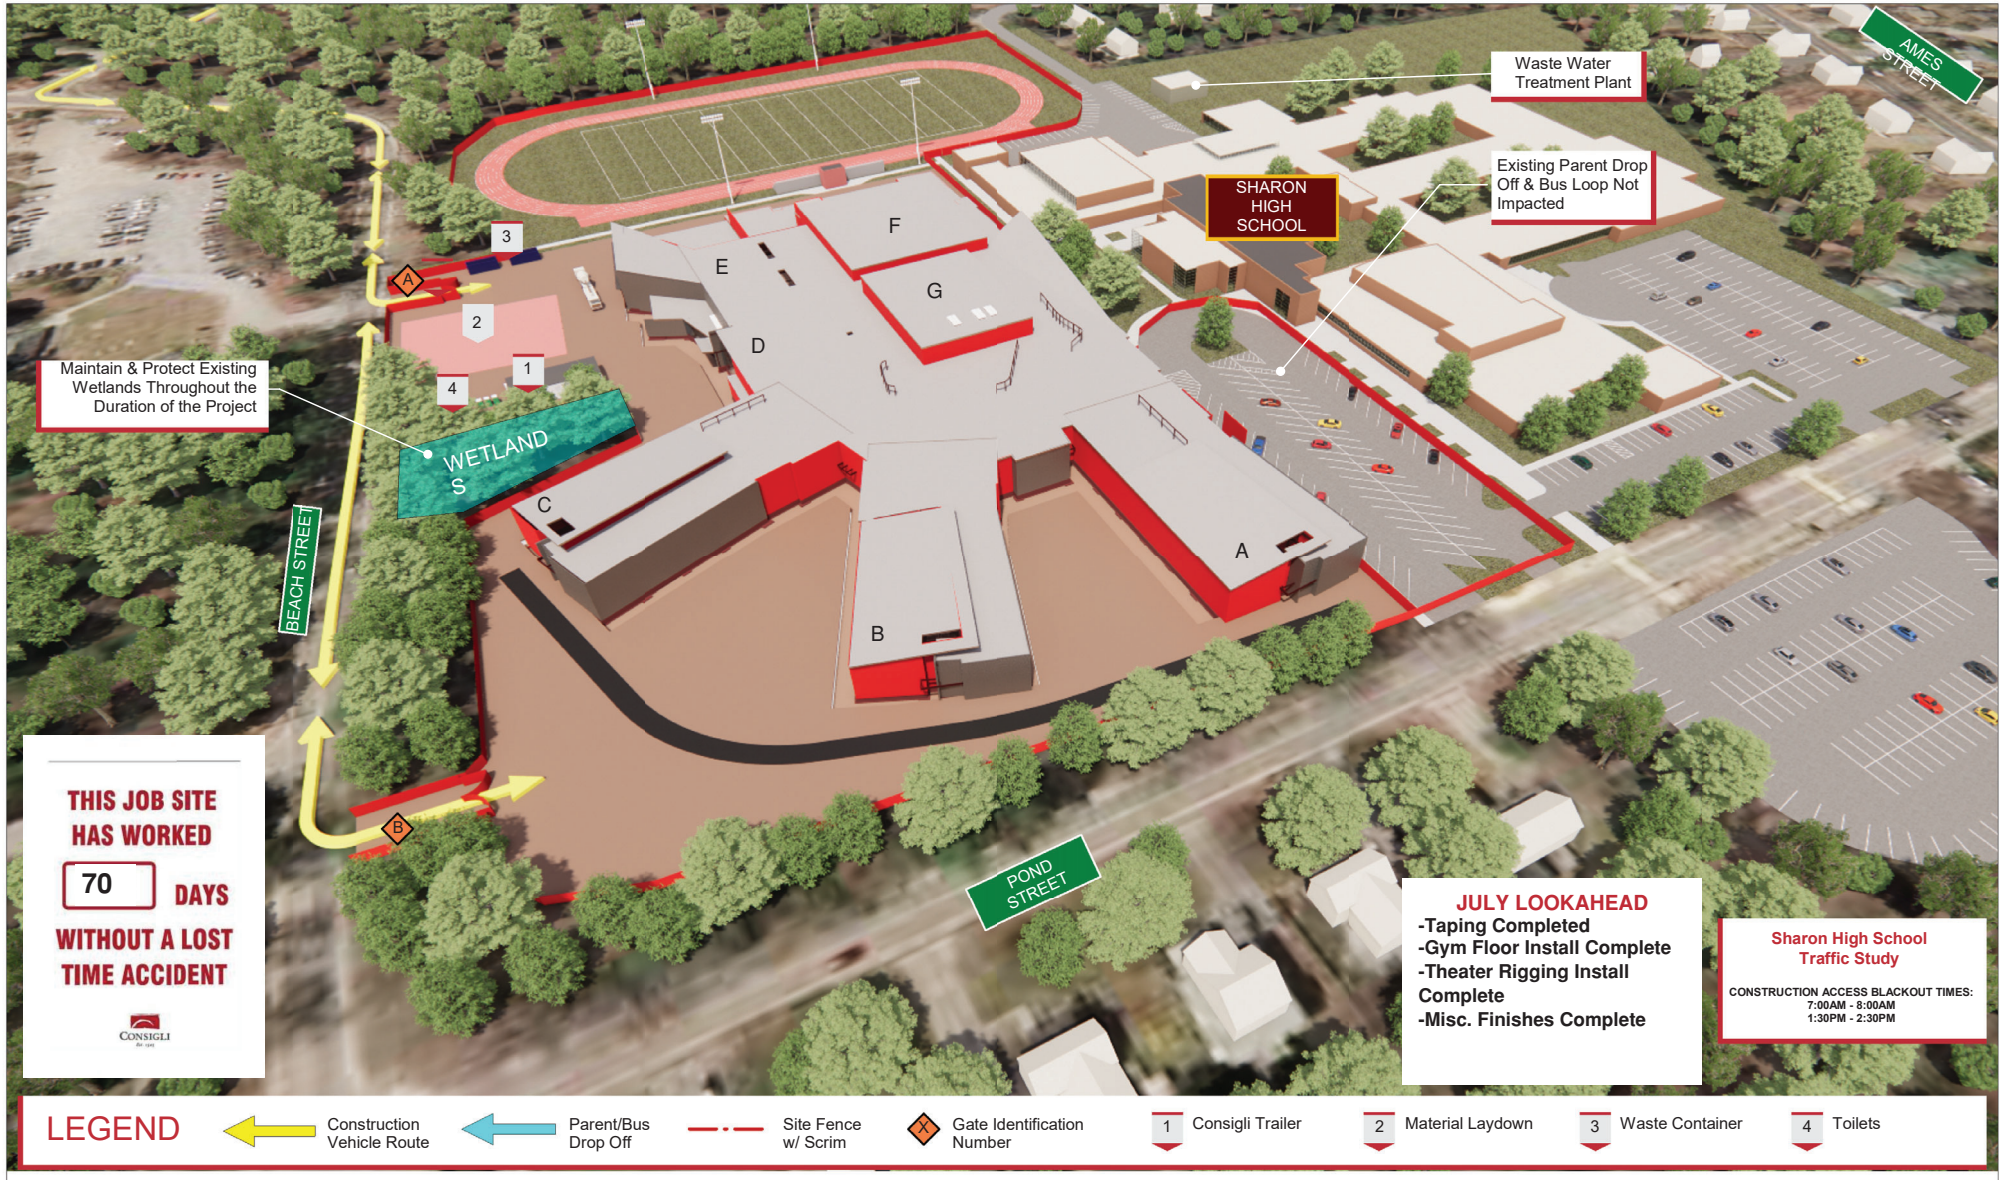

Consigli Construction - Sharon High School Project

Lookahead Schedule

7/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M
SCHOOL SCHEDULE																			
Teacher/Staff Move-in	11-Aug-22																		
MILESTONES																			
Waste Water Treatment Plant Scope Complete	29-Jul-22			CONSIGLI															
HOLIDAYS																			
SITWORK & UTILITIES																			
Form Misc. Sidewalks around the site				Riggs	X	X	X												
Place Misc. Sidewalks around the site				Riggs				X											
Backfill outdoor classroom				Vinagro	X														
Backfill pump station at Gate D				Vinagro	X	X	X	X	X										
FOOTBALL FIELD & PRESSBOX																			
Form and install rebar for pressbox footings				Riggs								X	X						
Place pressbox footings				Riggs									X	X					
Form Piers at pressbox footings				Riggs											X				
Place piers at pressbox footings				Riggs												X			
Back fill pressbox footings				Vinagro															X
Install Press Box				Dant Clayton															
ATHLETIC FACILITY BUILDINGS																			
Install Consession Sliders				Chandler Architectural								X	X						
Install Metal panel Façade				Riggs															
Install OH Duct				Apex	X	X	X	X	X										
Install OH Electric Heaters				NBK				X	X										
Install Doors				Thompson										X	X	X			
Paint Walls & OH Trusses/Plywood				King				X	X			X	X	X	X	X			
WASTE WATER TREATMENT PLANT																			
INTERIOR FITOUT/OH ROUGH/FINISHES																			
Building C - 2nd Floor																			
Install charging lockers in classroom wing				NEIS Specialties				X	X										
Install Signage Throughout Building				BlueBird	X	X	X	X	X										
Install Wall Graphic				BlueBird								X	X	X	X	X			
Install Toilet Partitons				NEIS Specialties									X	X	X	X			
Install interior phenolic panel at the end of the wing				Riggs	X	X	X	X	X										
Building C - 1st Floor																			
Install Toilet Partitons	Delivery TBD			NEIS Specialties									X	X	X	X			

Consigli Construction - Sharon High School Project

Lookahead Schedule

7/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M
Final polish				Kaloutas			X												
Install Charging lockers in classroom wing	Shipping 7/8			NEIS Specialties				X	X										
Building D - 2nd Floor																			
Wire fumehoods				WJ Griffin															
Install Operable partions/glass folding doors	Delivery TBD			Corbin Hufcor															
OH Elec inspection				WJ Griffin					X										
OH Building Inspection				CONSIGLI					X										
Flood ACT Ceilings				K&K						X		X	X	X					
Install lockers in Hallway				NEIS Specialties				X	X			X							
Install P-Lam at lockers				NEIS Casework									X	X					
Finish grouting hallway				High Point															
Finish grout at stair 3				High Point															
Building D - 1st floor																			
OH Elec inspection				WJ Griffin					X										
OH Building Inspection				CONSIGLI					X										
Flood ACT Ceilings				K&K						X		X	X	X					
Install lockers in Hallway				NEIS Specialties				X	X			X							
Install P-Lam at lockers				NEIS Casework									X	X					
Install Mirrors in wellness/weight rooms				Chandler Architectural								X	X	X					
Building E - 2nd Floor/Media Center																			
Install carpet in media center				Alleghaney								X	X	X	X	X			
Install door to the green roof				Chandler Architectural				X											
Install interior glass at media center	Delivery TBD			Chandler Architectural											X	X			X
Building E - 1st Floor/Dining Commons																			
Install Ceiling in dining commons				K&K								X	X	X	X	X	X		X
Install Mirrors in wellness/weight rooms				Chandler Architectural											X	X			
Building E - Kitchen																			
Install Coiling Doors				Overhead Doors				X	X										
Wire kitchen equipment				WJ Griffin	X	X	X	X	X										
OH Elec inspection				WJ Griffin								X							
OH Building Inspection				CONSIGLI								X							
Flood ACT Ceilings				K&K									X	X	X				
Building F - Lockerooms & Community Education																			
Install Coiling Doors in community education				Overhead Doors					X										
Building F - GYM																			
Complete Gym Floor				Kenvo	X	X	X	X	X										
Install elevated track rubber flooring				Capital Carpet								X	X	X	X	X			
Building F - Main Lobby																			
Install Veg green wall				Xquisite												X			X
Install Display Cases				Riggs	X	X	X	X	X										
Install Vinyl wall graphic				BlueBird								X	X	X	X	X			

Consigli Construction - Sharon High School Project

Lookahead Schedule

7/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25	
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	
Install Signage				BlueBird	X	X	X	X	X											
Install int glass storefronts				Chandler Architectural			X	X	X											
Install wood benches in main lobby				Riggs										X	X	X				X
Building F - Stair 6																				
Install Rubber treads				Capital Carpet											X	X				
Building F - Stair 1																				
Install interior phenolic panel at stairwell wall				Riggs	X	X	X	X	X											
Install Rubber treads				Capital Carpet											X	X				
Install Zen garden under stair 1				Xquisite																X
Building G North of Auditorium - 2nd Floor																				
OH Elec inspection				WJ Griffin					X											
OH Building Inspection				CONSIGLI					X											
Flood ACT Ceilings				K&K						X		X	X	X	X	X				
Install interior glass at HM Door Frames				Chandler Architectural	X	X	X													
Install windows in studio art	Waiting for loading zone to close			Chandler Architectural																
Caulk window sills				Armani				X												
Building G North of Auditorium - 1st Floor																				
OH Elec inspection				WJ Griffin					X											
OH Building Inspection				CONSIGLI					X											
Flood ACT Ceilings				K&K						X		X	X	X	X	X				
Install calking on countertops				NEIS Casework																
Install side lights in doorframes in admin offices				Chandler Architectural																
Install interior phenolic panel at stairwell wall				Riggs	X	X	X	X	X											
Install sidelights and transom at storefront 01&04				Chandler Architectural		X	X	X	X											
Install Storefront 01&04				Chandler Architectural	X															
Building G - Auditorium & Mezzanine																				
Install Locking Rail				Texas Scenic																
Draperly Installation at 2nd floor mezzanine				Texas Scenic			X	X	x			x								
Install Stage Flooring				Kenvo	X	X	X	X	X			X	X	X	X	X				
Install Carpet in Aisle ways in Aud and mezzanine	Need Delivery Date			Alleghaney																
Install conduit and boxes on catwalk rails				WJ Griffin	X	X	X	X	X			X	X	X	X	X				X
Theatrical Equipment install on catwalk rails				PRO AV								X	X	X	X	X				X
Install 2 Ships ladders to catwalks on stage	Need Delivery Date			Berlin Steel																
Install Tile on the stage				High Point	X	X	X	X												
Building G - Stair 2																				
Install Light Fixtures				WJ Griffin																
Install Rubber treads				Capital Carpet								X	X	X	X	X				
Building A - 2nd Floor																				
Wire Fumehoods				WJ Griffin																
Install calking on countertops				NEIS Casework																

Consigli Construction - Sharon High School Project

Lookahead Schedule

7/11/2022

Description of Work	Notes	P6 Activity Code	% Comp	Responsibility	7/11	7/12	7/13	7/14	7/15	7/16	7/17	7/18	7/19	7/20	7/21	7/22	7/23	7/24	7/25
					M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M
Install FR Door assembly at stair 2				Chandler Architectural								X	X	X	X				
Install interior phenolic panel at the end of the wing				Riggs			X	X											
Building A - 1st Floor																			
HM Glass in Door Frames				Chandler Architectural	X	X	X	X	X										
Install FR Door assembly at stair 2				Chandler Architectural				X	X	X									
Building B - 2nd Floor																			
Install Wall Tile in Hallway				High Point	X	X	X												
Grout wall tile in hallway				High Point			X	X											
OH Electrical Inspection				WJ Griffin								X							
OH Building Inspection				CONSIGLI								X							
Flood ACT Ceilings				K&K									X	X	X	X	X		
Install Bathroom Doors (2413-2418)				Thompson	X	X													
Install Bathroom Accessories				NEIS Specialties				X	X										
Install caulking on countertops				NEIS Casework				X	X										
Install interior glass at end of wing study rooms	Being delivered 7/27			Chandler Architectural															
Install interior penolic panel at the end of the wing				Riggs								X	X	X	X	X			
Building B - 1st Floor																			
OH Electrical Inspection				WJ Griffin										X					
OH Building Inspection				CONSIGLI										X					
Flood ACT Ceilings				K&K	X	X	X								X	X	X		X
Install B1 Doors				Thompson	X	X	X	X	X										
Install Bathroom Accessories				NEIS Specialties				X	X										
Install caulking on countertops				NEIS Casework				X	X										
Install interior glass at end of wing study rooms	Being delivered 7/27			Chandler Architectural															
ROOFING & FAÇADE WORK																			
Building C																			
Install corners at the end of the wing	Delivery date 7/18			Riggs									X	X	X	X	X		
Building E																			
Install phenolic panel at inside wing wall E south				Riggs	X	X	X												
Install metal panel @ green roof				Riggs															
Install metal panel under canopy @ loading zone				Riggs															
Building F																			
Install MCM over main canopy at CW 06				Riggs	X	X	X	X	X			X	X	X	X	X			
Building A																			
Install corners at the end of the wing	Delivery date 7/18			Riggs									X	X	X	X	X		
Building B																			
Install TAKTL Panels on North and East elevations				Riggs	X	X	X	X	X			X	X	X	X	X			
