

4 Week Look Ahead Schedule 07-19-21

- Structural steel erection, decking & detailing are ongoing. Steel erection is nearing completion targeting 7/22.
- Roof installation is ongoing.
- Concrete slab placement is ongoing. Preparation & placement of concrete slabs will continue to follow steel erection. Please note the next slab on grade- which may include after hours work -is tentatively scheduled for 7/26 or 7/27 (notice attached).
- Overhead MEP rough-in as well as light gauge metal framing is ongoing at multiple areas.
- Masonry installation- including shafts and CMU back-up walls are ongoing.
- Underground plumbing & electrical work is ongoing.
- Work at the athletic facility is ongoing.
- Work at the athletic field is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/











																			$\overline{}$										
		•	D SCHEDULE																<u> </u>							-			
			7/19/2021																										
Description of Work	Notes	P6 Activity Code	Responsibility	7/19 M																								8/20 8/21 FR S	
SCHOOL SCHEDULE MILESTONES																													
Structural Steel Erection Complete	22-Jul		Supermetal/GP East				Х																						
HOLIDAYS																													
WEATHER Rain Day - Friday 7/9/21																													
Rain Day - Monday 7/12/21																													
Rain - Morning of 7/19/21				Х																									
Frame exterior walls			Century																										
Install Window Blocking & Sheathing			Century																							\perp			
Envelope consultant testing & inspection Install AVB			3IVE Armani																							+			
SITE UTILITIES			Armam																										
Backfill electrical conduit at transformer and building		A9670	Marois																										
foundation Begin design work for gas main to new building			Columbia																							+			
FIELD WORK					V																								
Remove Irrigation and Strip Top Soil Pave New High Jump Area			Vinagro Vinagro	X	Х	Х	Х							Х	Х		+									+-+			
Excavate and backfill for athletic equipment footings			Vinagro						Х	Х		Х				X X	Х												
Install Athletic Equipment footings Install underground drainage			Vinagro Vinagro		Х	Х	Х	Х	X	X		X X X X		X	Х	Х Х	X			X	X	X >	(X		ХХ	X	X	X	
ATHLETIC FACILITY						,		,		,		A				, , ,	,											,	
Excavate & Backfill for UG Plumbing At Consession Stand			Marois	X	Х	х																							
Install UG Plumbing at Bathrooms			Grasseschi		^		Χ	Х	Х																				
Excavate & Backfill for UG Plumbing At Bathrooms Electric into AF			Marois MAK					Х	X																	+			
Electric in Bathrooms			Griffin				Χ	X	X																	$\pm \pm \pm$			
Mobilize Mason at Consession Stand / Layout & Set up Staging			Fernandes						X																				
Install Exterior CMU Walls at Consession Stand			Fernandes							Х	X	х х				х х										+ +			
Install Exterior CMU Walls at Bathrooms			Fernandes MEP Trades						V	Х		X X X X			X											1			
MEP Rough in CMU walls Underground Utilities/Slab on Grade			WEF Trades						^	^		^ ^		^	^	^ ^	^												
Building A																													
Place Building A SOG	Supply Issue due to Rain Delays - Placement moved from 7/20/21		Riggs						x	Х																			
Building B																													
Install underground electrical Fine Grade For SOG		A8890	Griffin Marois	X	X	X	V	~	X																				
Install Vapor Barrier/Insulation at SOG			Riggs	^	^	^	^	^		Х	Х															+			
Install Mesh at SOG			Riggs									Х									V								
Install Electrical Floor Boxes Place Building B SOG			Griffin Riggs								X 2	X X		Х						Х		X				+			
Building E			50																										
Excavate and backfill for underground Plumbing/Electrical			Marois	X	Х	х	х	x																					
Install Sanitary underground - Kitchen Waste Run		A9080	Grasseschi	Χ	Х	Χ	Χ	Х	Х	Х	Х									Х	Х	Х							
Install UG Electrical		A9090	Griffin	X	Х	Χ	Х	Х																		+			
Final Grade Install Vapor Barrier/Insulation at SOG		A9440	Marois									X X		Х	Х	Х Х										+			
Install Vapor Barrier/Insulation at SOG Install Mesh at SOG		A944U	Riggs Riggs														X			Х	Х	X >	(X			+			
Building D			เมลลล																			^ /	X						
Install underground electrical		A8970	Griffin						Х	Х	X 2	Х			Х					.,	V	V	, .						
Fine Grade for SOG Install Vapor Barrier/Insulation at SOG		A9410	Marois Riggs											Х	Х	X X	X			X	X	X X	X X			+			
Install Mesh at SOG		A9410	Riggs																						ХХ	X			
Install Electrical Floor Boxes Place Building D SOG		A9410	Griffin Riggs																							+	Х	X	
Building F		710410	านชูชูง																										
FPS Concrete Collar Boxes	Include Epoxy at Base Plates		Riggs	Х	Х	Х	Х	Х							T														
Excavate and Backfill for underground Plumbing/Electrical	Flates		Marois	Х	Х	Х	Х	Х	X	Х																			
Install Sanitary underground			Grasseschi	Х	Х					,																† †			
Install UG Electrical			Griffin	X		Х	Х	Х																		† †			
			Marois	Х																									
Fine Grade (Excluding Gym)			Wai 013															_								\perp			
Fine Grade (Excluding Gym) Install Vapor Barrier/Insulation at SOG Install Mesh at SOG		A9430 A9430	Riggs Riggs		Х	Х	Х	X		X																			


		•	D SCHEDULE 7/19/2021																									
Description of Work	Notes	P6 Activity Code	Responsibility	7/19 7/2 M T				23 7/2 R S	7/26 M			9 7/30 R FR	8/1 S					8/8 S		/10 8/1 T W		12 8/13 R FR		8/16 8/17 M T				21 8/22 S S
Install electrical conduit at Slab			Griffin							Х	Х																	
Place Building F SOG Steel Erection/Concrete Slab on Deck			Riggs								Х																	
Steel Erection/Concrete Slab on Deck Building C																												
Building E																												
Install Railing supports at green roof		A9370	GP East																									
Place Concrete Deck at Green Roof	Placed with E Building	A9370	Riggs																									
	SOG	A9370	Niggs																									
Building D																												
Building F Deck and Detail F Building (GYM)		A9220	Supermetal/GP East	х х		X 2	ХХ																					
Install Roof Blocking at GYM Perimeter		A9220	Century	^ ^			X X		X	Х																		
Roof Deck Turnover			Consigli																									
Roof Drain Layout			Grasseschi				X X																					
Install Blocking at Roof Drains Deck and Detail elevated track			Century Supermetal/GP East			,	X X																					
Install MEP Roof Penetrations		A9360	MEP Trades																									
FPS SOD	+	/18000	Riggs																									
SOD Placement (Place with Building G)			Riggs																									
Building A																												
Building B	Attor Tarain 2011																											
Deck and Detail B Building - Roof	After Topping Off Ceremony	A9170	Supermetal/GP East						X	Х	x x	X		Х	X >	X	Х											
Place SOD	Scromony		RIggs				Х																					
Building G																												
Steel Erection G Building		A9140	Supermetal/GP East	X X						.,	.,																	
Deck and Detail Building G Layout & Install MEP Penetrations			Supermetal/GP East MEP Trades	X X	.)	X 2	X X		X	Х	X X	Х		V	X													
Install Mesh & Rebar			Riggs											^	^ /	X	X		Х	Х Х	: X	. X						
FPS SOD			Riggs																					ХХ	Х	Х	X	
Roofing/Façade/Fit Out/MEP OH Rough																												
Building C - 2nd Floor																												
Initial Polished Concrete		A14950 A9950	Kaloutas	V V		v ,	ХХ							Х	X >	X	X											
Framing Exterior Walls Install window blocking		A9950	Century Century	X X			X X		X	X	X																	
Install OH Duct and HVAC Pipe			NBK	X X		X 2	X X		X	X	X X	Х																
Install OH Plumbing			Grasseschi																									
Frame Interior Walls Building C - 1st Floor			Century	X X)	X 2	X X		X	Х	X X	Х																
Install MEP Hangers			MEP Trades																									
Install OH FP Rough			JCI	ХХ			Х Х																					
Framing Exterior Walls		A9950	Century	X X			X X																					
Install window blocking Initial Polished Concrete		A15050	Century Kaloutas	X X		X /	X X		X	Х	X X	X							v	Х Х		, v						
Install OH Duct and HVAC Pipe	Pending Delivery Date	A 15050	NBK						^										^	^ ^	^							
Install OH Plumbing	· · · · · · · · · · · · · · · · · · ·		Grasseschi																									
Frame Interior Walls		A12810	Century											Х	X >	X	X		X	X X	X	X						
Building E - 2nd Floor			MED To - !																									
Install MEP Hanger Stubs - prior to fire proofing			MEP Trades			·	V .																					
Install Fire Proofing - Interior structure/Roof Deck		40050	H Carr	XX			X X																					
Framing Exterior Walls Install window blocking		A9950	Century Century	X X			X X X		X	Х	ХХ	X																
Install OH Duct and HVAC Pipe	1	A11110	NBK						X	X	X X	X		Х	X >	X	Х											
Install OH Plumbing		A11170	Grasseschi	X X		X 2																						
Install OH FP Rough		A11180	JCI	X X		X 2	X X																					
Frame Interior Walls Building D - 2nd Floor		A11410	Century																									
Install MEP Hanger Stubs - prior to fire proofing			MEP Trades	X X	,	X :	ХХ																					
Install Fire Proofing - Overhead (Roof Structure)			H Carr						Х	Х	Х Х	Х																
Initial Polished Concrete		A14930	Kaloutas																									
Framing Exterior Walls Install OH Duct and HVAC Pipe	Awaiting Delivery Date	A9950 A11120	Century NBK		-		_															_						
Install OH Plumbing	Awaiting Delivery Date	A11120 A11210	Grasseschi																									
Install OH FP Rough		A11220	JCI																									
Frame Interior Walls		A11440	Century																									
Building F		A40040	Cantum				y v		V	X	Y																	
Install Roof Blocking (GYM) Install Roofing (GYM)		A10940	Century Capeway			'	X X		^	^		X		Х	X >	(X	Х											
Install HM Door Frames			Century												X													
Install CMU in Lockerooms			Fernandes																X	X X	X	X						
Building A Install LGMF at Low/High Roofing Wall			Century											V	X	, ,	X		V	X X		, ,						
Install LGMF at Low/High Roofing Wall Initial Polished Concrete A2			Kaloutas											۸	^ '	λ λ	^		^	^ X	· X	X X		ХХ	X	X	X	
Building B			ituioutus																					^ ^	Λ			
Install Roof Blocking			Century						X	Χ	ХХ	Х		Χ	X >	X	X		Χ	X X	X	X						
																								_				

		'	D SCHEDULE 7/19/2021																																	
			1/19/2021																																	-
Description of Monte	Notes	P6 Activity	Deen an aibilite	7/19	7/20	7/21	7/22	7/23 7/2	24 7/2	25 7/2	6 7/27	7/28	7/29	7/30	7/31	8/1	8/2	8/3	8/4	8/5	8/6	8/7	8/8	8/9 8	3/10 8	/11 8	12 8	13 8	/14 8/	15 8/1	6 8/1	17 8/18	8/19	8/20	8/21	8/22
Description of Work	Notes	Code	Responsibility	М	Т	w	TR	FR S	S	М		w		FR		s	М	Т	w	TR	FR	S	s	М					s s	6 M		· w		FR	s	
Install LGMF at Low/High Roofing Wall			Century																																	
Building G																																				
Install Roof Blocking			Century																																	
Install CMU at Auditorium Walls			Fernandes														Х	Х	Χ	Χ	Х			Χ	Χ	Χ	X	X		Х	X	X	Χ	Χ		
Install CMU at Elevator 2			Fernandes							X	X	Х	Х	Х																						

Sharon High School



SHARON HS PROGRESS UPDATE JULY 2021

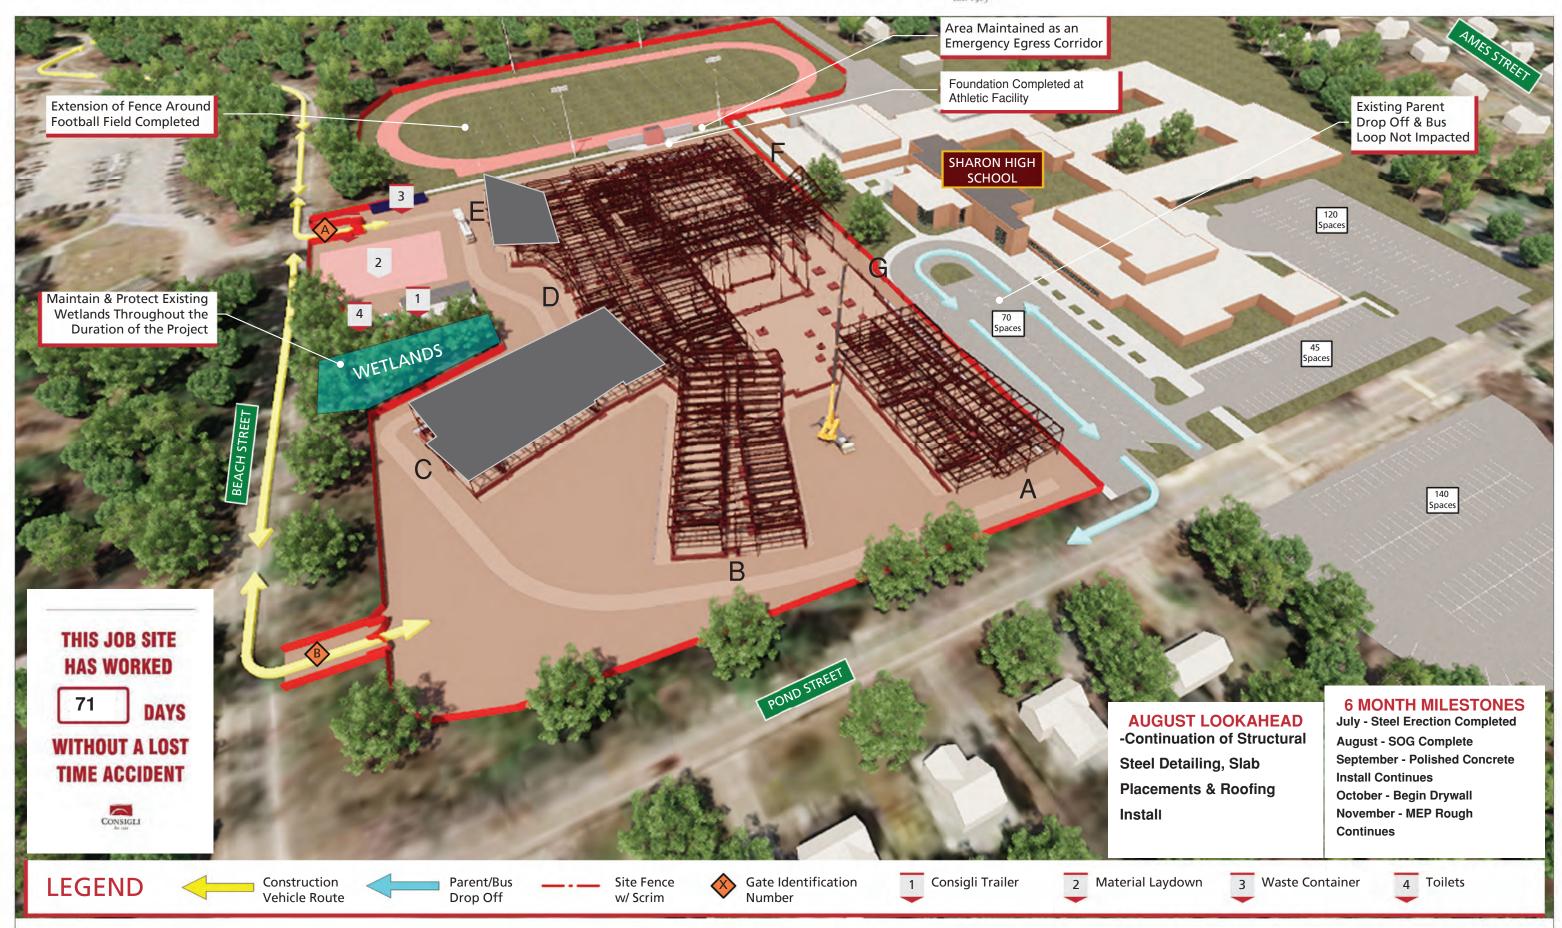



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at https://www.shsbuilding.com/

Best Regards,

Matthew Gulino

Associate | Owner's Project Manager

PMA Consultants

mgulino@pmaconsultants.com

Matthew Gulino
