

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule 08-02-21

- Structural steel erection is complete. Minor decking & detailing is ongoing.
- Roof installation is ongoing.
- Concrete slab placements are ongoing.
- Overhead MEP rough-in is ongoing at multiple areas
- Both interior and exterior light gauge metal framing are ongoing at multiple areas.
- Masonry installation - including interior auditorium walls- is ongoing.
- Underground plumbing & electrical work is ongoing but nearing completion
- Polished concrete has started on the 2nd floor.
- Work at the athletic field including drainage & athletic equipment foundations is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>


Town of  
**SHARON**  
Massachusetts



# Sharon High School



**SHARON HS PROGRESS UPDATE  
AUGUST 2021**

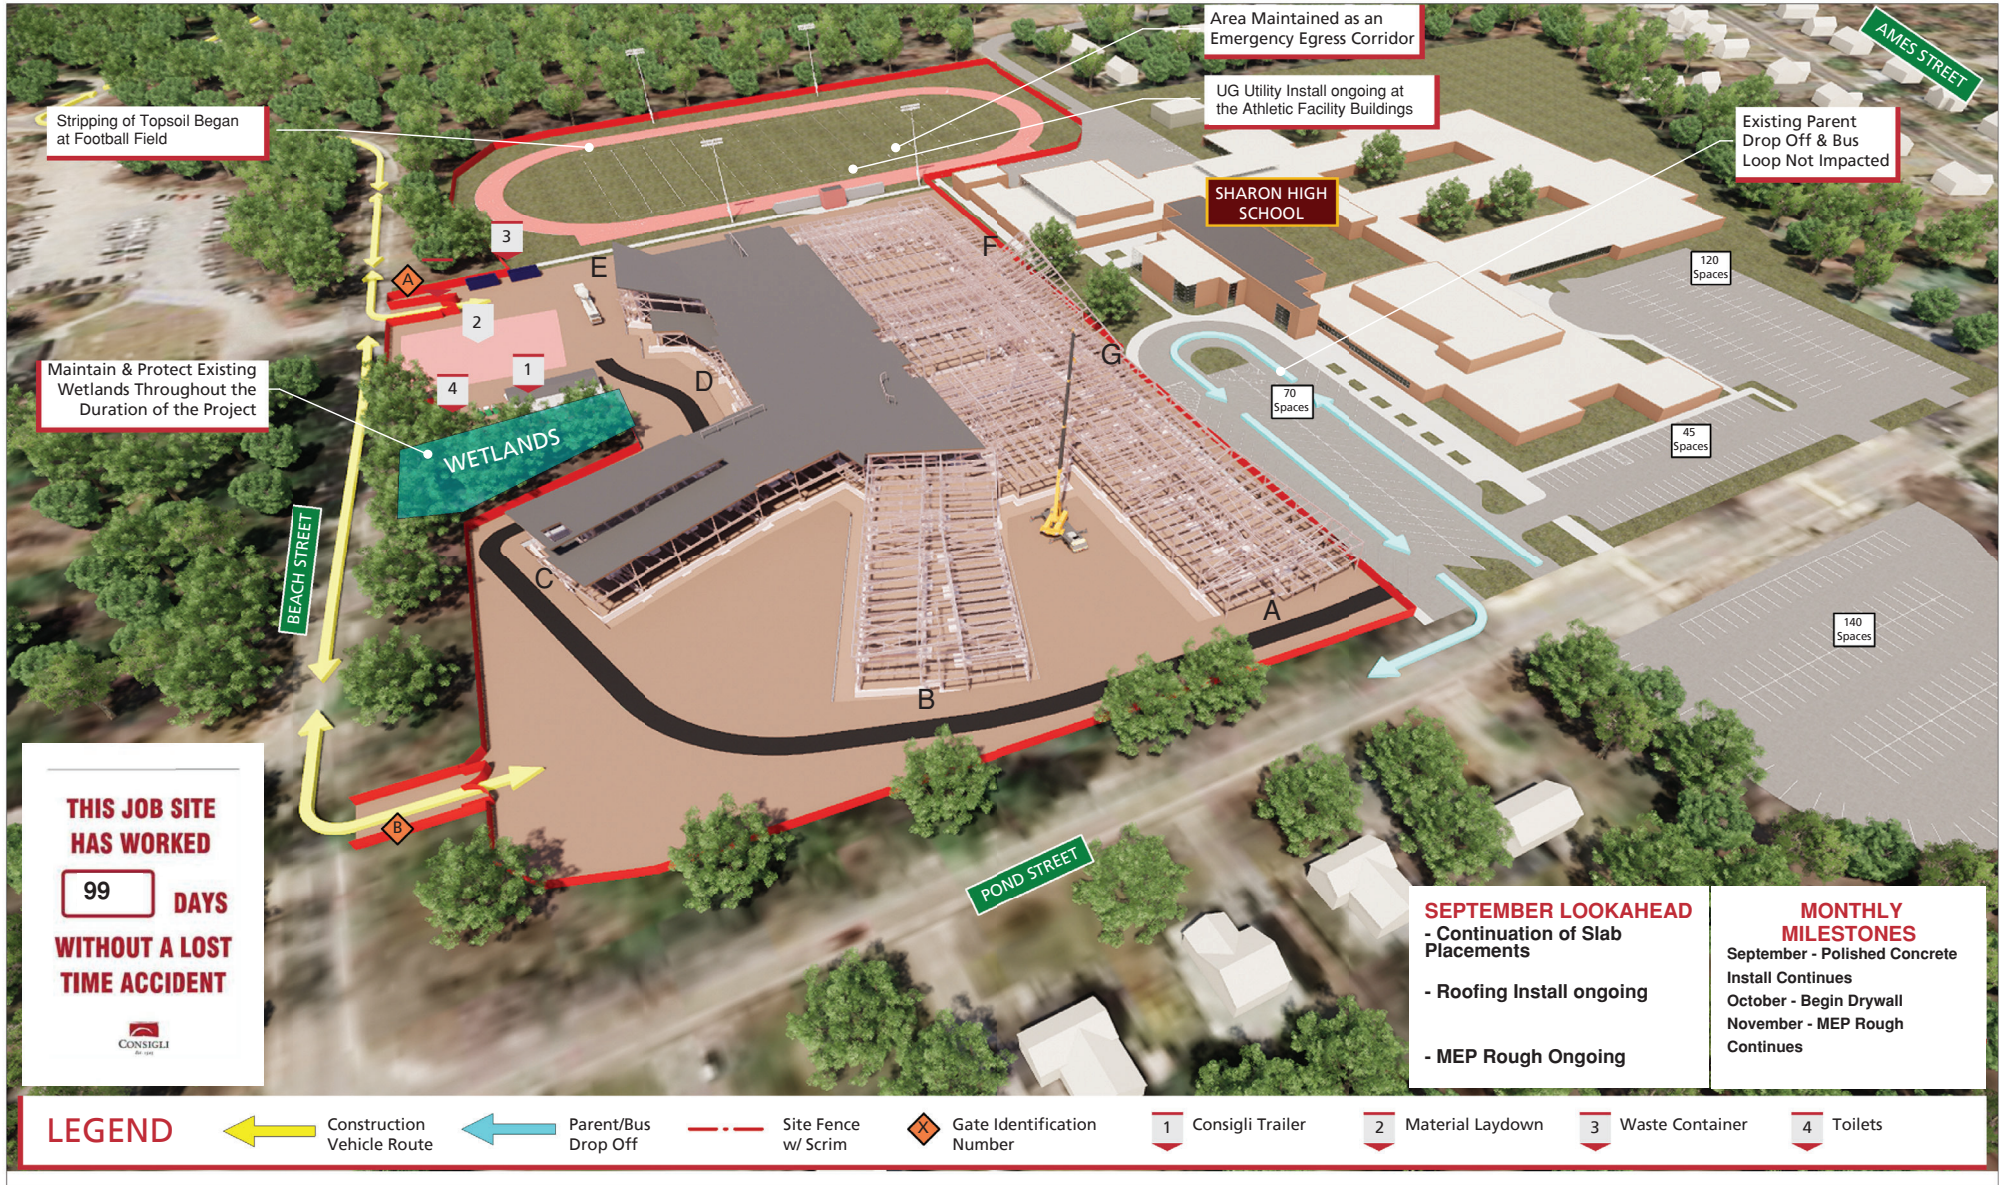

LOOK AHEAD SCHEDULE

8/2/2021

Description of Work	Notes	P6 Activity Code	Responsibility	8/2	8/3	8/4	8/5	8/6	8/7	8/8	8/9	8/10	8/11	8/12	8/13	8/14	8/15	8/16	8/17	8/18	8/19	8/20	8/21	8/22	8/23	8/24	8/25	8/26	8/27	8/28	8/29	8/30	8/31	9/1	9/2	9/3	9/4		
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
<b>SCHOOL SCHEDULE</b>																																							
SHS - Teachers First Day Back	26-Aug																																						
SHS - Students First Day Back	30-Aug																																						
<b>MILESTONES</b>																																							
<b>HOLIDAYS</b>																																							
<b>WEATHER</b>																																							
<b>MOCK UP</b>																																							
Frame exterior walls			Century								X	X	X	X	X																								
Install Window Blocking & Sheathing			Century											X	X		X																						
Envelope consultant testing & inspection			3IVE																X	X																			
Install AVB			Armani																					X	X	X	X	X											
<b>SITE UTILITIES</b>																																							
Continual check in with Columbia for gas service			Columbia																																				
Continual check in with Eversource on pole relocation			Eversource																																				
<b>FIELD WORK</b>																																							
Pave New High Jump Area			Vinagro				X																																
Excavate For Pressbox footings			Vinagro			X																																	
FPS Pressbox Footings			Riggs			X	X	X			X	X																											
Backfill Pressbox Footings			Vinagro									X	X	X																									
Excavate and backfill for athletic equipment footings			Vinagro								X	X	X	X	X																								
Install Athletic Equipment footings			Xquisite									X	X	X	X																								
Install underground drainage			Vinagro	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
<b>ATHLETIC FACILITY</b>																																							
Install Interior CMU Walls at Concession Stand & Bathrooms			Fernandes																																				
MEP Rough in CMU walls			MEP Trades																																				
<b>Underground Utilities/Slab on Grade</b>																																							
<b>Building A</b>																																							
<b>Building B</b>																																							
Install Electrical Floor Boxes			Griffin																																				
Place Building B SOG			Riggs																																				
<b>Building E</b>																																							
Install UG Storm line			Grasseschi			X	X																																
Backfill and fine grade storm			Marois				X	X			X	X																											
Install Conduit for Electrical Floor Boxes			Griffin									X	X	X																									
Install Vapor Barrier/Insulation at SOG		A9440	Riggs														X	X	X	X																			
Install Mesh at SOG			Riggs																			X		X	X	X													
Install Electrical Floor Boxes			Griffin																								X	X											
Install Radiant Flooring			NBK/APEX																																				
Place Building E SOG			Riggs																																				
<b>Building D</b>																																							
Install underground electrical		A8970	Griffin	X	X	X	X	X			X	X	X																										
Backfill & Fine Grade for SOG			Marois	X	X	X	X	X			X	X	X	X	X																								
Install Vapor Barrier/Insulation at SOG		A9410	Riggs											X	X		X																						
Install Mesh at SOG		A9410	Riggs														X	X	X	X																			
Install Electrical Floor Boxes			Griffin																			X	X																
Place Building D SOG		A9410	Riggs																					X										X					
<b>Building F</b>																																							
Fine Grade (Excluding Gym)			Marois			X	X	X			X																												
Install Edge Form			Riggs								X	X	X	X																									
Install Vapor Barrier/Insulation at SOG		A9430	Riggs								X	X	X	X	X																								
Install Mesh at SOG		A9430	Riggs														X	X	X																				
Place Building F SOG			Riggs																	X	X																		
<b>Steel Erection/Concrete Slab on Deck</b>																																							
<b>Building E</b>																																							
Install Railing supports at green roof		A9370	GP East								X	X	X	X	X																								
Place Concrete Deck at Green Roof	Placed with E Building SOG	A9370	Riggs																																				
<b>Building D</b>																																							
<b>Building F</b>																																							
Install MEP Roof Penetrations		A9360	MEP Trades			X	X	X																															
Detail Weld at Track			GP East								X	X	X	X	X																								
Install Mesh at Elevated Track											X	X	X	X	X																								
FPS SOD - Elevated Track			Riggs																																				
SOD Placement Elevated Track			Riggs															X	X	X	X	X																	
<b>Building B</b>																																							
Deck and Detail B Building - Roof		A9170	Supermetal/GP East										X	X		X	X	X	X	X																			
<b>Building G</b>																																							
Deck and Detail Building G Roof			Supermetal/GP East	X	X	X	X	X			X	X	X																										
Layout & Install MEP Penetrations G 2nd Floor			MEP Trades																																				
Install Mesh & Rebar at 2nd Floor Deck			Riggs																																				
FPS SOD G North			Riggs																																				
<b>Roofing/Façade/Fit Out/MEP OH Rough</b>																																							
<b>Building C - 2nd Floor</b>																																							





**Sharon High School: Notice of Potential After-Hours Work**

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

*Matthew Gulino*

Matthew Gulino  
Associate | Owner's Project Manager  
PMA Consultants  
[mgulino@pmaconsultants.com](mailto:mgulino@pmaconsultants.com)
