

The Sharon High School Construction Project




4 Week Look Ahead Schedule 10-12-21

- Structural steel detailing is nearing completion. Stair installation is also ongoing.
- Roof installation is ongoing.
- Slab on grade placements are ongoing coordinating w/ below & in slab MEPs.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. Pulling of electrical is also ongoing.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. Installation of drywall tops is ongoing. Wall close-in is scheduled for the coming weeks.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing.
- Windows are beginning to arrive on-site. Mock up installation & testing upcoming.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Work at the athletic field- including prep for sod- is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



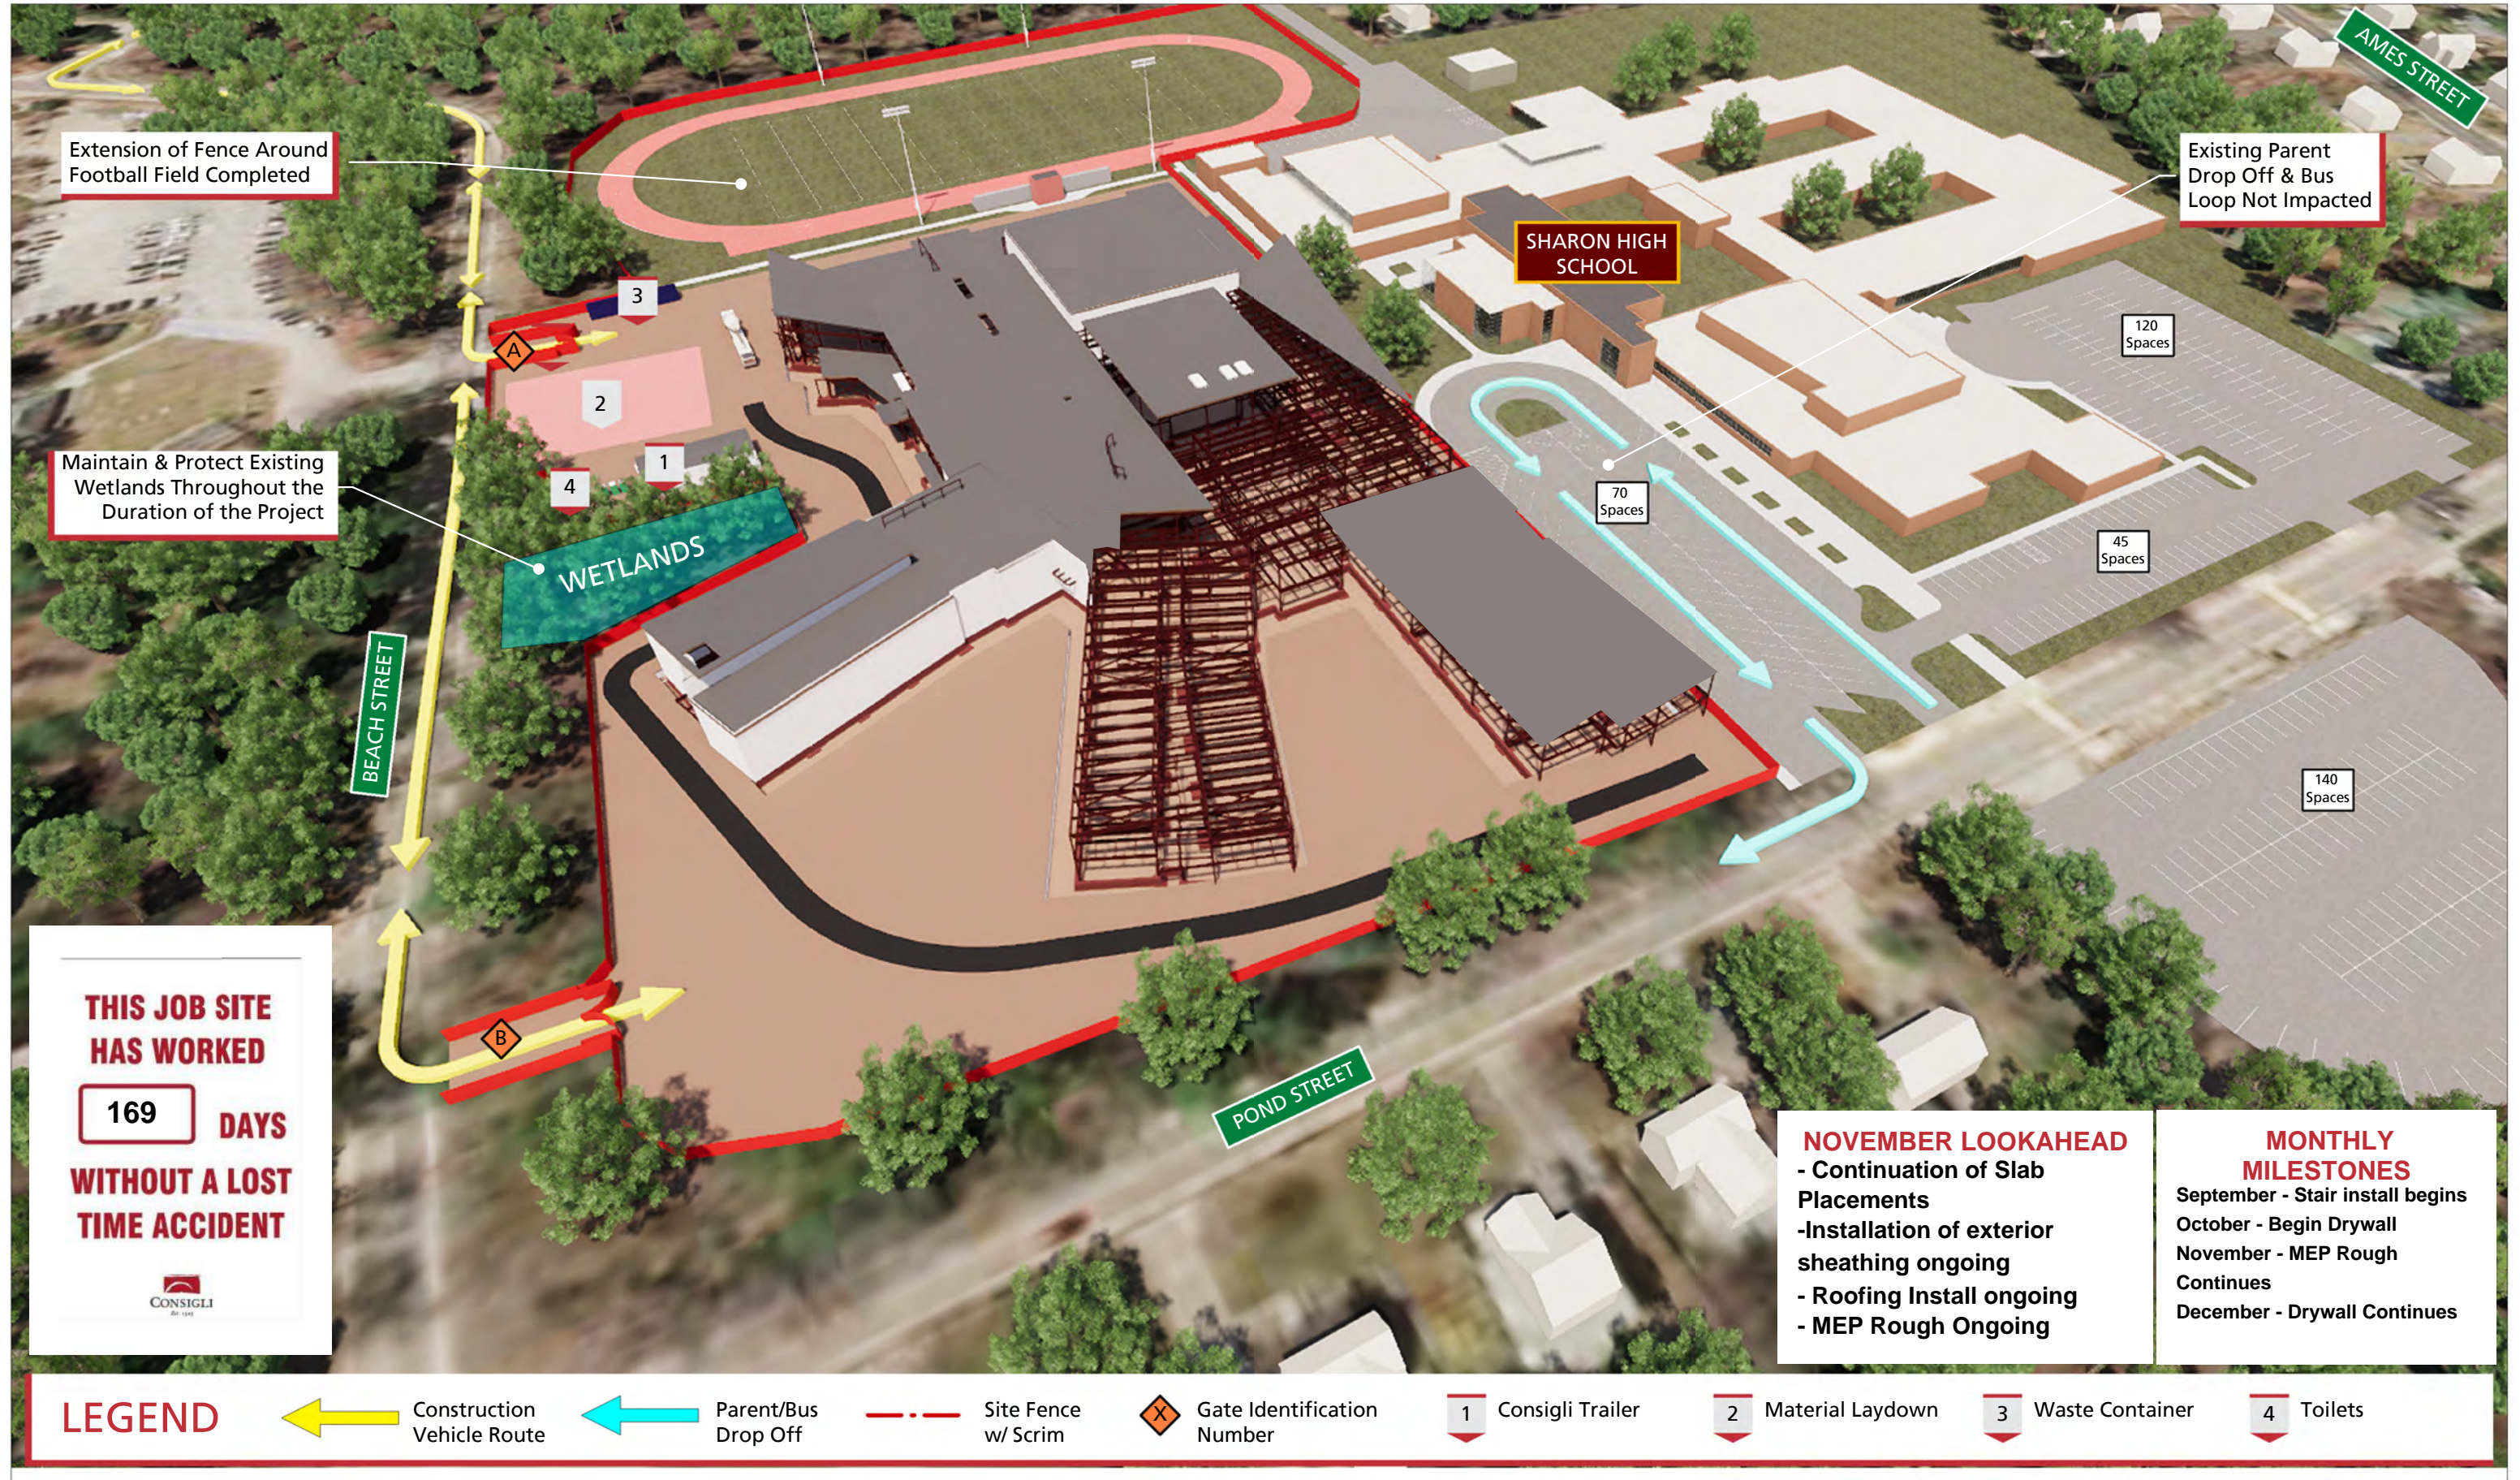

LOOK AHEAD SCHEDULE

10/12/2021

Description of Work	Notes	P6 Activity Code	Responsibility	10/12	10/13	10/14	10/15	10/16	10/17	10/18	10/19	10/20	10/21	10/22	10/23	10/24	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/6	
				T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
SCHOOL SCHEDULE																															
MILESTONES																															
HOLIDAYS																															
Columbus Day - Site will be open				X																											
WEATHER																															
MOCK UP																															
Install AVB			Armani	X	X	X	X																								
Install Aluminum Windows			Chandler																												
SITE UTILITIES																															
Continual check in with Eversource for gas service			Eversource																												
Continual check in with Verizon on pole relocation			Verizon																												
FIELD WORK																															
Excavate for Long Jump Pits			Vinagro	X	X	X	X																								
Form Place Strip Long Jump Pits			Riggs							X	X	X	X	X				X	X												
Install Sidewalk around Discus Cage			Xquisite															X	X												
Install Athletic Equipment footings			Xquisite																												
Lay Sod			Xquisite									X	X	X																	
ATHLETIC FACILITY																															
Install Interior CMU Walls at Concession Stand & Bathrooms	PENDING COORDINATION AND TRUSS DESIGN		Fernandes																												
MEP Rough in CMU walls			MEP Trades																												
CONCRETE FLATWORK AND UNDERGROUND UTILITIES																															
Building E																															
Install Grease Traps at Kitchen			Grasseschi															X	X	X	X										
Install Radiant Flooring			NBK	X	X	X	X																								
Install Top Layer Mesh at SOG at radiant flooring			Riggs																					X	X	X					
Place Building E SOG at dining commons & radiant flooring			Riggs																							X					
STEEL ERECTION/DETAILING																															
Building B																															
Install all window and brick support angles			Supermetal/GP East	X	X	X	X																								
Set perimeter roof blocking and cantilevered supports			Supermetal/GP East	X	X	X	X																								
Weld roof screens and channel supports			Supermetal/GP East	X	X	X	X																								
Building G																															
Install (2) Brace frames at Black Box	To be installed after auditorium slab has been prepped		Supermetal/GP East																												
INTERIOR FITOUT/OH ROUGH																															
Building C																															
Install OH Duct - 2nd floor			APEX	X	X	X	X			X	X	X	X	X																	
Install OH Duct - 1st floor			APEX							X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Plumbing Rough in Walls at Science rooms			Grasseschi	X	X	X	X																								
Electrical/Fire Alarm/TelData Inwall Rough - 2nd Floor			Griffin	X	X	X	X																								
Electrical/Fire Alarm/TelData Inwall Rough - 1st Floor			Griffin							X	X	X	X	X																	
Insulate Plumbing Lines - 1st & 2nd Floor			Grasseschi														X	X	X	X	X										
Building D																															
Initial Polished Concrete - 2nd Floor	Kaloutas Re-Mob onsite Mid Nov	A15050	Kaloutas																												
Install OH Plumbing - 2nd Floor			Grasseschi	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Electrical/Fire Alarm/TelData Inwall Rough - 2nd Floor	Not Inc. Wire		Griffin																												
Plumbing Rough in Walls at Science rooms - 2nd Floor			Grasseschi	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Install Door Frames - 1st Floor			Century																												
Tie in Roof Drains - 1st Floor			Grasseschi	X	X	X	X																								
Install OH Plumbing - 1st Floor			Grasseschi																												
Plumbing Rough in Walls at Science rooms - 1st Floor			Grasseschi	X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Building E																															
Install Drywall Tops			Century																												
Install OH Plumbing - 2nd Floor			Grasseschi	X	X	X	X			X	X	X	X	X																	
Plumbing Rough in Walls at Science rooms - 2nd Floor			Grasseschi	X	X	X	X			X	X	X	X	X																	
Insulate Plumbing Lines - 2nd Floor			Grasseschi														X	X	X	X	X										
Electrical/Fire Alarm/TelData Inwall Rough - 2nd Floor	Not Inc. Wire		Griffin																												
Building F																															
Install Stair 1 Rails			Berlin Steel	X	X																										
Install Intumescent FP - GYM			H. Carr																												
Install Spray FP - 1st Floor			H. Carr														X	X	X	X	X			X	X	X	X	X			

LOOK AHEAD SCHEDULE
10/12/2021

Description of Work	Notes	P6 Activity Code	Responsibility	10/12	10/13	10/14	10/15	10/16	10/17	10/18	10/19	10/20	10/21	10/22	10/23	10/24	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/6
				T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S
Install Roofing			Capeway													X	X	X	X	X			X	X						



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
