

The Sharon High School Construction Project



4 Week Look Ahead Schedule 10-25-21

- Continue Stair installation & placing concrete treads.
- Roof installation is ongoing.
- Slab placements are targeting Auditorium & Dining areas over the next 3 weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. Pulling of electrical is also ongoing.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. In wall inspections are ongoing. Wall close-in is scheduled to begin this week.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing.
- Installation of exterior panel back-up system is beginning in the coming weeks.
- Windows are beginning to arrive on-site. Mock up installation & testing upcoming.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Work at the athletic field is ongoing- sod installation is scheduled for next week.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts




PMA Consultants



TAPPÉ
ARCHITECTS



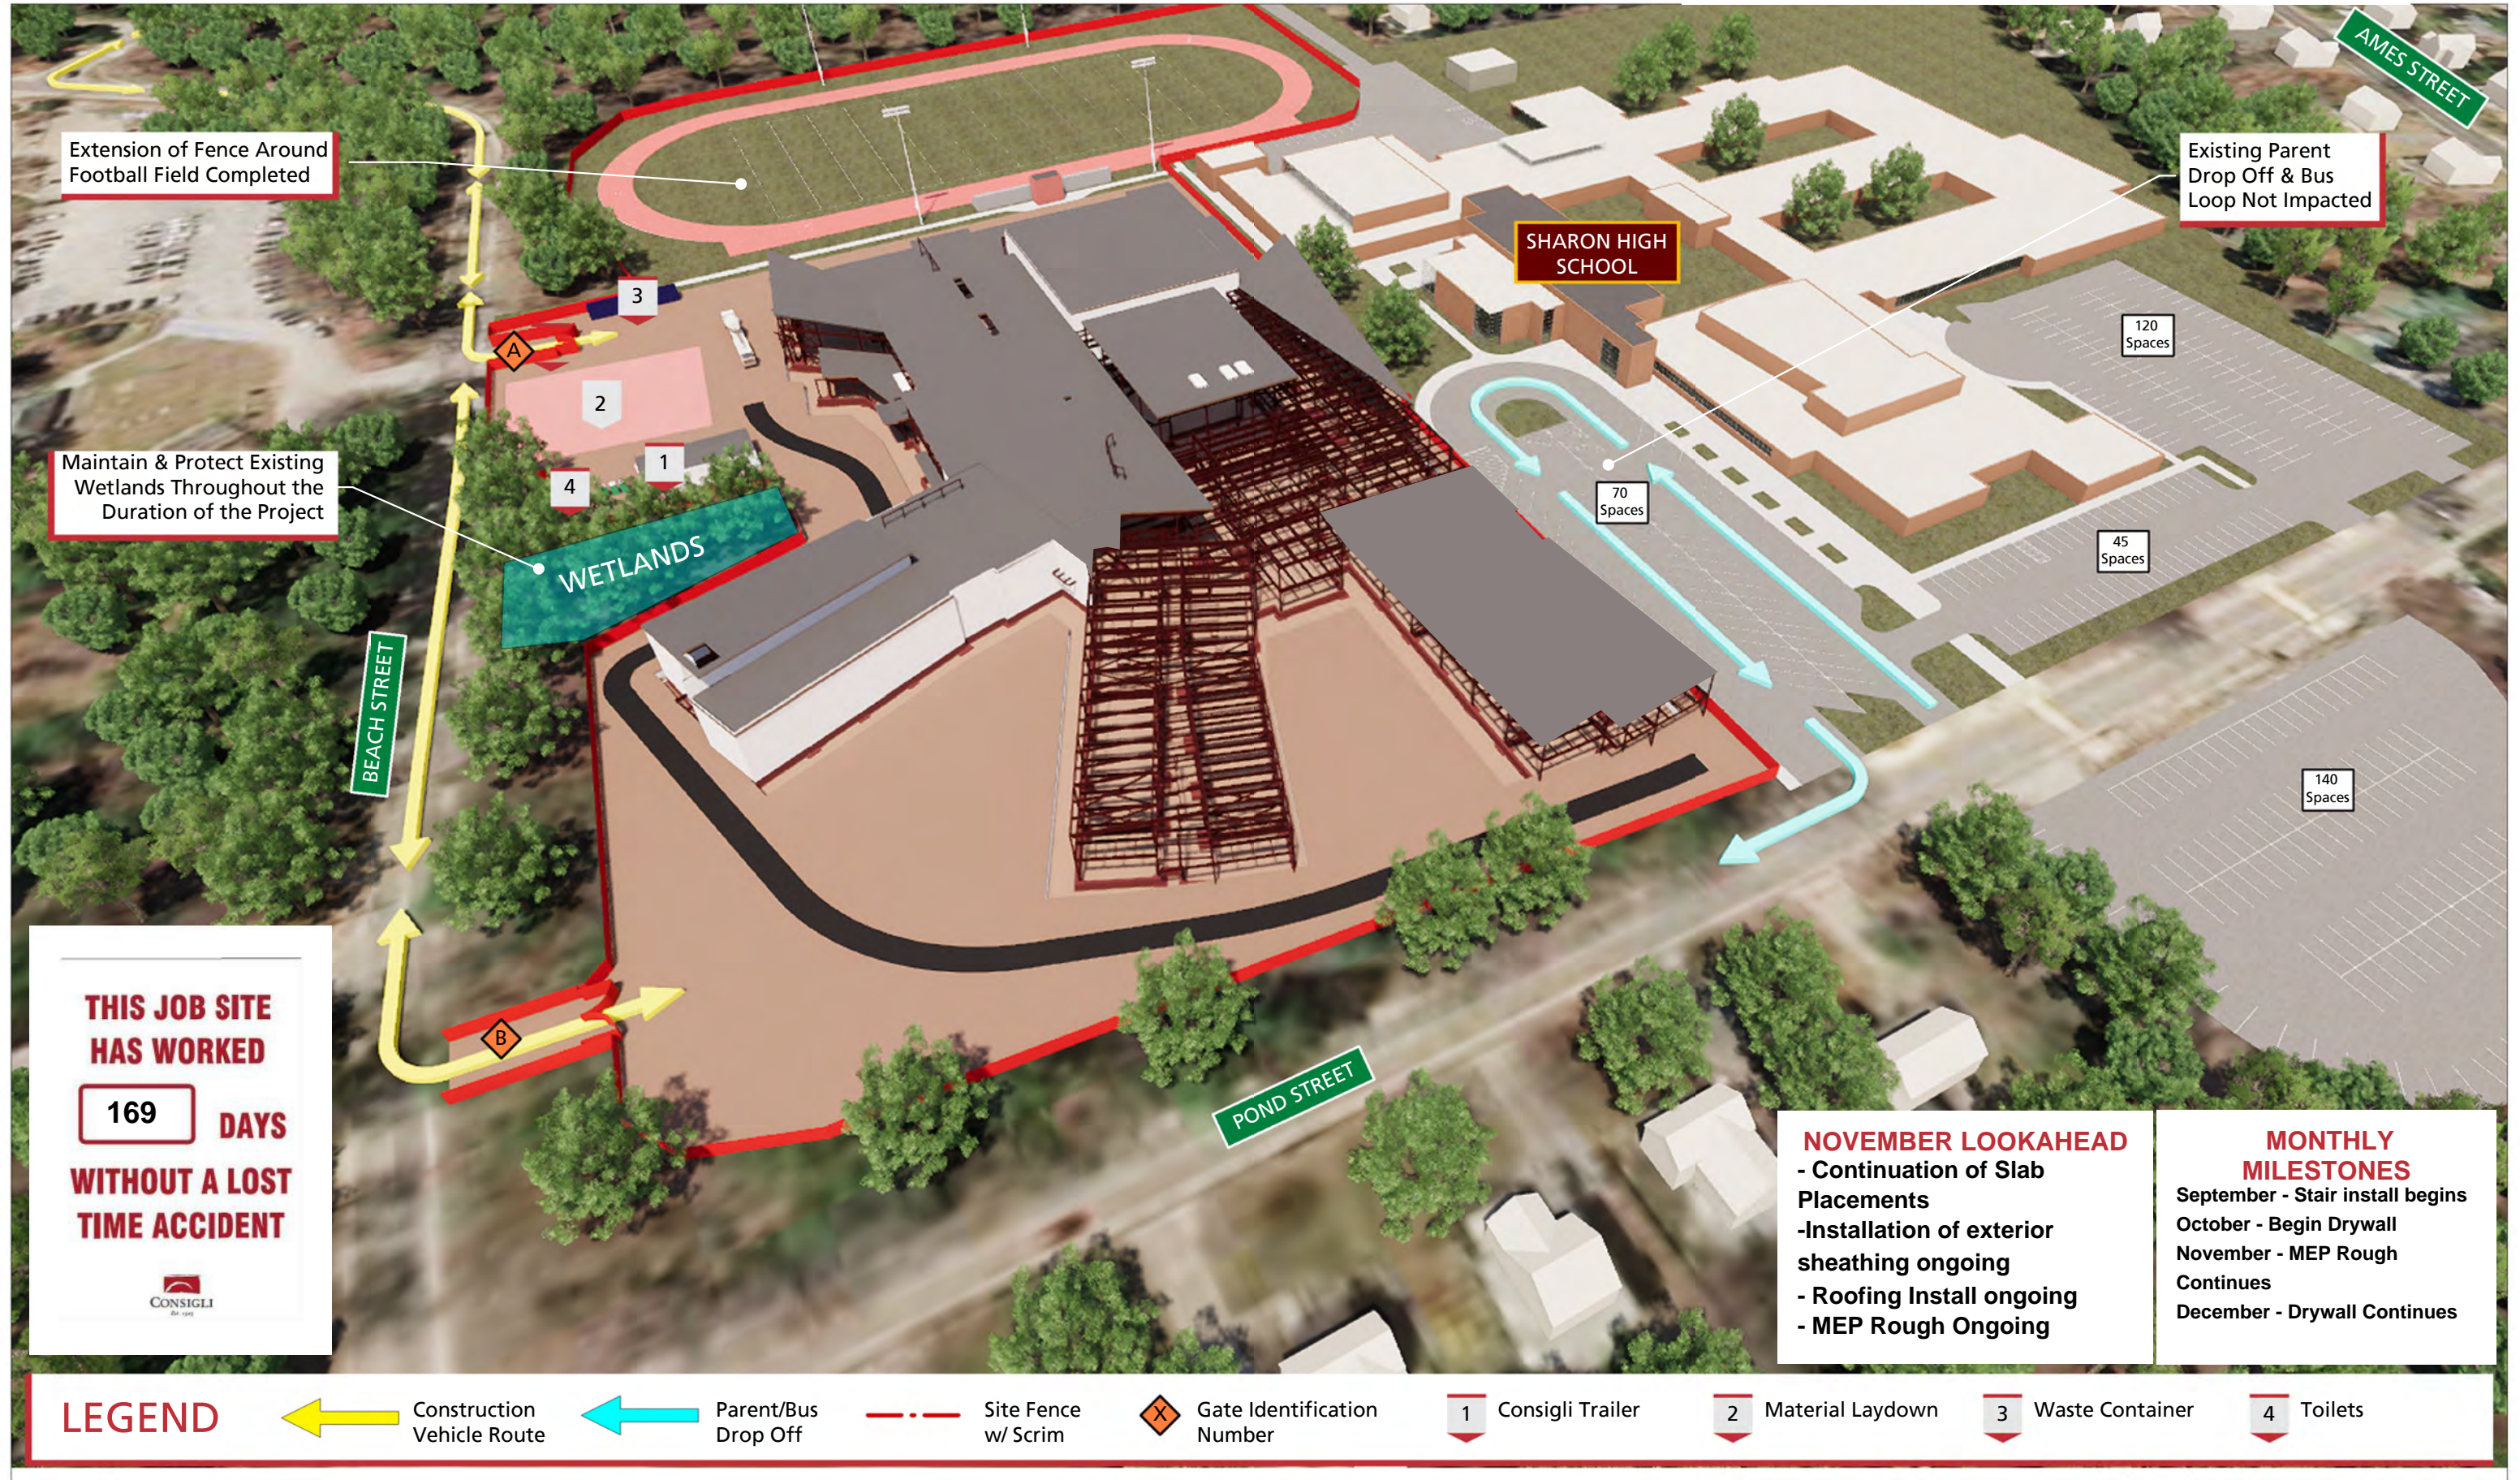

LOOK AHEAD SCHEDULE

10/25/2021

Description of Work	Notes	P6 Activity Code	Responsibility	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/7	11/8	11/9	11/10	11/11	11/12	11/13	11/14	11/15	11/16	11/17	11/18	11/19	11/20	11/21	
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
SCHOOL SCHEDULE																																
MILESTONES																																
HOLIDAYS																																
Veterans Day - Site Will Be Open																					X											
WEATHER																																
Rain Day (Including Heavy Winds)				X	X	X																										
MOCK UP																																
Install Masonry back up system			Fernandes																													
Install metal panel back up system			Riggs	X	X	X																										
Install Aluminum Windows			Chandler	X	X	X	X	X																								
SITE UTILITIES																																
Continual check in with Eversource for gas service			Eversource																													
Continual check in with Verizon on pole relocation			Verizon																													
Install drainage at south west side of building			Vinagro	X	X	X	X	X																								
FIELD WORK																																
Lay Sod	Pushed from 10-27 Due to Rain		Xquisite										X	X	X																	
Subgrade long jump lawn area			Vinagro	X	X	X	X	X																								
ATHLETIC FACILITY																																
Install Interior CMU Walls at Concession Stand & Bathrooms	PENDING COORDINATION AND TRUSS DESIGN		Fernandes																													
MEP Rough in CMU walls			MEP Trades																													
INTERIOR FITOUT/OH ROUGH																																
Building C																																
Install OH Duct - 1st floor			APEX	X																												
Plumbing Rough in Walls at Science rooms			Grasseschi	X	X																											
Insulate Plumbing Lines - 1st & 2nd Floor			Grasseschi	X	X	X	X	X																								
Touchup fire proofing			H. Carr																													
Install fire stopping			Gleason Powers	X	X																											
Inwall Inspections complete	Both floors		All Trades			X																										
Insulate and board walls	Both floors		Century				X	X	X		X	X	X	X	X		X	X	X													
Tape Walls	Both floors		Century														X	X	X	X	X					X	X	X	X	X		
Prime and first coat walls			King																							X	X	X	X	X		
Install wall tile			High Point																							X	X	X	X	X		
Install Ceiling grid			K&K																													
Frame hard ceiling			Century																							X	X	X	X	X		
Building D																																
Electrical/Fire Alarm/TelData Inwall Rough			Griffin	X	X	X	X	X			X	X	X	X	X		X	X	X	X	X				X	X						
Plumbing Rough in Walls			Grasseschi	X	X	X	X	X			X	X																				
Layout & Frame Interior Walls - 1st Floor	Remaining Walls		Century	X	X	X	X	X																								
Install ductwork - 1st Floor			Apex	X	X	X	X	X																								
Touchup fire proofing			H. Carr				X	X																								
Install fire stopping			Gleason Powers				X	X	X																							
Inwall Inspections complete	Second Floor		All Trades																							X	X	X				
Insulate and board walls	Second Floor		Century																							X	X	X	X	X		
Tape Walls	Second Floor		Century																									X	X	X		
Inwall Inspections complete	First Floor		All Trades																								X	X				
Insulate and board walls	First Floor		Century																													
Tape Walls	First Floor		Century																													
Building E																																
Install (2) Brace frames at Black Box	To be installed after auditorium slab has been prepped		Supermetal/GP East					X																								
Install Grease Traps at Kitchen			Grasseschi	X	X	X																										
Finish Fine Grading at Kitchen			Marois				X	X																								
Install Top Layer Mesh at SOG at radiant flooring			Riggs		X	X	X	X			X	X	X																			
Place Building E SOG at dining commons & radiant flooring			Riggs										X																			
Install Drywall Tops	2nd floor		Century	X	X	X	X	X																								
Plumbing Rough in Walls	2nd floor		Grasseschi	X	X	X	X	X			X	X	X	X	X		X	X	X													
Electrical/Fire Alarm/TelData Inwall Rough	2nd floor		Griffin	X	X	X	X	X			X	X	X	X	X		X	X	X	X	X				X	X						
Touchup fire proofing	2nd floor		H. Carr				X	X																		X	X					
Install fire stopping			Gleason Powers										X	X	X																	
Inwall Inspections complete	2nd floor		All Trades																									X				
Insulate and board walls	2nd floor		Century																										X	X		
Frame walls at first floor - after slabs			Century	X	X	X	X	X			X	X	X	X	X		X	X	X	X	X											
Install ductwork	1st floor		Apex			X	X	X			X	X	X	X	X		X	X	X	X	X				X	X	X	X	X			
Plumbing Rough in Walls	1st floor		Grasseschi																							X	X	X	X	X		

LOOK AHEAD SCHEDULE

10/25/2021

Description of Work	Notes	P6 Activity Code	Responsibility	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/7	11/8	11/9	11/10	11/11	11/12	11/13	11/14	11/15	11/16	11/17	11/18	11/19	11/20	11/21						
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S						
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S						
Electrical/Fire Alarm/TeiData Inwall Rough	1st floor		Griffin															X	X	X	X	X			X	X	X	X	X								
Inwall Inspections complete	2nd floor		All Trades																																		
Building F																																					
Place Stair 6 Treads			Riggs									X																									
Install Intumescent FP - GYM			H. Carr	X	X	X	X	X			X	X																									
Install OH Duct			NBK/APEX								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Install OH HVAC Pipe		A11120	NBK/APEX								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Install OH Plumbing		A11210	Grasseschi								X	X	X	X	X			X	X	X	X	X			X	X	X										
Install OH FP Rough		A11220	JCI								X	X	X	X	X																						
Install OH Electrical Rough		A11220	Griffin								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Frame Interior Walls -Gym & lobby		A11440	Century	X	X	X	X	X			X	X	X	X	X			X	X	X	X	X															
Install fire proofing at locker rooms and cont. ed.			H Carr	X	X	X	X	X			X	X																									
Frame hard ceilings in Locker rooms			Century																																		
Frame hard ceilings at running track			Century																																		
Building G																																					
Place Stair 2 Treads			Riggs									X																									
Prep and place slab at main lobby/back half of auditorium			Riggs								X	X	X	X	X			X	X	X																	
Prep and place black box theater slab			Riggs															X	X	X	X	X			X	X	X	X	X								
Install Stair 2 Rails			Berlin Steel															X	X																		
Install interior framing	1st floor		Century	X	X	X	X	X																													
Install OH Plumbing rough			Grasseschi				X	X			X	X	X	X	X			X	X	X	X	X			X	X	X										
Install OH FP rough			JCI			X	X	X			X	X	X	X	X										X	X	X										
Install OH Electrical Rough			Griffin								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Building G - Auditorium																																					
Prep for slab in auditorium			Marois	X	X	X	X	X																													
Install Waterproofing membrane underslab at auditorium			Superior				X	X			X	X																									
Install Vapor Barrier/Mesh at Stage			Riggs									X	X	X	X																						
Install floor boxes in auditorium			Griffin								X	X	X	X	X																						
Place slab at Auditorium Stage			Riggs																																		
Place slab at Auditorium			Riggs																																		
Install Dancefloor in Auditorium			Consigli																																		
Install OH FP Rough			JCI																																		
Install OH plumbing			Grasseschi																																		
Install OH ductwork			Apex																																		
Building A																																					
Frame interior walls			Century																																		
Install OH MEP rough post coordination			MEP Trades															X	X	X	X	X			X	X	X	X	X								
Building B																																					
Install spray fire proofing at roof structure			H Carr																																		
Frame interior walls			Century	X	X	X	X	X																													
Install OH MEP rough post coordination			MEP Trades																																		
ROOFING & FAÇADE WORK																																					
Building C																																					
Install AVB at Façade - (South - East)			Armani	X	X	X	X																														
Install AVB at clerestory			Armani								X	X	X	X	X																						
Install metal panel back up system			Riggs								X	X	X	X	X			X	X	X	X	X															
Wash Brick			Fernandes																										X	X							
Building D																																					
Frame/Sheath/Block Exterior walls			Century	X	X	X																															
Install AVB			Armani			X	X	X			X	X	X																								
Install Brick on remaining exterior walls - west elevation			Fernandes								X	X	X	X	X																						
Install Skylight			Chandler Architectural																						X	X	X										
Install metal panel back up system			Riggs																						X	X	X	X	X								
Building E																																					
Temp in CW 20 - café			Commonwealth															X	X	X	X	X															
Frame/Sheath/Block Remaining Exterior walls			Century	X	X	X																															
Install Brick Façade at High Roofs	West Elevation		Fernandes	X	X	X	X	X			X	X	X	X	X																						
Install AVB at CMU exterior walls - post roof install			Armani	X	X	X	X	X																													
Install Brick Façade at CMU exterior walls			Fernandes								X	X	X	X	X			X	X	X	X	X															
Install Windows at West Side			Chandler Architectural																						X	X	X	X	X								
Install Skylights			Chandler Architectural																																		
Building F																																					
Install roof protection			Riggs/Capeway	X	X	X	X																														
Install Brick Façade at High Roofs	North & West Elevation		Fernandes	X	X	X	X	X			X	X	X	X	X			X	X	X																	
Install AVB at CMU exterior walls - post roof install			Armani	X	X	X	X	X																													
Install Brick Façade at CMU exterior walls			Fernandes								X	X	X	X	X			X	X	X	X	X															
Install Windows at North & West Side			Chandler Architectural																						X	X	X	X	X								
Install Skylight - Main Lobby			Chandler Architectural															X	X	X	X	X			X	X	X	X	X								

LOOK AHEAD SCHEDULE

10/25/2021

Description of Work	Notes	P6 Activity Code	Responsibility	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/7	11/8	11/9	11/10	11/11	11/12	11/13	11/14	11/15	11/16	11/17	11/18	11/19	11/20	11/21		
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S		
				Building G - North																													
Frame CW opening at Stair 1			Century	X	X	X																											
Install AVB at window blocking and sheathing north elevation			Armani	X	X	X	X	X			X	X	X	X	X																		
Install Masonry façade			Fernandes														X	X	X	X	X			X	X	X	X	X					
Install metal panel back up system			Riggs																														
Install low roof roofing membrane			Capeway																						X	X	X	X	X				
Building G - Auditorium																																	
AVB remedial work at columns			Armani	X	X	X																											
Install Masonry Façade			Fernandes	X	X	X	X	X			X	X	X	X	X																		
Building A																																	
Install sheathing on south elevation			Century																														
Install window blocking			Century	X	X	X																											
Install AVB at window blocking and sheathing			Armani				X	X			X	X	X	X	X																		
Install Masonry Façade			Fernandes														X	X	X	X	X			X	X	X	X	X					
Building B																																	
Install Roofing at slope and low roof	Pushed from 10-25 due to rain		Capeway				X	X			X	X	X	X	X																		
Install exterior framing and sheathing			Century	X	X	X	X	X																									
Install window blocking			Century	X	X	X	X	X			X	X	X	X	X																		
Install AVB at window blocking and sheathing			Armani														X	X	X	X	X			X	X	X	X	X					
Install Masonry Façade			Fernandes																					X	X	X	X	X					



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
