

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule

- Over the last week the project hit two milestones. The roof is now weather tight & our last interior slab placement is complete.
- Skylight installation is planned for the coming weeks.
- Major mechanical equipment (RTU's etc.) is stored locally and scheduled for installation over the coming weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. This includes increased wire pulling efforts.
- Interior light gauge metal framing are ongoing at multiple areas. In wall inspections are ongoing. Wall close-in is ongoing. Drywall finishing has started.
- Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing. Installation of exterior panel is on the radar.
- Temporary heaters are running. See enclosed notice for details- this will enable temperature sensitive interior work such as drywall taping & other finish activities to begin.
- Windows are beginning to arrive on-site. Mockup installation & testing upcoming.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of  
**SHARON**  
Massachusetts



**PMA Consultants**




**TAPPÉ  
ARCHITECTS**



# Sharon High School



## LOGISTICS UPDATE November 30, 2021

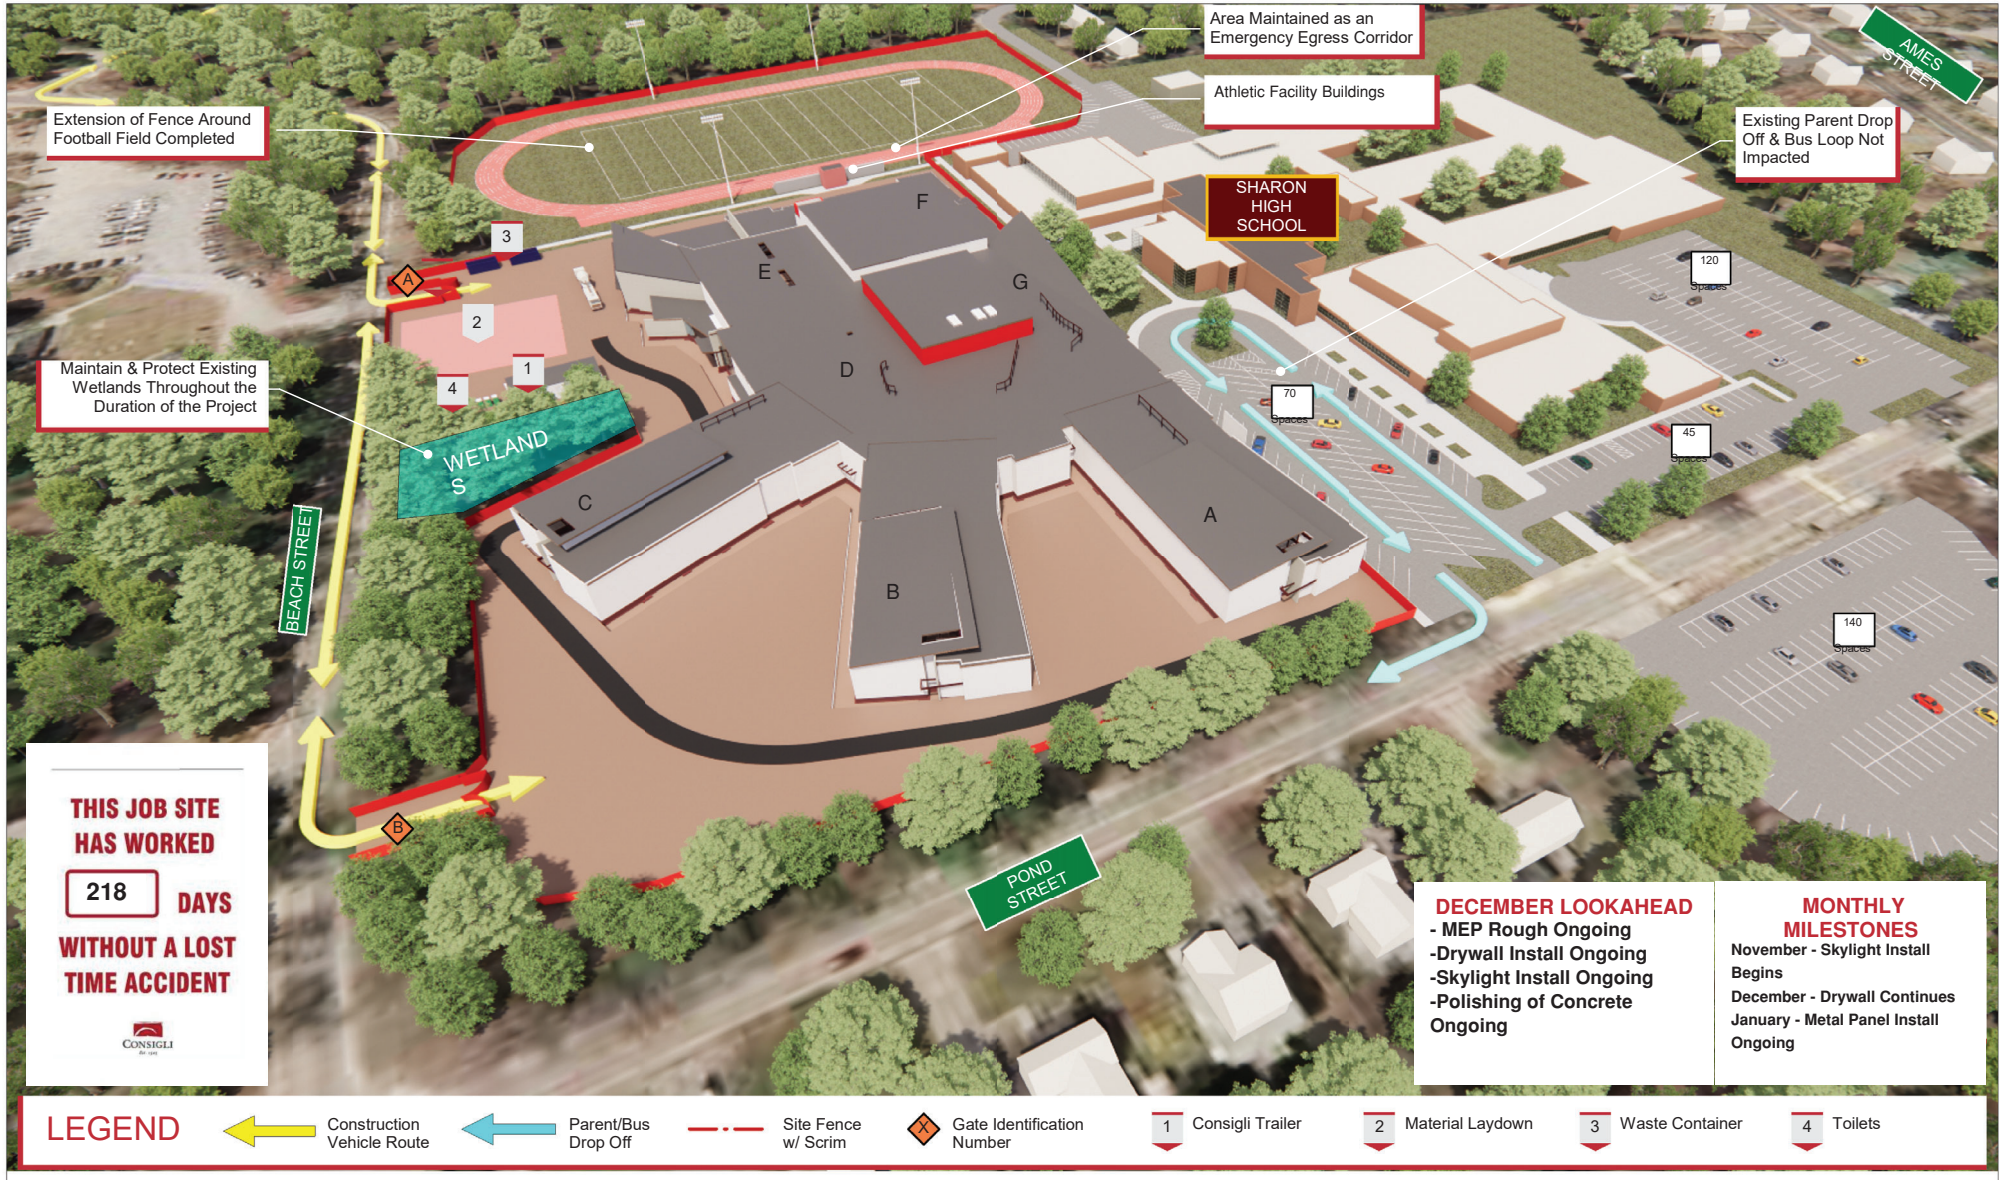

Extension of Fence Around Football Field Completed

Area Maintained as an Emergency Egress Corridor

Athletic Facility Buildings

Existing Parent Drop Off & Bus Loop Not Impacted

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

WETLAND S

SHARON HIGH SCHOOL

**THIS JOB SITE HAS WORKED**  
**218 DAYS**  
**WITHOUT A LOST TIME ACCIDENT**



**DECEMBER LOOKAHEAD**  
- MEP Rough Ongoing  
- Drywall Install Ongoing  
- Skylight Install Ongoing  
- Polishing of Concrete Ongoing

**MONTHLY MILESTONES**  
November - Skylight Install Begins  
December - Drywall Continues  
January - Metal Panel Install Ongoing

### LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets









**Sharon High School: Notice of Ongoing Winter Heating**

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

*Matthew Gulino*

Matthew Gulino  
Associate | Owner's Project Manager  
PMA Consultants  
[mgulino@pmaconsultants.com](mailto:mgulino@pmaconsultants.com)
