The Sharon High School Construction Project

4 Week Look Ahead Schedule

- Temporary heaters are running. See enclosed notice- this allows temperature sensitive interior work to begin.
- Installation of helical piles (to support the press box) is scheduled to begin next week.
- Major mechanical equipment (RTU's etc.) is stored locally and scheduled for installation over the coming weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. This includes increased wire pulling efforts.
- Interior light gauge metal framing are ongoing at multiple areas. In wall inspections are ongoing. Wall close-in is ongoing. Drywall finishing is ongoing.
- Paint & tile subcontractors have begun. Ceiling grid installation is upcoming.
- Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing. Installation of exterior panel is on the radar.
- Skylight installation is ongoing.
- Mock-up installation is ongoing- window testing is scheduled for early January. Window installation will follow.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/ Town of

SHARON












Sharon High School



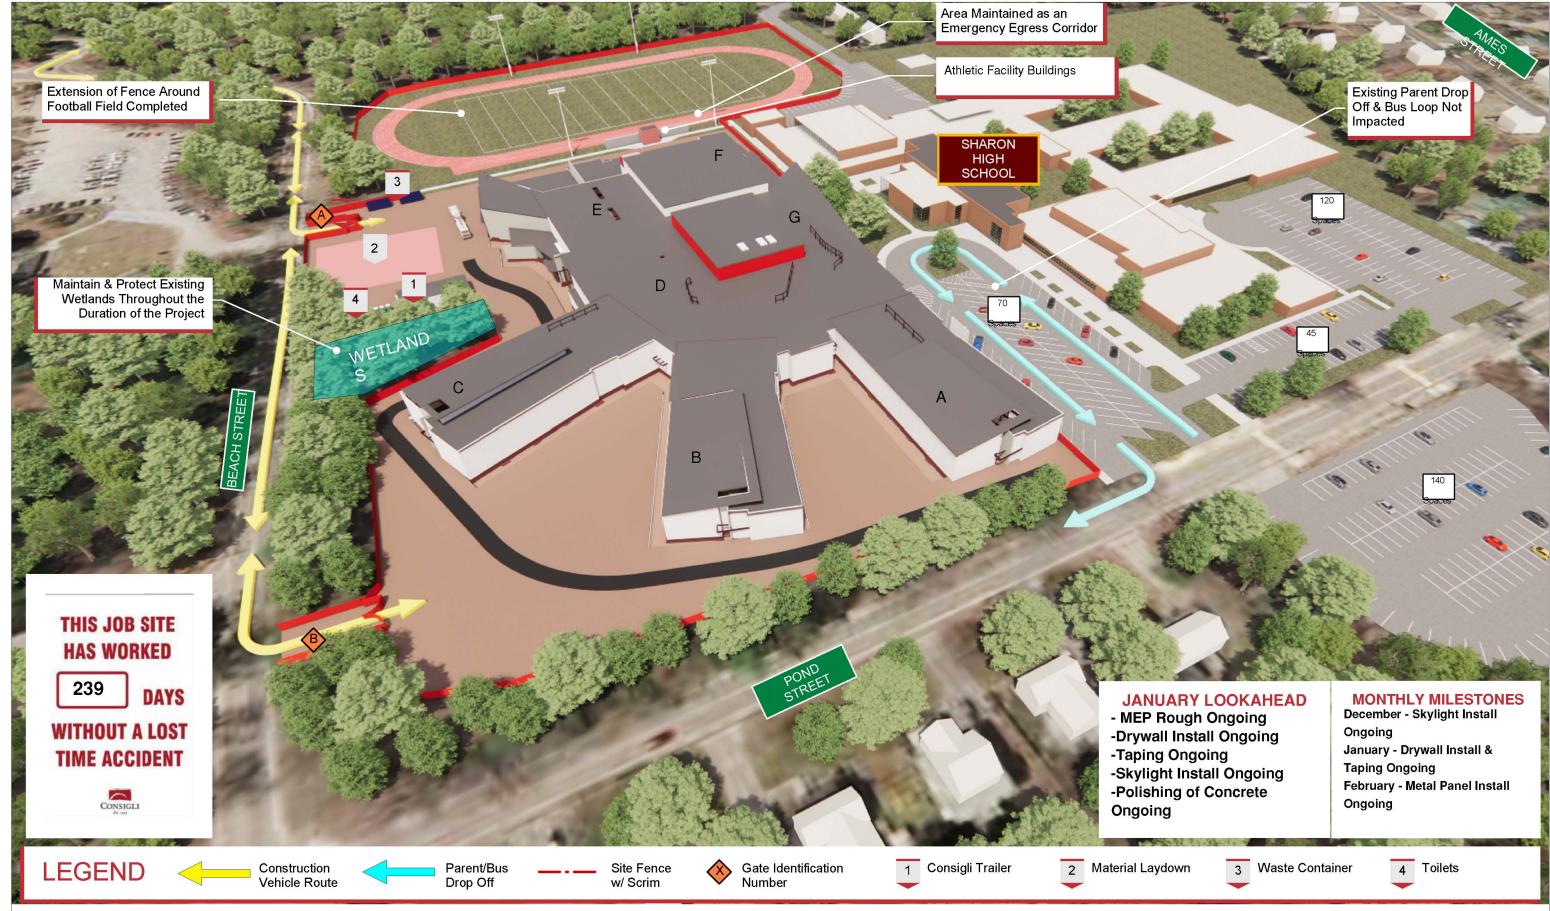

LOGISTICS UPDATE December 21, 2021

		LOOK AHEAD SCH	EDULE 12/20/2021																				
Description of Work	Notes	P6 Activity % Code Comp	Responsibility					12/25 12/26 S S							1/4 1/ T V		1/6 1/7 FR FR		1/10 M	1/11 T		/13 1/14 FR FR	1/15 1/16 S S
SCHOOL SCHEDULE MILESTONES HOLIDAYS																							
Christmas Eve - Site Open							Х					Х											
Christmas Day							~	Х					Х										
New Years Eve - Site Open																							
New Years Day																							
WEATHER MOCK UP																							
Install metal panel back up system and insulation			Riggs	XX	X X	Х	Х		Х	Х	Х												
Window Testing			Consigli/PMA											Х	Х								
SITE UTILITIES																							
Continual check in with Eversource for gas service			Eversource																				
FOOTBALL FIELD Prep subgrade at Pressbox for helical pile drilling			Vinagro			Х	Х		Х	Х	X	X X											
Helical Pile Drilling			Vinagro			^	^		^	^	^	^ ^		X	x >	<u>, </u>	x x						
																•							
Install Interior CMU Walls at Concession Stand & Bathrooms			Fernandes						Х	Х	Х	х х		Х	х	(x x						
MEP Rough in CMU walls	PENDING COORDINATION AND TRUSS DESIGN		MEP Trades																				
Instal Vapor Barrier & Mesh			Riggs																				
Place Slabs			Riggs																				
INTERIOR FITOUT/OH ROUGH																							
Building C																							
Tape Walls Prime and first coat walls	Both Floors		Century	X >	K X	Х	Х		Х	Х	Х	X X		X			X X		X	X		X X	
Install wall tile	Second Floor Second Floor		King High Point	X Y	< X	Y	Y		х	Y	Y	X X X		XX	X X X		X X X X		Х	Х	Х	X X	
Install Ceiling grid	Second Floor		K&K			^	^		^	^	^	^ ^		^	~ /		^ ^						
Frame hard ceiling	Both Floors		Century																				
Prime and first coat walls	First Floor		King																Х	Х	Х	х х	
Install wall tile	First Floor		High Point																				
Install Ceiling grid	First Floor		K&K																				
Building D	Second Floor - Science																						
Insulate and board walls	Classrooms		Century	X X	<																		
Tape Walls	Second Floor - Science Classrooms		Century						х	х													
Insulate and board walls	Second Floor		Century	XX	X X	Х	Х		Х	Х	Х												
Tape Walls	Second Floor		Century								Х	X X		Х	X >	(X X		Х	Х	Х	х х	
Electrical/Fire Alarm/TelData Inwall Rough	First Floor		Griffin	X >	K X	Х			V														
Inwall Inspections complete Insulate and board walls	First Floor First Floor		All Trades Century						X	Y	Y	x x		x	Y N		x x		X	Х	Y		
Tape Walls	First Floor		Century						^	^	^	^ ^					~ ^		X		X	x x	
Install Ceiling Grid	Start : Jan 17 2022		K&K																	~			
Polish Concrete on 2nd floor around stair 3 opening			Kaloutas																Х	Х	Х	х х	
Building E																							
Electrical/Fire Alarm/TelData Inwall Rough	Second Floor		Griffin		X X																		
Touchup fire proofing	Second Floor		H. Carr	X >	X X																		
Inwall Inspections complete Insulate and board walls	Second Floor Second Floor		All Trades Century		Х	x	х		x	x	x	x x		X	x								
Tape Walls	Second Floor		Century			~	^		^	^	~	<u>^ ^</u>				<u>(</u>	X X		X	Х	x	x x	
Install Stair 5			Berlin Steel						Х	Х	Х	X X			X X								
Place Stair Treads - Stair 5			Riggs														Х						
Install ductwork -Kitchen	First Floor		Apex		,		.,			.,													
Install ductwork -Wellness & Weight room area	First Floor		Apex		X X	X	X		X	X	X	X X											
Electrical/Fire Alarm/TelData Inwall Rough Inwall Inspections complete	First Floor First Floor		Griffin All Trades		X X	X	٨		Х	Х	Х	X X		X									
Insulate and board walls	First Floor		Century												x >	<u>(</u>	x x						
Install Ceiling Grid	Start : Jan 24 2022		K&K																				
Building F - North																							
Install OH Duct			Apex	X	< X	Х	Х		Х	Х	Х	ХХ		Х	X >	(х х						
Install Electrical Rough			Griffin						Х	Х	Х	ХХ											

		LOOK AHEA		DULE /20/2021																							
Description of Work	Notes	P6 Activity Code	% Comp	<u>Responsibility</u>	12/20 M		12/22 12/2 W TF	/23 12/24 R FR	12/26 S	12/27 M						1/3 1/ M T		1/5 W	1/6 TR		1/8 1/9 S S		1/11 T	1/12 W			15 1/16 S S
Frame hard ceilings in Locker rooms				Century																							
Polish Concrete in Main Lobby				Kaloutas												ХУ	Х	Х	Х	Х		X	Х	Х	Х	Х	
Building F - GYM																											
Install Intumescent FP - GYM Install Electrical Rough				H. Carr Griffin	X	Х	X X	ζ		v	v	X	v	V													
Install OH Ductwork Hangers				Apex				(X		X	X	X	X	X													
Install OH Ductwork	Delivery week of 1-28-22			Apex						~	~	~	~	~													
Frame hard ceilings at running track				Century																							
Install Gym Elevated Track Rails				Berlin Steel																							
Paint Gym Trusses				King Painting																							
Building F - Lockerooms Install OH Ductwork				APEX			X X			V	v	X	V	V		X X	v	V	V	V		×	v	v	X	V	
Install Electrical Rough				Griffin						X	X	X	X	X		<u> </u>	^	^	^	^		^	^	^	^	^	
Building G																											
Install Stair 2 Rails				Berlin Steel																							
Install interior framing	2nd Floor			Century	Х	Х	X X	< X															1				
Install OH Plumbing rough	2nd Floor			Grasseschi	Х	Х	X X	X X		Х	Х	Х	Х	Х		ХУ	X	Х	X	Х		Х	Х	Х	Х	Х	
Install OH Ductwork Install OH HVAC Pipe	2nd Floor 1st floor			Apex NBK	Y	Y	x x			Y	Y	X	x	X		хх	x	x	x	x		v	Y	Y	Х	X	
Install OH Duct Hangers	1st floor			Apex	^	^				^	^	^	^	^		~ ^	^	^	^	^		^	^	^	^	^	
Install OH Ductwork				Apex	Х	Х	X X	(X		Х	Х	Х	Х	Х		X X	х	Х	Х	Х							
Install OH FP rough	2nd Floor			ĴĊI	Х	Х	ХХ	< X																			
Install OH Electrical Rough	Not incl. wire			Griffin																							
Building G - Auditorium																	v	V	V	V							
Install OH FP Rough Install OH plumbing				JCI Grasseschi	X	Y								_		,	X	X	Х	X							
Install OH HVAC Pipe				NBK	~	~				Х	Х	х	Х	Х	 	X X	x	Х	Х	Х		Х	Х	Х	Х	x	
Install OH ductwork				Apex														X		X		X	X	X		X	
Install OH Electrical Rough				Griffin																							
Install Auditorium Rails				Berlin Steel																							
Building G - Black Box Install OH plumbing				Grasseschi	V	V	X			V	v	X	V	V													
Install OH HVAC Pipe				NBK	X	X	X X X X			X	X	X		X													
Install OH ductwork				Apex	~	~					~	~~	~	~													
Electrical/Fire Alarm/TelData Inwall Rough				Griffin																							
Building A	0.14			NDV	X	X																					
Install OH HVAC Pipe Install OH FP Rough	2nd floor 1st floor			NBK JCI	X	X X	X X X X			x	X	X	X	x						_							
Install OH HVAC Pipe	1st floor			NBK			X X					X				X X	x	Х	х	Х							
Polish Concrete	1st floor			Kaloutas	Х	Х	ХХ	< X																			
Polish Concrete	2nd floor			Kaloutas						Х	Х	Х	Х	Х													
Building B Frame interior walls	2nd floor			Century																							
Install OH MEP rough post coordination	2110 11001			MEP Trades																							
ROOFING & FAÇADE WORK																											
Building C																											
Install Windows on 1st Floor	Delivery Jan 3			Chandler Architectural																_		X	Х	Х	Х	X	
Install Windows on 2nd Floor Building D			, c	Chandler Architectural																							
Install Brick on remaining exterior walls - west elevation				Fernandes	Х	Х																					
Wash Brick				Fernandes	~	~	Х																				
Install Skylight			C	Chandler Architectural	Х																						
Building E																											
Set Curbs for Rooftop Units				NBK/APEX							Х																
Flash Roofing Membrane to Curbs				Capeway						Х	Х																
Set Rooftop Units	Date TBD			NBK/APEX																							
Building F																											
Install Skylight - Main Lobby			C	Chandler Architectural	+					Х		Х	Х	Х		X X	x	Х	Х	Х		Х	Х	Х	Х	Х	
Set Curbs for Rooftop Units				NBK/APEX	+					Х	Х																
Flash Roofing Membrane to Curbs				Capeway						Х	Х																
Set Rooftop Units	Date TBD			NBK/APEX																							

	LOOK AHEAD SCHEDULE																													
Description of Work	Notes	P6 Activity	%	Responsibility			12/22 1													1/5		1/7	1/8 1/9				1/13 1			
		Code	Comp		М	Т	W	TR F	FR S	5 9	s	М	тν	V TR	FR	S	S	M	Т	W	TR	FR	S S	М	Т	W	TR	FR	S	S
Install Masonry Façade	North Elevation			Fernandes	Х	Х	Х																							
Wash Brick	North Elevation			Fernandes			Х																					1		
Building G - North																												7		
Install AVB at window blocking and sheathing north elevation				Armani	Х	Х	Х	X	Х			Х	X X	(X	Х			Х	Х	Х	Х	Х							1	
Install Masonry façade				Fernandes																								1		
Wash Brick				Fernandes																								1		
Building A																														
Install AVB at window blocking and sheathing for Masonry Install				Armani	х	Х	х																							
Install Masonry Façade				Fernandes								Х	X X	(X	Х			Х	Х	Х	Х	Х		X	Х	Х	Х	Х	1	
Wash Brick				Fernandes																										
Building B																											1	7		
Install AVB at window blocking and sheathing for Masonry Install				Armani	х	х																								
Install Masonry Façade				Fernandes	Х	Х	Х	X	Х			Х	X X	(X	Х															
Wash Brick				Fernandes											Х						-									



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at https://www.shsbuilding.com/

Best Regards,

Matthew Gulino

Matthew Gulino Associate | Owner's Project Manager PMA Consultants mgulino@pmaconsultants.com
