

The Sharon High School Construction Project




4 Week Look Ahead Schedule 01/11/2021

- Upcoming Activities Include:
 - Excavate & prep for building foundations
 - Install rebar for building foundations
 - Place concrete for building foundations
 - See attached progress update ****New****
 - See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information:
<https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



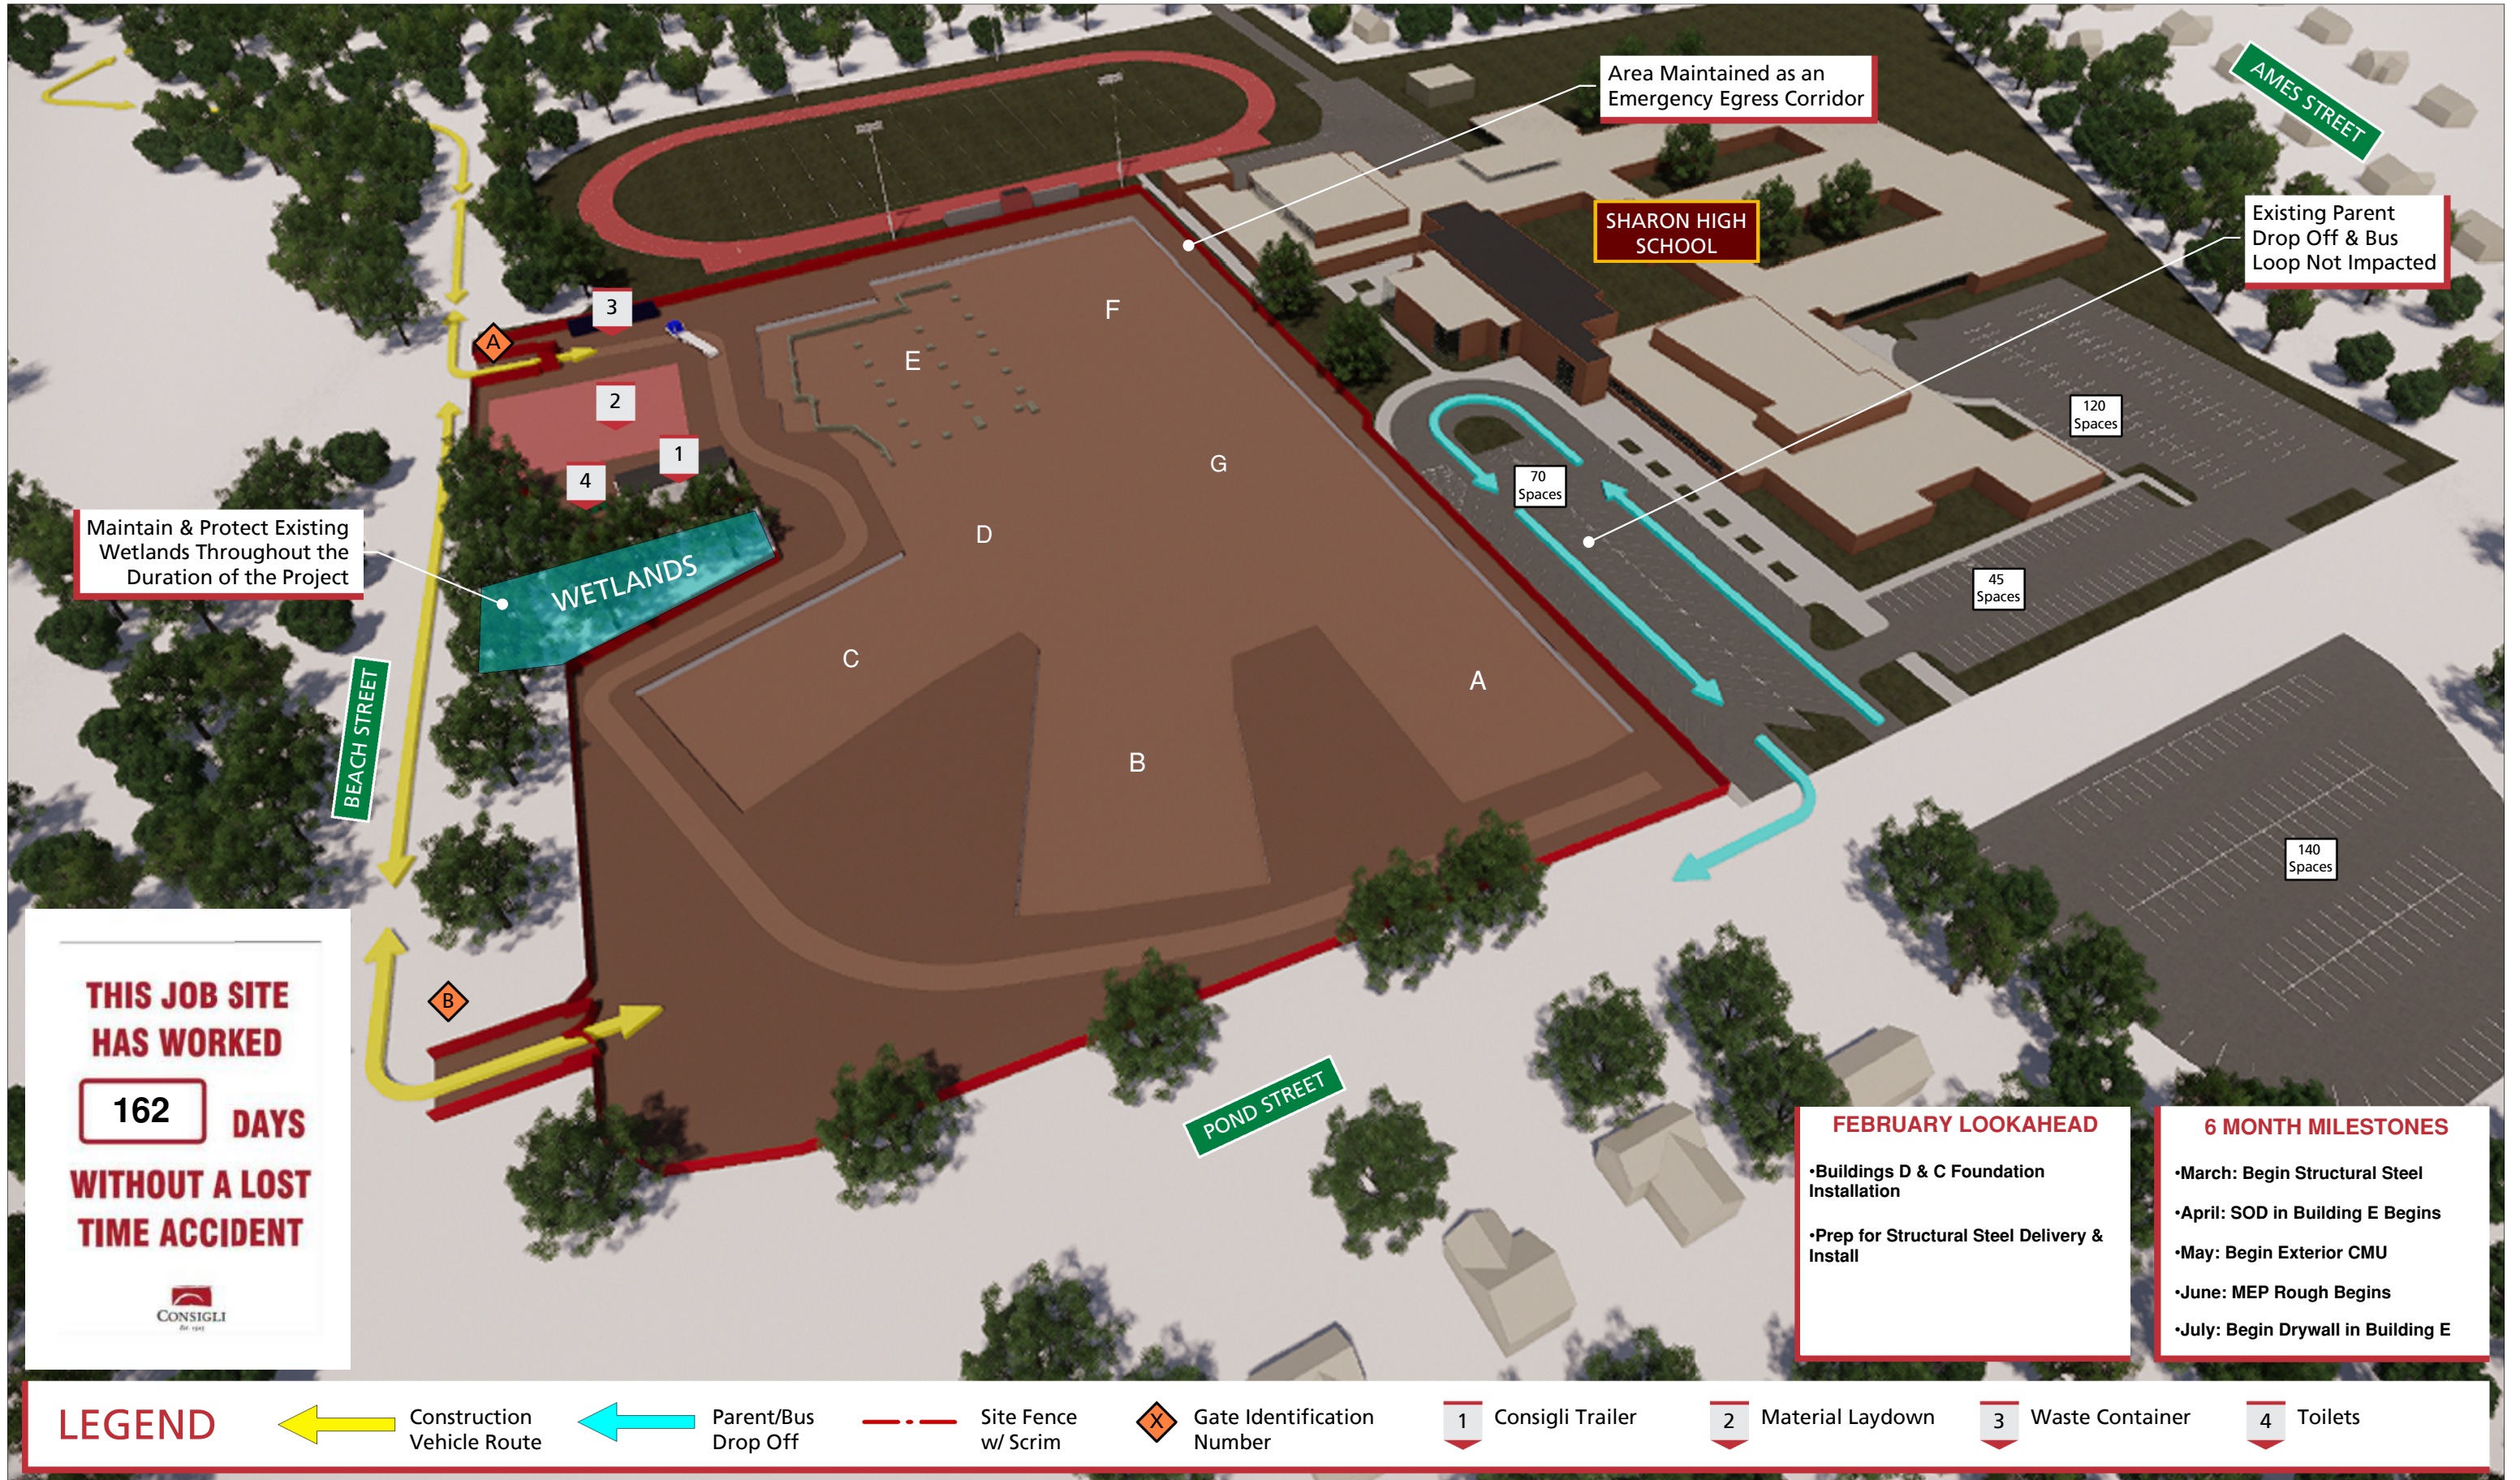

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

Area Maintained as an Emergency Egress Corridor

Existing Parent Drop Off & Bus Loop Not Impacted

THIS JOB SITE HAS WORKED
162 DAYS
WITHOUT A LOST TIME ACCIDENT



FEBRUARY LOOKAHEAD

- Buildings D & C Foundation Installation
- Prep for Structural Steel Delivery & Install

6 MONTH MILESTONES

- March: Begin Structural Steel
- April: SOD in Building E Begins
- May: Begin Exterior CMU
- June: MEP Rough Begins
- July: Begin Drywall in Building E

LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- Consigli Trailer
- Material Laydown
- Waste Container
- Toilets

LOOK AHEAD SCHEDULE
Date Updated: 1-11-21

Description of Work	Responsibility	1/11	1/12	1/13	1/14	1/15	1/16	1/17	1/18	1/19	1/20	1/21	1/22	1/23	1/24	1/25	1/26	1/27	1/28	1/29	1/30	1/31	2/1	2/2	2/3	2/4	2/5	2/6	2/7
		M	T	W	TR	F	S	S	M	T	W	TR	F	S	S	M	M	T	W	TR	F	S	S	M	T	W	TR	S	S
SCHOOL SCHEDULE																													
Students onsite in school session	SHARON HS	X	X		X	X				X		X	X			X	X		X	X			X	X		X	X		
Fully remote day	SHARON HS			X							X							X							X				
Early Release Day	SHARON HS																												
School Vacation Day	SHARON HS								X																				
MILESTONES																													
RAPS Complete - December 18th 2020	Marois																												
Steel Erection Start Date - Mobilization/Delivery - March 15th 2020	Supermetal																												
HOLIDAYS																													
Martin Luther King Day - January 18th, 2021									X																				
WEATHER																													
SITWORK																													
SITE UTILITIES																													
Excavate/Backfill electrical ductbank	Marois																						X	X	X	X	X		
Install electrical ductbank	MAK																						X	X	X	X	X		
Install drainage and associated piping	Marois																						X	X	X	X	X		
Begin design work for gas main to new building	Columbia								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
BUILDING FOUNDATION																													
Dewatering	Marois	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X	X
Install Foundations for Building E	Riggs	X	X	X	X	X			X	X	X	X	X			X	X	X											
Install Damproofing on E Building Foundations Walls	Superior															X	X	X	X	X			X	X	X	X	X		
Backfill foundations Building D	Marois					X			X	X	X												X	X	X	X	X		
Excavate for foundations Building D	Marois	X	X	X	X	X			X	X	X	X	X																
Install Foundations for Building D	Riggs								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X		
Install Foundations for Building C	Riggs																						X	X	X	X	X		
