

The Sharon High School Construction Project




4 Week Look Ahead Schedule 02/15/2021

- Upcoming Activities Include:
 - Excavate & prep for building foundations
 - Install rebar & place concrete for building foundations
 - Waterproof foundations & ejector pit
 - Backfill foundations
 - Structural steel begins in March
 - See attached progress update
 - See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information:
<https://www.shsbuiding.com/>

Town of
SHARON
Massachusetts



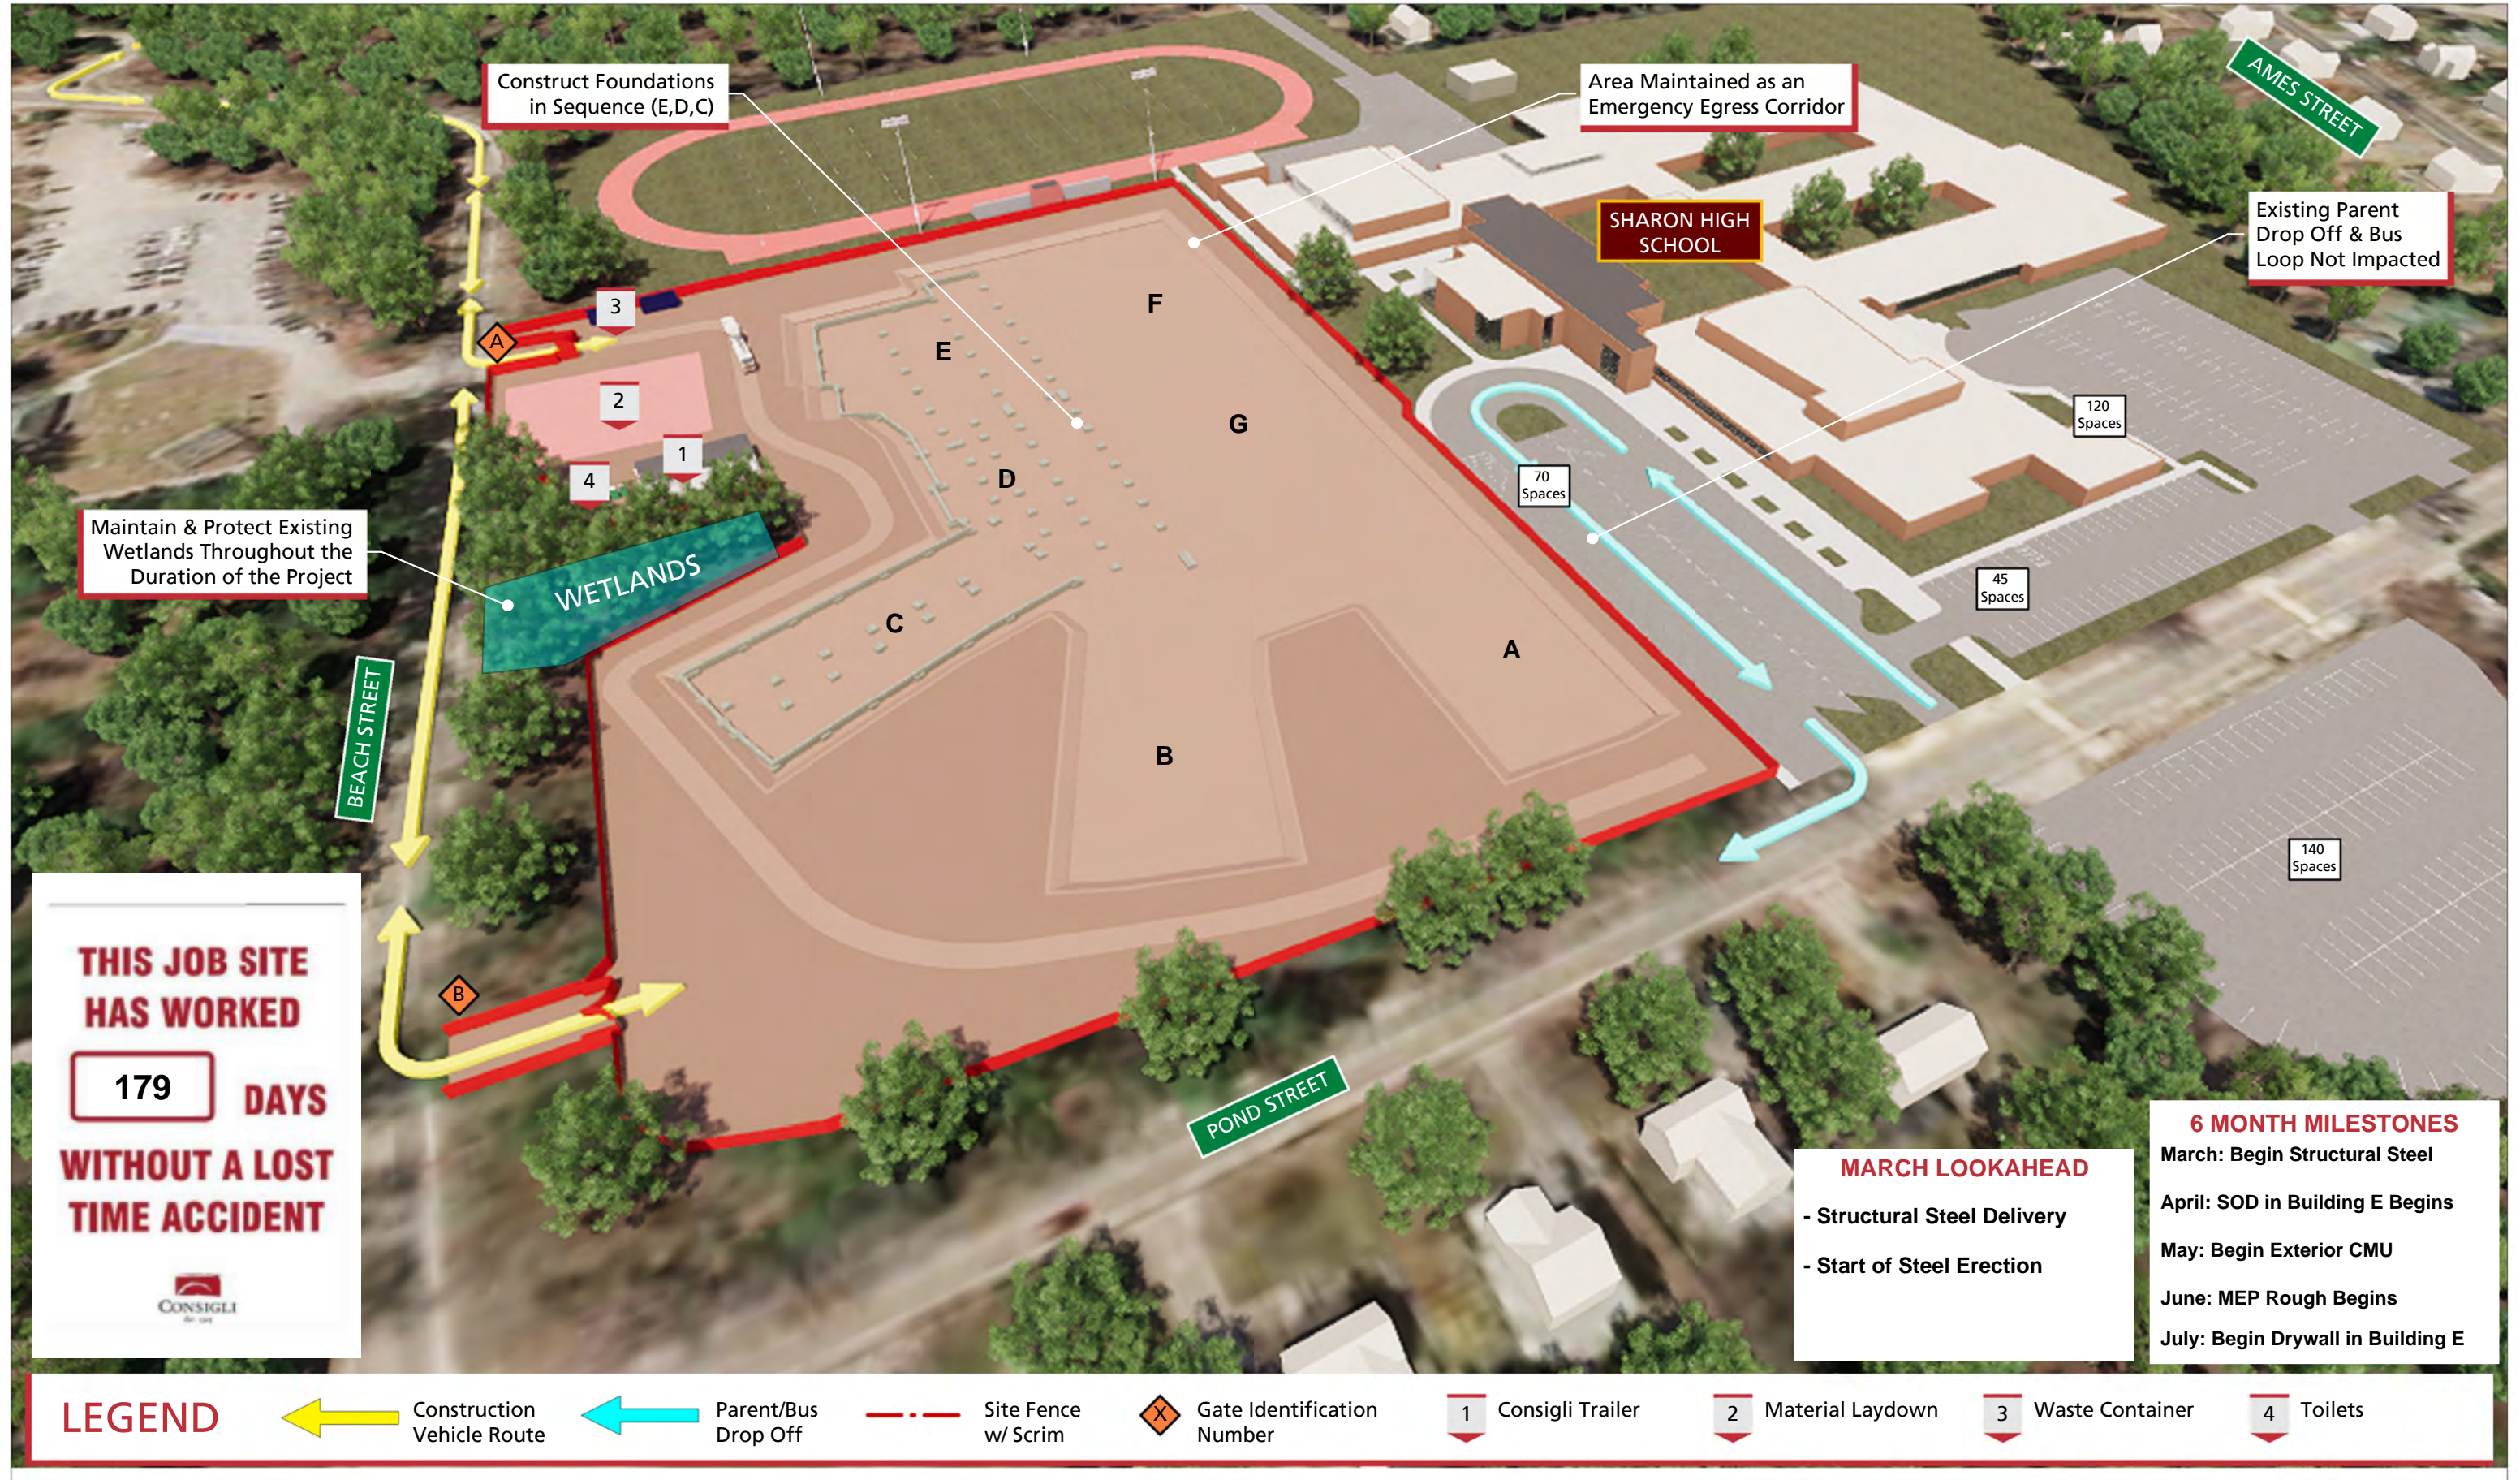

**THIS JOB SITE
HAS WORKED
179 DAYS
WITHOUT A LOST
TIME ACCIDENT**



MARCH LOOKAHEAD

- Structural Steel Delivery
- Start of Steel Erection

6 MONTH MILESTONES

- March: Begin Structural Steel
- April: SOD in Building E Begins
- May: Begin Exterior CMU
- June: MEP Rough Begins
- July: Begin Drywall in Building E

LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- Consigli Trailer
- Material Laydown
- Waste Container
- Toilets

