

4 Week Look Ahead Schedule 03/01/2021

- Upcoming Activities Include:
 - o Prep & place building foundations
 - Dampproof, insulate & backfill foundations
 - o Install elec. ductbank, water & fire services
 - O Structural steel begins in mid to late March
 - See attached progress update
 - See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/












Sharon High School



SHARON HS PROGRESS UPDATE MARCH 2021

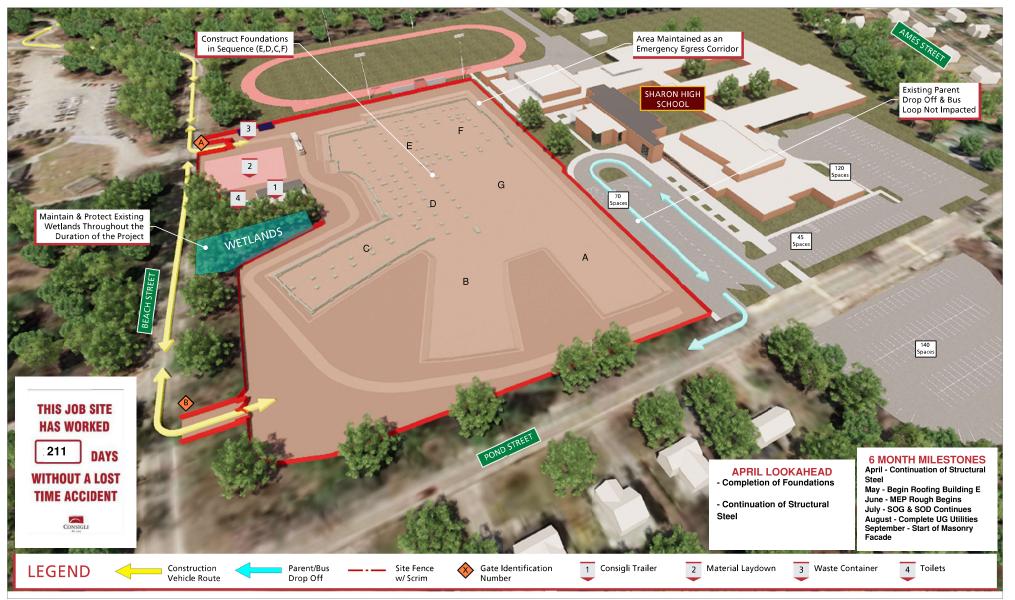

	II.	LOOK AHEAD SCHEDULE 3/1/2021																												
Description of Work Notes	P6 Activity Code	Responsibility	3/1 M	3/2 T	3/3 W	3/4 TR	3/5 TR	3/6	3/7 S	3/8 M	3/9 T		3/11 TR		3/13	3/14 S	3/15 M	3/16 T	3/17 W	3/18 TR	3/19 TR	3/20	3/21 S	3/22 M	3/23 T	3/24 W		3/26 TR		3/28 S
SCHOOL SCHEDULE																														
Students onsite in school session		SHARON HS	Х	Χ		Χ	Χ			Χ	Χ		Χ	Χ			Χ	Χ		Χ	Х			Х	Χ		Χ	Χ		
Fully remote day		SHARON HS			Χ							Χ							Χ							Χ				
Early Release Day MILESTONES		SHARON HS																												
Steel Erection Start Date - Mobilization/Delivery - March 15th 2020 HOLIDAYS		Supermetal															х													
WEATHER																														
SITEWORK																														
SITEWORK SITE UTILITIES																														
Excavate/Backfill electrical ductbank - Post foundation Backfilling - Pending Weather	A9670	Marois								Х	Х	Х	Х	Х			Х	Х	Х	Х	Х			Х	Х	Х	Х	Х		
Install electrical ductbank - Post foundation backfilling pending weather	A9670	MAK								Х	Х	Х	Х	Х			Х	Х	Х	Х	Х			Х	Х	Х	Χ	Х		
Install drainage and associated piping - Post Backfilling	A9660	Marois								Х	Х	Х	Х	Х			Х	Х	Х	Х	Х			Х	Х	Х	Х	Х		
Install Domestic Water Service Into building		Marois											Χ	Х			Χ	Χ	Χ					Х	Х	Χ				
Install Fire Service Service Into building		Marois											Χ				Χ	Χ	Χ					Х	Χ	Χ				
Begin design work for gas main to new building		Columbia	Х	Χ	Χ	Χ	Х			Х	Х	Х	Χ	Х			Х	Χ	Χ	Χ	Х			Х	Χ	Χ	Х	Х		
BUILDING FOUNDATION Dewatering		Marois	Х	X	V	Х	Х	V	V	V	X	V	X	V	Х	V	Х	X	Х	V	Х	V	X	V	X	X	Х	Х	Х	X
Building E		IVIALUIS	^	^	^	^	^	Х	Х	^	^	^	^	^	^	Х	^	^	^	Х	^	X	^	Х	^	^	^		^	^
Install Waterproofing on E Building Ejector Pit	A10700	Superior				Х																								
Backfill foundations Building E and prep for footings at	71.0.00	Marois		Х	Х	Х	Х																							
K Line				^	^																									
Install remaining footings on K Line		Riggs				Χ	X			Χ	Х																			
Building D Install Damproofing on D Building Foundations Walls	A10670	Superior				Х																								
Backfill foundations Building D	A10070	Marois				^				Х	Х	Х																		
Building C		IVIAI OIS								^	^	^																		
Backfill foundations (footings) Building C		Marois																												
Install Damproofing on C Building Foundations Walls	A10660	Superior											Χ	Х			Χ	Χ												
Backfill foundations (walls) Building C		Marois															Χ	Χ	Χ	Χ	Χ			Х						
Building F																														
Install Foundations (footings) for Building F	A9020	Riggs	Х	Х	Х	Х	Х			Х	Х	Х	Х	х																
Backfill foundations (footings) Building F		Marois	Х	X	Χ		Х																							
Install Foundation Walls for Building F	A9020	Riggs								Χ	Х	Χ	Х	Х			Χ	Χ												
Install Damproofing on F Building Foundations Walls	A10660	Superior																									Х	Х		
Building A	10222		,,,		.,																									
Excavate foundations Building A	A8820	Marois	Х	Χ	Х	Χ	Χ																					-		
Install Foundations (footings) for Building A	A9020	Riggs	Х	Χ	Χ	Χ	Х			Χ	Х	Χ	Х	Х																
Backfill foundations (footings) Building A		Marois	Х	Χ	Χ	Χ	Χ																							
Install Foundation Walls for Building A	A9020	Riggs															Х	Χ	Χ	Χ	X			Х	Х					
