

4 Week Look Ahead Schedule 03/29/2021

- Upcoming Activities Include:
 - O Structural steel erection has started & deliveries are ongoing
 - O Continue underground utilities (both site and within building)
 - O Prep, place, dampproof & insulate foundations is ongoing but nearing completion
 - See attached progress update
 - See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/












Sharon High School



SHARON HS PROGRESS UPDATE APRIL 2021

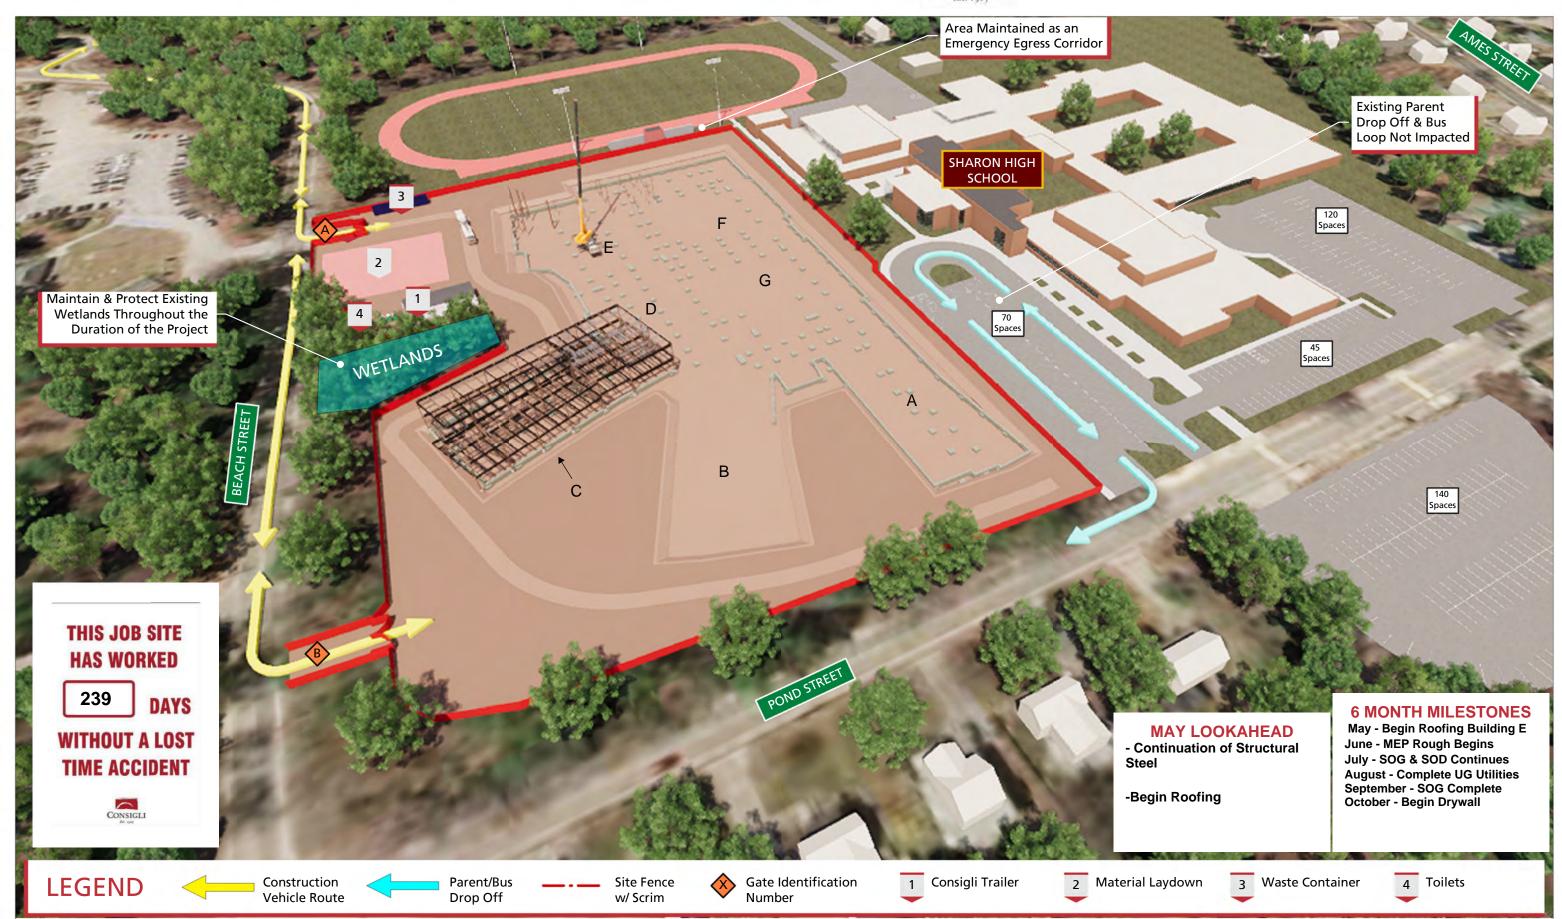

	LOOK AHEAD SCHEDULE 3/22/2021																														
Description of Work	Notes	P6 Activity Code	Responsibility	3/29 M	3/30 T			4/2 TR	4/3	4/4 S	4/5 M	4/6 T	4/7 W	4/8 TR	4/9 TR	4/10	4/11 S	4/12 M	4/13 T	4/14 W	4/15 TR	4/16 TR	4/17	4/18 S	4/19 M	4/20 T	4/21 W	4/22 TR	4/23 TR	4/24	4/25 S
SCHOOL SCHEDULE								111	·											,,,	110								111		
Students onsite in school session			SHARON HS	Х	Х		Х	Х			Х	Χ		Х	Χ			Χ	Χ		Χ	Х									
Fully remote day			SHARON HS			Χ							Χ							Χ											
Early Release Day			SHARON HS																												
Good Friday - No School			SHARON HS					Х																							
April Vacation - No School			SHARON HS																						Χ	Χ	Χ	Χ	Х		
MILESTONES Foundation Placement Complete 4/30/21			Riggs																												
HOLIDAYS			990																												
Patriot's Day																									V						
WEATHER																									^						
WEATHER																															
SITEWORK SITE UTILITIES																															
Excavate/Backfill electrical ductbank - Post steel		40070									V	V/	V	V	\ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \ \			V		V						.,		V	V		
erection/coordination meeting with Eversource		A9670	Marois								Х	Х	X	Х	Χ			Χ	Х	Х	Х	Х				Х	Х	Х	Х		
Install electrical ductbank - Post steel		A9670	MAK								Х	Х	Х	Х	Х			Х	Х	Х	Х	Х				Х	Х	Х	Х		
erection/coordination meeting with Eversource		79010			.,	.,	.																								
Begin design work for gas main to new building			Columbia	Х	Х	Х	Х	X			Х	Х	Χ	Х	Χ			Х	Χ	Х	Х	X				Х	Х	Х	Х		
BUILDING FOUNDATION			Mana:-	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V	V		V	V	V	V	V	V
Dewatering E			Marois	X	Х	Х	Х	Х	Х	Х	Х	Х	Х	Х	X	Х	Χ	Χ	Χ	Х	Х	Х	Χ	Х		Х	Х	Х	Х	Х	Х
Building E Building D																															
Building C																															
Building F																															
Install Damproofing on F Building Foundations Walls		A10660	Superior	Х	Х																										
Backfill foundations (Walls) Building F		A10000	Marois		X	Х	Х	Х																							
Building A			IIIdi Olo		, , , , , , , , , , , , , , , , , , ,	Λ		^																							
		40000									.,		.,	.,																	
Install Foundation Walls for Building A		A9020	Riggs								Х	Х	Х	Х	Х																
Install Damproofing on A Building Foundations Walls		A10660	Superior															Χ	Х	.,	.,										
Backfill foundations (Walls) Building A - Install Foundations	tion Drain		Marois																Χ	Χ	Х	X									
Building G																															
Install Foundations (footings) for Building G		A9020	Riggs	Х	X	X																									
Backfill foundations (footings) Building G			Marois			Х	Х	Х																							
Install Foundation Walls for Building G		A9020	Riggs	Х	Х	Х	Х	Х			Х	Х	Х	Х	Х			Х	Х	.,	.,	.,									
Install Damproofing on A Building Foundations Walls		A10660	Superior					-						Х	Х			Х	Х	X	Х	Х									
Backfill foundations (Walls) Building G		7110000	Marois																							Х	Х	Х	Х		
Building B																															
Excavate for Foundations Building B			Marois															Х	Х	Х	Х	Х									
Install Foundations (footings) for Building B		A9020	Riggs	Х	Х	Х																				Х	Х	Х	Х		
Steel Erection																															
Building C																															
Steel Erection C Building		A9120	Supermetal/GP East		Х	Х																									
Deck and Detail C Building		A9190	Supermetal/GP East	X	X	Х	Х	Х			Х	Χ	Χ	Χ	Χ			Χ	Χ												
Building E		40400	0	V	V							V	V	V	\ <u>'</u>				V	V	\/	V				.,	\/	V	V		
Steel Delivery E Building Steel Erection E Building		A9160 A9160	Supermetal/GP East Supermetal/GP East		Х	Х	Y	_				X	X	X	X			Χ	X	X	X	X				X	X	X	X		
Deck and Detail E Building		A9160 A9230	Supermetal/GP East			^	^				^	^	X		X			X	X	X	X	X				X	X	X	X		
Underground Utilities		710200	Caponinotali Oi Last										, , ,					Α.									^	^	, ·		
Building E/D																															
Building F/G																															
Excavate and backfill for underground utilities			Marois										Х	Х	Х			Х	Х	Х	Х	Х									
Underground acid piping (deep runs)			Grasseschi										Х	Х	Х			Х	Х	Х	Х	Х									
