

4 Week Look Ahead Schedule 05/24/2021

- Upcoming Activities Include:
 - o Structural steel erection, decking, detailing & associated deliveries are ongoing
 - Placement of our first concrete slab is scheduled for this week. Preparation & placement of concrete slabs will continue to follow steel erection. Once placed, slabs will enable MEP trades to begin rough in.
 - Roofing and associated prep activities have started
 - Underground plumbing & electrical work is ongoing
 - o Fireproofing is scheduled to begin once slabs are placed
 - See attached progress update
 - See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/












Sharon High School



SHARON HS PROGRESS UPDATE MAY 2021

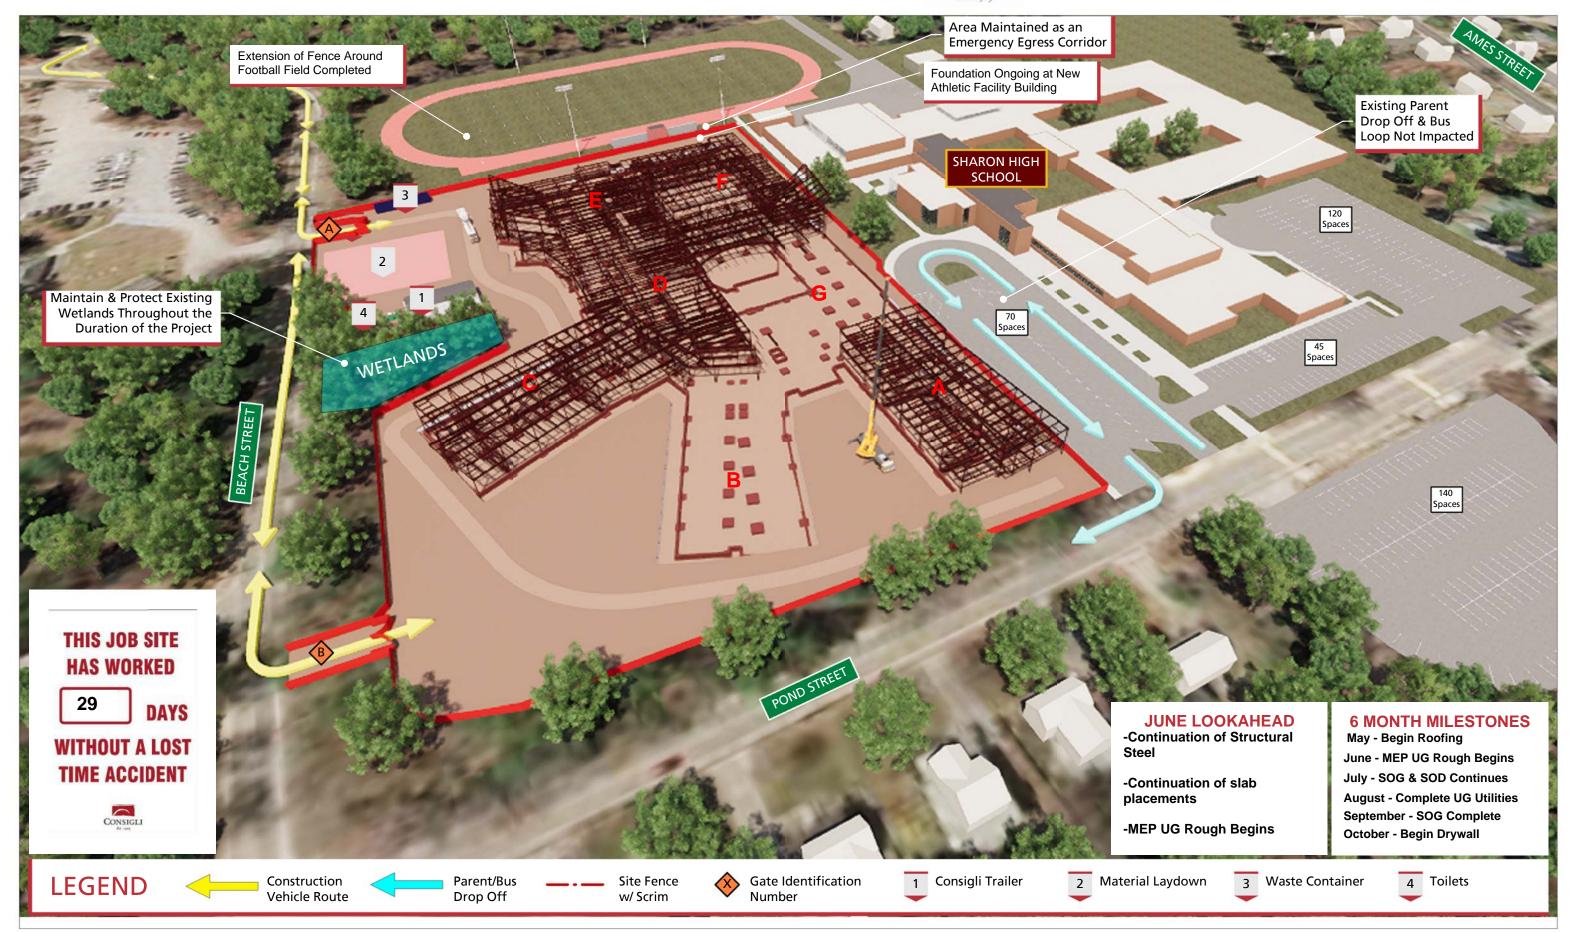

		LOOK AHEA	AD SCHEDULE 5/24/2021																											
Description of Work	Notes	P6 Activity Code	Responsibility	5/24 M	5/25 T	5/26 W	5/27 TR	5/28 FR	5/29	5/30 S		6/1 T		6/3 TR	6/4 FR	6/5	6/6 S	6/7 M	6/8 T	6/9 W	6/10 TR	6/11 FR	6/12	6/13 S	6/14 M	6/15 T	6/16 W		6/18 FR	6/20 S
Students onsite in school session			SHARON HS	Х	Х	Х	X	Х			Х	Х	Х	Х	Х			Х	Х	Χ	Х	Х			Х	Х	Χ			
Fully remote day			SHARON HS																											
Last Day of School MILESTONES			SHARON HS																								X			
Structural Steel Erection Complete	12-Jul		Supermetal/GP East																											
HOLIDAYS Memorial Day											V																			
WEATHER											Х																			
SITEWORK SITE UTILITIES																														
Excavate/Backfill electrical ductbank - Post steel	Pending Notes from	40070											.,	.,																
erection/coordination meeting with Eversource	Arch Engineers	A9670										Х	Х	Х	Х															
Install electrical ductbank - Post steel erection/coordination meeting with Eversource	Pending Notes from Arch Engineers	A9670											Х	Х	Х			Х	Х	Χ										
Begin design work for gas main to new building	Arch Engineers		Columbia	Х	Х	Х	Х	Х			Χ	Χ	Χ	Χ	Х			Х	Х	Χ	Χ	Х			Χ	Χ	Χ	Х	Х	
BUILDING FOUNDATION																														
Athletic Facility/Consession Install footings			Riggs	X	X	X																								
Install Foundation Walls			Riggs	,,	,	X	Х	Х				Χ	Χ	Χ	Х															
Underground Utilities Building A																														
Excavate and Backfill for underground sanitary piping -																						.,					.,	.,	- V	
Post Steel Erection/Deck and Detail			Marois																	Χ	Х	Х			Х	Х	Χ	Х	Х	
Install Sanitary underground			Grasseschi																	Χ	Χ	Х				Χ	Χ	Χ	Х	
Form/Place/Strip Column Collars	Include Base Plate Epoxy and Angles		Riggs															Х	Х	Χ	Х	Х			Χ	Х				
Building B	Epoxy and rangios																													
Building C	Include Base Plate																													
Form/Place/Strip Column Collars	Epoxy and Angles		Riggs	Х	Х	Х																								
Fine Grade - Southern Half			Marois	Х	Х	Х																								
Install Underground Conduit Run FPS SOG - Vapor Barrier, Rebar, mesh			Wayne J Griffin Riggs	X	Х	Х	X	Х				X	Y	Х	Х			X	X	Х										
Building D			Riggs											Λ				Λ	Α											
Excavate and backfill for underground plumbing			Marois																											
Install Sanitary underground			Grasseschi																											
Building E	Include Base Plate																													
Form/Place/Strip Column Collars	Epoxy and Angles		Riggs				Х	Х				Х	Х																	
Excavate and backfill for underground plumbing			Marois																											
Install Underground Plumbing			Grasseschi																	X	X	Х			Χ	Х	Х	Х	Х	
Building F																														
Steel Erection/Concrete Slab on Deck																														
Building C		10000	MEDITALE																											
Install MEP sleeves Place Concrete Deck	PUSHED	A9330 A9330	MEP TRADES Riggs		Х																								-	
Building E	. 0025																													
Install rebar and mesh on SOD Install MEP sleeves		A9330 A9330	Riggs MEP TRADES	X	X	X	X																							
Deck and Detail E Building	Include Studs	A9330 A9230	Supermetal/GP East		^	^																								
Building D																														
Steel Erection D Building - C Building Deck and Detail D Building	Include Studs	A9130 A9200	Supermetal/GP East Supermetal/GP East		X	X	X	X																					-	
Building F	s.uus Stuus						^	,																						
Steel Erection F Building Deck and Detail F Building	Include Studs	A9150	Supermetal/GP East Supermetal/GP East	X	X		V	X																						
Assemble & Erect trusses for gymnasium	molude Studs	A9200 A9200	Supermetal/GP East Supermetal/GP East		^	X		X				Х	Х	Х	Х			Х	Х	Х	Х									
Deck and Detail F Building (GYM)	Include Studs	A9200	Supermetal/GP East															Х	Х	Χ	Χ	Х			Χ	Χ	Χ	Х	Х	
Building A Steel Delivery A Building		A14470	Supermetal/GP East																											
Steel Erection A Building		A9100	Supermetal/GP East	X	Х	Χ		Х																						
Deck and Detail A Building Building B	Include Studs	A9170	Supermetal/GP East				X	Х				Х	Х	Х	Х			Х	Х	X	Х									
Steel Delivery B Building		A14470	Supermetal/GP East				Х	Х																						
 	-																													

		LOOK AHEA	AD SCHEDULE																												
			5/24/2021																												
Description of Work	Notes	P6 Activity Code	Responsibility	5/24 M		5/26 W		5/28 FR	5/29 1	5/30 S	5/31 M	6/1 T	6/2 W	6/3 TR	6/4 FR	6/5	6/6 S	6/7 M	6/8 T	6/9 W	6/10 TR	6/11 FR	6/12	6/13 S	6/14 M	6/15 T	6/16 W	6/17 TR		6/19	6/20 S
Steel Erection B Building		A9100	Supermetal/GP East					Х				Χ	Х	Х	Х																
Deck and Detail B Building	Include Studs	A9170	Supermetal/GP East												Х			Χ	Х	Χ	Χ	Χ			Х	Χ	Х	Χ	Х		
Building G																															
Steel Delivery G Building			Supermetal/GP East															X	Х	Х	Х	Х									
Steel Erection G Building			Supermetal/GP East																						X	Χ	Χ	Χ	Χ		
Roofing & Façade																															
Building C																															
Install Roof Blocking			Century	Х	Х	Х																									
Install LGMF at Low/High Roofing Wall			Century									Χ	Χ	Χ	X			Χ	Χ												
Install Exterior Framing Clips			Century									Χ	Χ	Χ	Х			Χ	Χ	Χ	Χ	Χ			Х	Χ	Х	Χ	Χ		
Install Roofing		A10920	Capeway									Χ	Χ	Χ	Х			Χ	Χ	Х	Χ	Χ									
Install Fire Proofing - Exterior structure		A9260	H Carr															Χ	Χ	Χ	Χ	Χ			Х	Χ	Х	Χ	Х		
Building E																															
Install Roof Blocking			Century	Χ	X	X	X	Х				Χ	Χ	Χ	Х			Χ	Χ	Х	Χ	X			X	Χ					
Install Roofing		A10920	Capeway																						X	Χ	Х	Х	Χ		
Building D																															
Install Roof Blocking			Century																						X	Χ	Χ	Χ	Х		
