

The Sharon High School Construction Project



4 Week Look Ahead Schedule 06/03/2021


- **Upcoming Activities Include:**

- Structural steel erection, decking, detailing & associated deliveries are ongoing
- Placement of the first slab on deck has been completed. Slab on deck and slab on grade placements will continue through the summer
- Roofing and associated prep activities have started
- Underground plumbing & electrical work is ongoing
- Fireproofing is scheduled to begin once slabs are placed
- See attached progress update
- See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information:
<https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



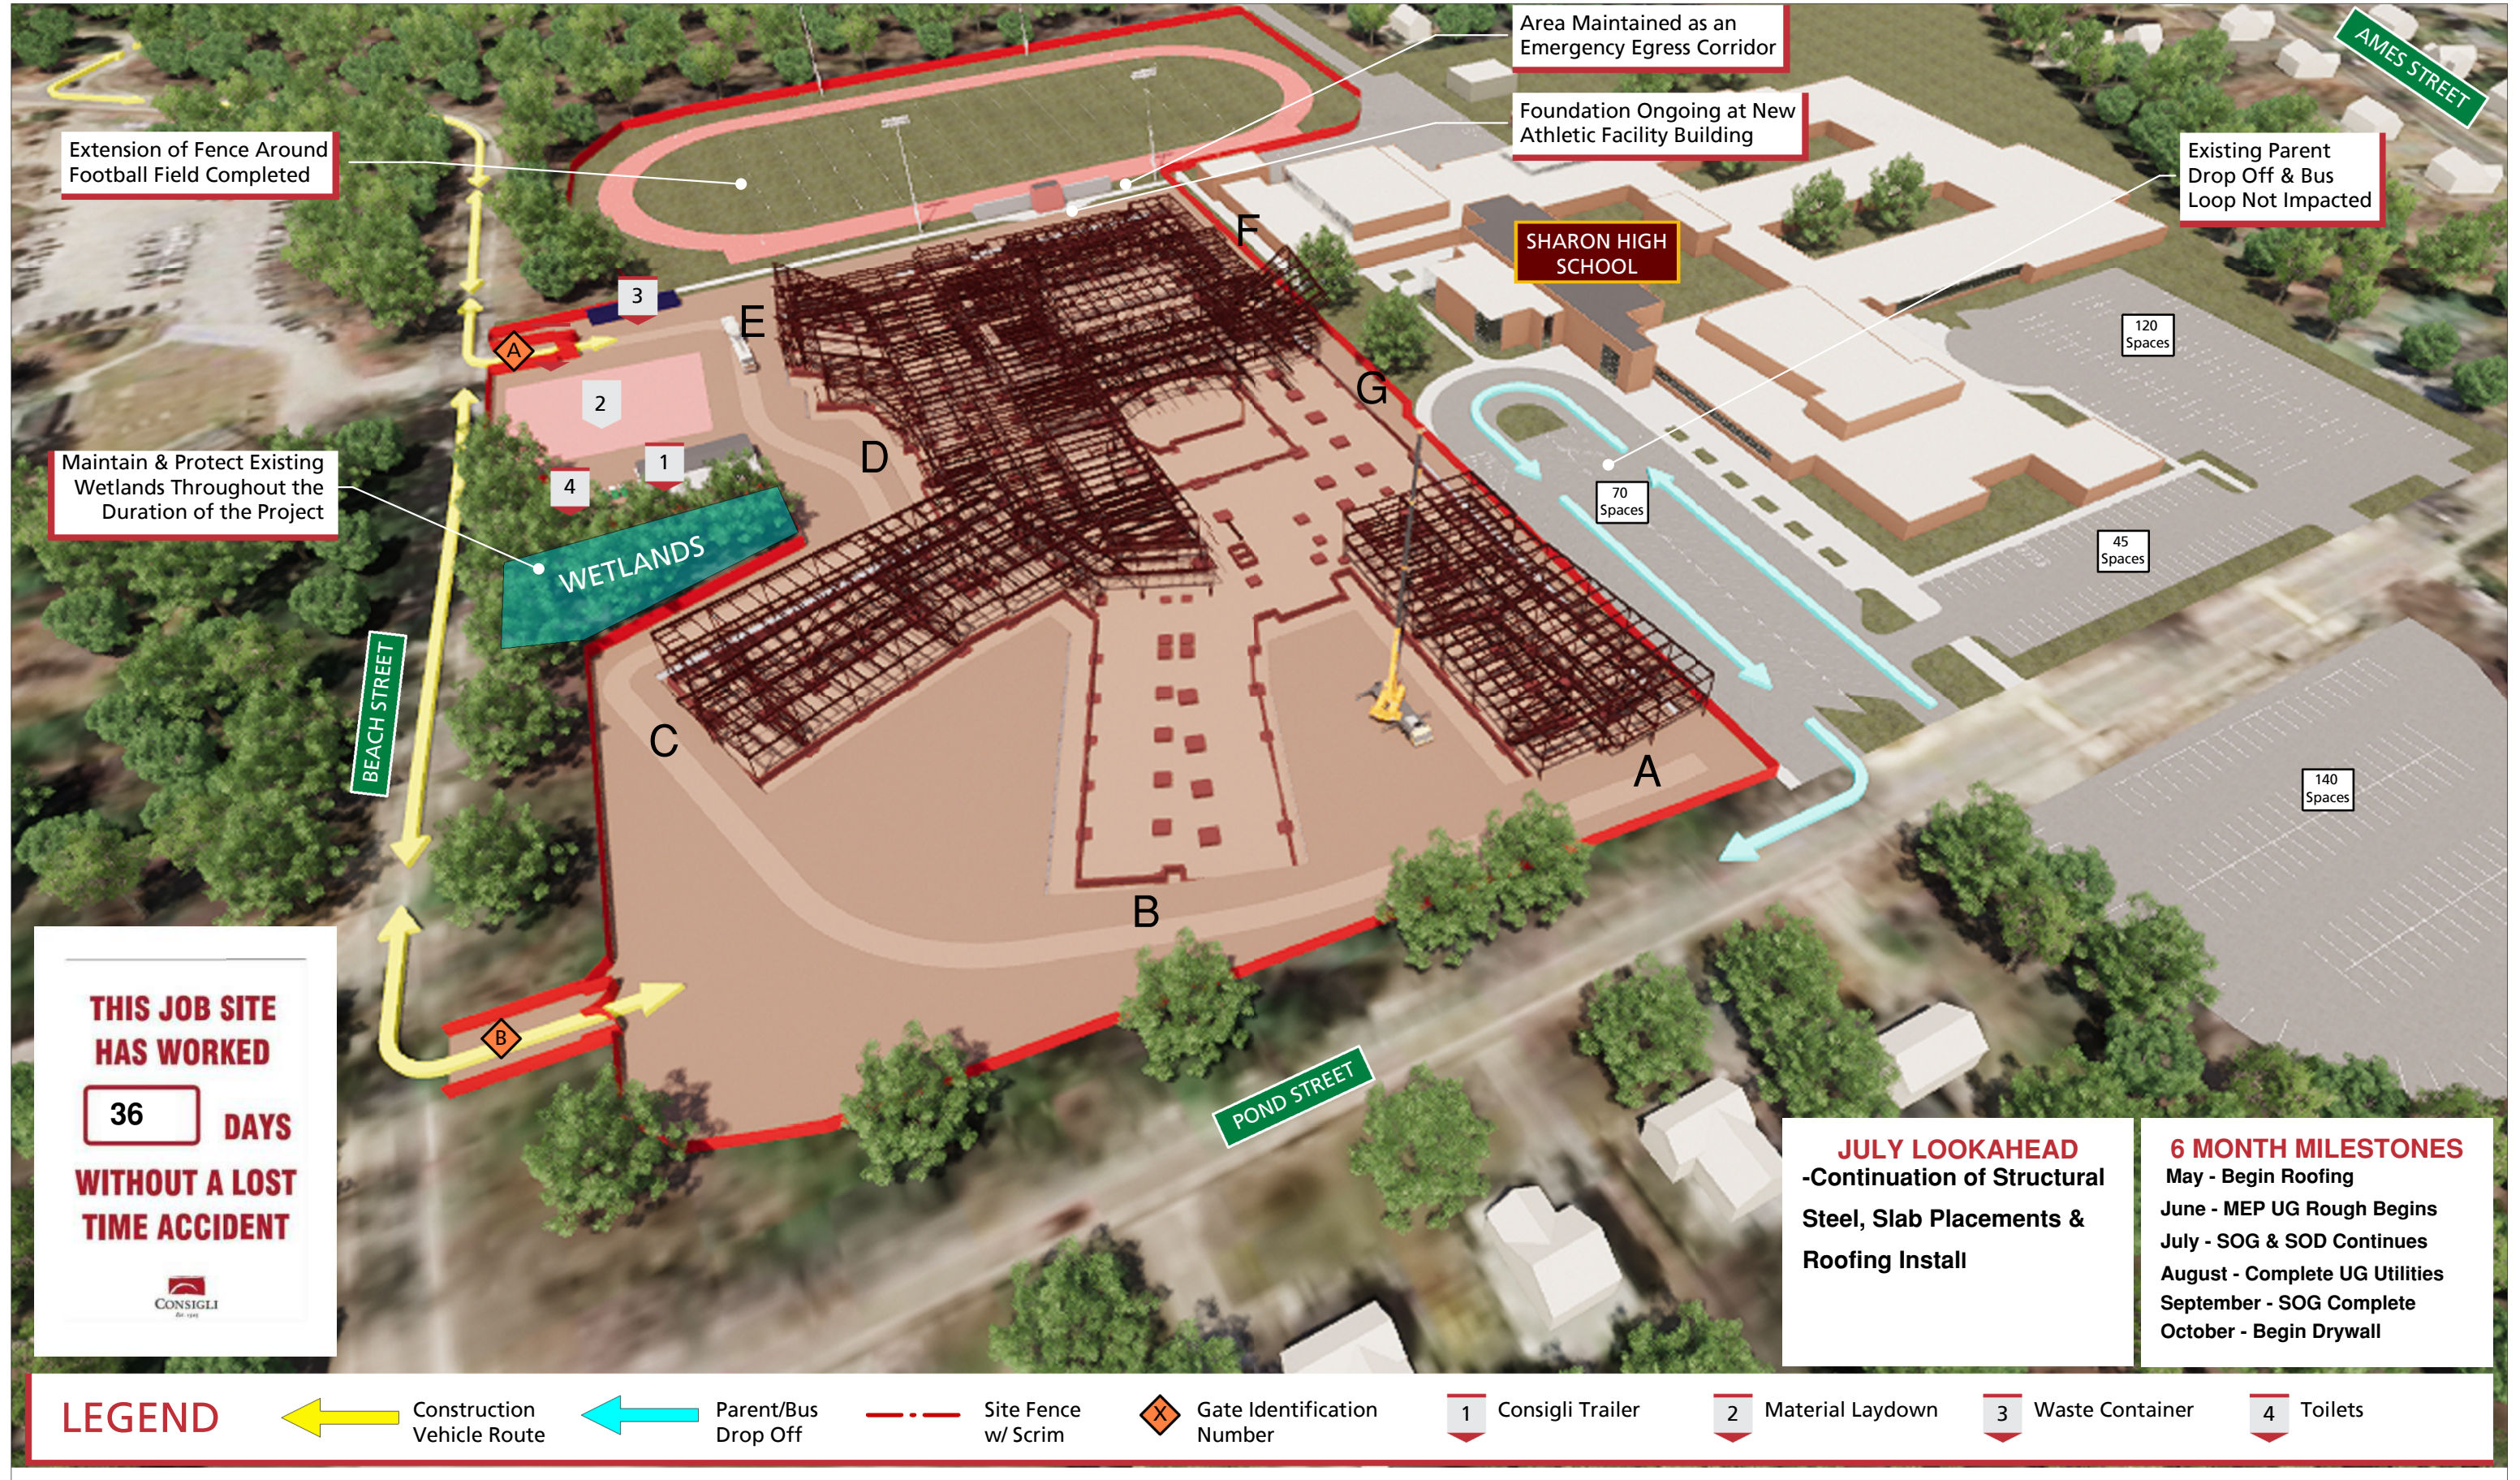

LOOK AHEAD SCHEDULE																																					
5/28/2021																																					
Description of Work	Notes	P6 Activity Code	Responsibility	5/31	6/1	6/2	6/3	6/4	6/5	6/6	6/7	6/8	6/9	6/10	6/11	6/12	6/13	6/14	6/15	6/16	6/17	6/18	6/19	6/20	6/21	6/22	6/23	6/24	6/25	6/26	6/27						
				M	T	W	TR	FR	1	S	M	T	W	TR	FR	1	S	M	T	W	TR	FR	1	S	M	T	W	TR	FR	1	S						
SCHOOL SCHEDULE																																					
Students onsite in school session			SHARON HS	X	X	X	X	X			X	X	X	X	X			X	X	X																	
Fully remote day			SHARON HS																																		
Last Day of School			SHARON HS																	X																	
MILESTONES																																					
Structural Steel Erection Complete	12-Jul		Supermetal/GP East																																		
HOLIDAYS																																					
Memorial Day				X																																	
WEATHER																																					
SITWORK																																					
SITE UTILITIES																																					
Excavate/Backfill electrical ductbank - Post steel erection/coordination meeting with Eversource	Pending Notes from Arch Engineers	A9670					X	X																													
Install electrical ductbank - Post steel erection/coordination meeting with Eversource	Pending Notes from Arch Engineers	A9670						X		X	X	X																									
Begin design work for gas main to new building			Columbia		X	X	X	X		X	X	X	X	X				X	X	X	X	X			X	X	X	X	X								
BUILDING FOUNDATION																																					
Athletic Facility/Consession																																					
Install footings			Riggs																																		
Install Foundation Walls			Riggs		X	X	X	X																													
Install Damproofing at foundations walls			Superior							X	X																										
Backfill foundations walls			Marois									X	X	X																							
Underground Utilities/Slab on Grade																																					
Building A																																					
Excavate and Backfill for underground sanitary piping - Post Steel Erection/Deck and Detail			Marois															X	X	X	X	X			X	X	X	X	X								
Install Sanitary underground			Grasseschi																X	X	X	X	X			X	X	X	X								
Form/Place/Strip Column Collars	Include Base Plate Epoxy and Angles		Riggs																																		
Building B																																					
Building C																																					
Form/Place/Strip Column Collars	Include Base Plate Epoxy and Angles		Riggs																																		
Install Underground Conduit Run			Wayne J Griffin																																		
FPS SOG - Vapor Barrier, Rebar, mesh			Riggs		X	X	X	X		X	X	X	X	X																							
Place C Building SOG												X	X	X																							
Building D																																					
Excavate and backfill for underground plumbing			Marois		X	X	X	X		X	X	X																									
Install Sanitary underground			Grasseschi		X	X	X	X																													
Building E																																					
Form/Place/Strip Column Collars	Include Base Plate Epoxy and Angles		Riggs		X	X																															
Excavate and backfill for underground plumbing			Marois								X	X	X	X				X	X	X	X	X			X	X											
Install Sanitary underground - Kitchen			Grasseschi									X	X	X	X			X	X	X	X	X			X	X	X	X									
Building F																																					
Excavate and backfill for underground plumbing			Marois					X		X	X	X	X	X				X	X	X																	
Install Storm underground			Grasseschi							X	X	X	X	X				X																			
Steel Erection/Concrete Slab on Deck																																					
Building C																																					
Wet Cure SOD		A9330	Riggs	X	X	X																															
Building E																																					
Place Concrete Deck		A9370	Riggs		X																																
Wet Cure SOD		A9370	Riggs			X	X	X	X	X	X																										
Building D																																					
Steel Erection D Building - Remaining Steel		A9160	Supermetal/GP East							X	X	X	X	X																							
Deck and Detail D Building - Remaining Steel	Include Studs	A9230	Supermetal/GP East							X	X	X	X	X																							
Building F																																					
Deck and Detail F Building	Include Studs	A9150	Supermetal/GP East		X	X																															
Assemble & Erect trusses for gymnasium		A9220	Supermetal/GP East		X	X	X	X		X	X	X	X	X				X	X																		
Deck and Detail F Building (GYM)	Include Studs	A9220	Supermetal/GP East															X	X	X	X	X			X	X											
Building A																																					
Steel Erection A Building		A9100	Supermetal/GP East		X	X																															
Deck and Detail A Building	Include Studs	A9170	Supermetal/GP East		X	X	X	X		X	X	X	X																								
Building B																																					
Steel Delivery B Building		A14470	Supermetal/GP East																																		
Steel Erection B Building		A9100	Supermetal/GP East			X	X	X		X	X	X																									
Deck and Detail B Building	Include Studs	A9170	Supermetal/GP East				X			X	X	X	X	X				X	X	X	X	X			X	X											
Building G																																					
Steel Delivery G Building		A14510	Supermetal/GP East							X	X	X	X	X																							
Steel Erection G Building		A9140	Supermetal/GP East															X	X	X	X	X			X	X	X	X	X								
Roofing & Façade																																					
Building C																																					
Install LGMF at Low/High Roofing Wall			Century		X	X	X	X		X	X																										
Install Exterior Framing Clips			Century		X	X	X	X		X	X	X	X	X				X	X	X	X	X			X	X	X	X	X								
Install Roofing		A10920	Capeway		X	X	X	X		X	X	X	X	X				X	X	X	X	X			X	X	X	X	X								
Install Fire Proofing - Exterior structure		A9260	H Carr							X	X	X	X	X				X	X	X	X	X			X	X	X	X	X								
Building E																																					
Install Roof Blocking			Century		X	X	X	X		X	X	X	X	X				X	X																		
Install Roofing		A10920	Capeway		X	X	X	X		X	X	X	X	X				X	X	X	X	X			X	X	X	X	X								
Building D																																					
Install Roof Blocking			Century															X	X	X	X	X			X	X	X	X	X								
