

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule 06/14/2021

- **Upcoming Activities Include:**


- Structural steel erection, decking, detailing & associated deliveries are ongoing. Installation of gymnasium roof trusses is scheduled for next week.
- Concrete slab placement is ongoing. Preparation & placement of concrete slabs will continue to follow steel erection. This is enabling framing & MEP trades to begin work.
- Roof installation is ongoing.
- Underground plumbing & electrical work is ongoing (site & within the building)
- Fireproofing is ongoing.
- Installation & backfill of foundations at athletic facility is ongoing.
- Our first slab on grade placement occurred this week- this process may extend beyond normal working hours (see enclosed notice). We will continue to highlight potential upcoming slab on grade placements dates in this look ahead schedule.
- See attached progress update. See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbldg.com/>

Town of  
**SHARON**  
Massachusetts





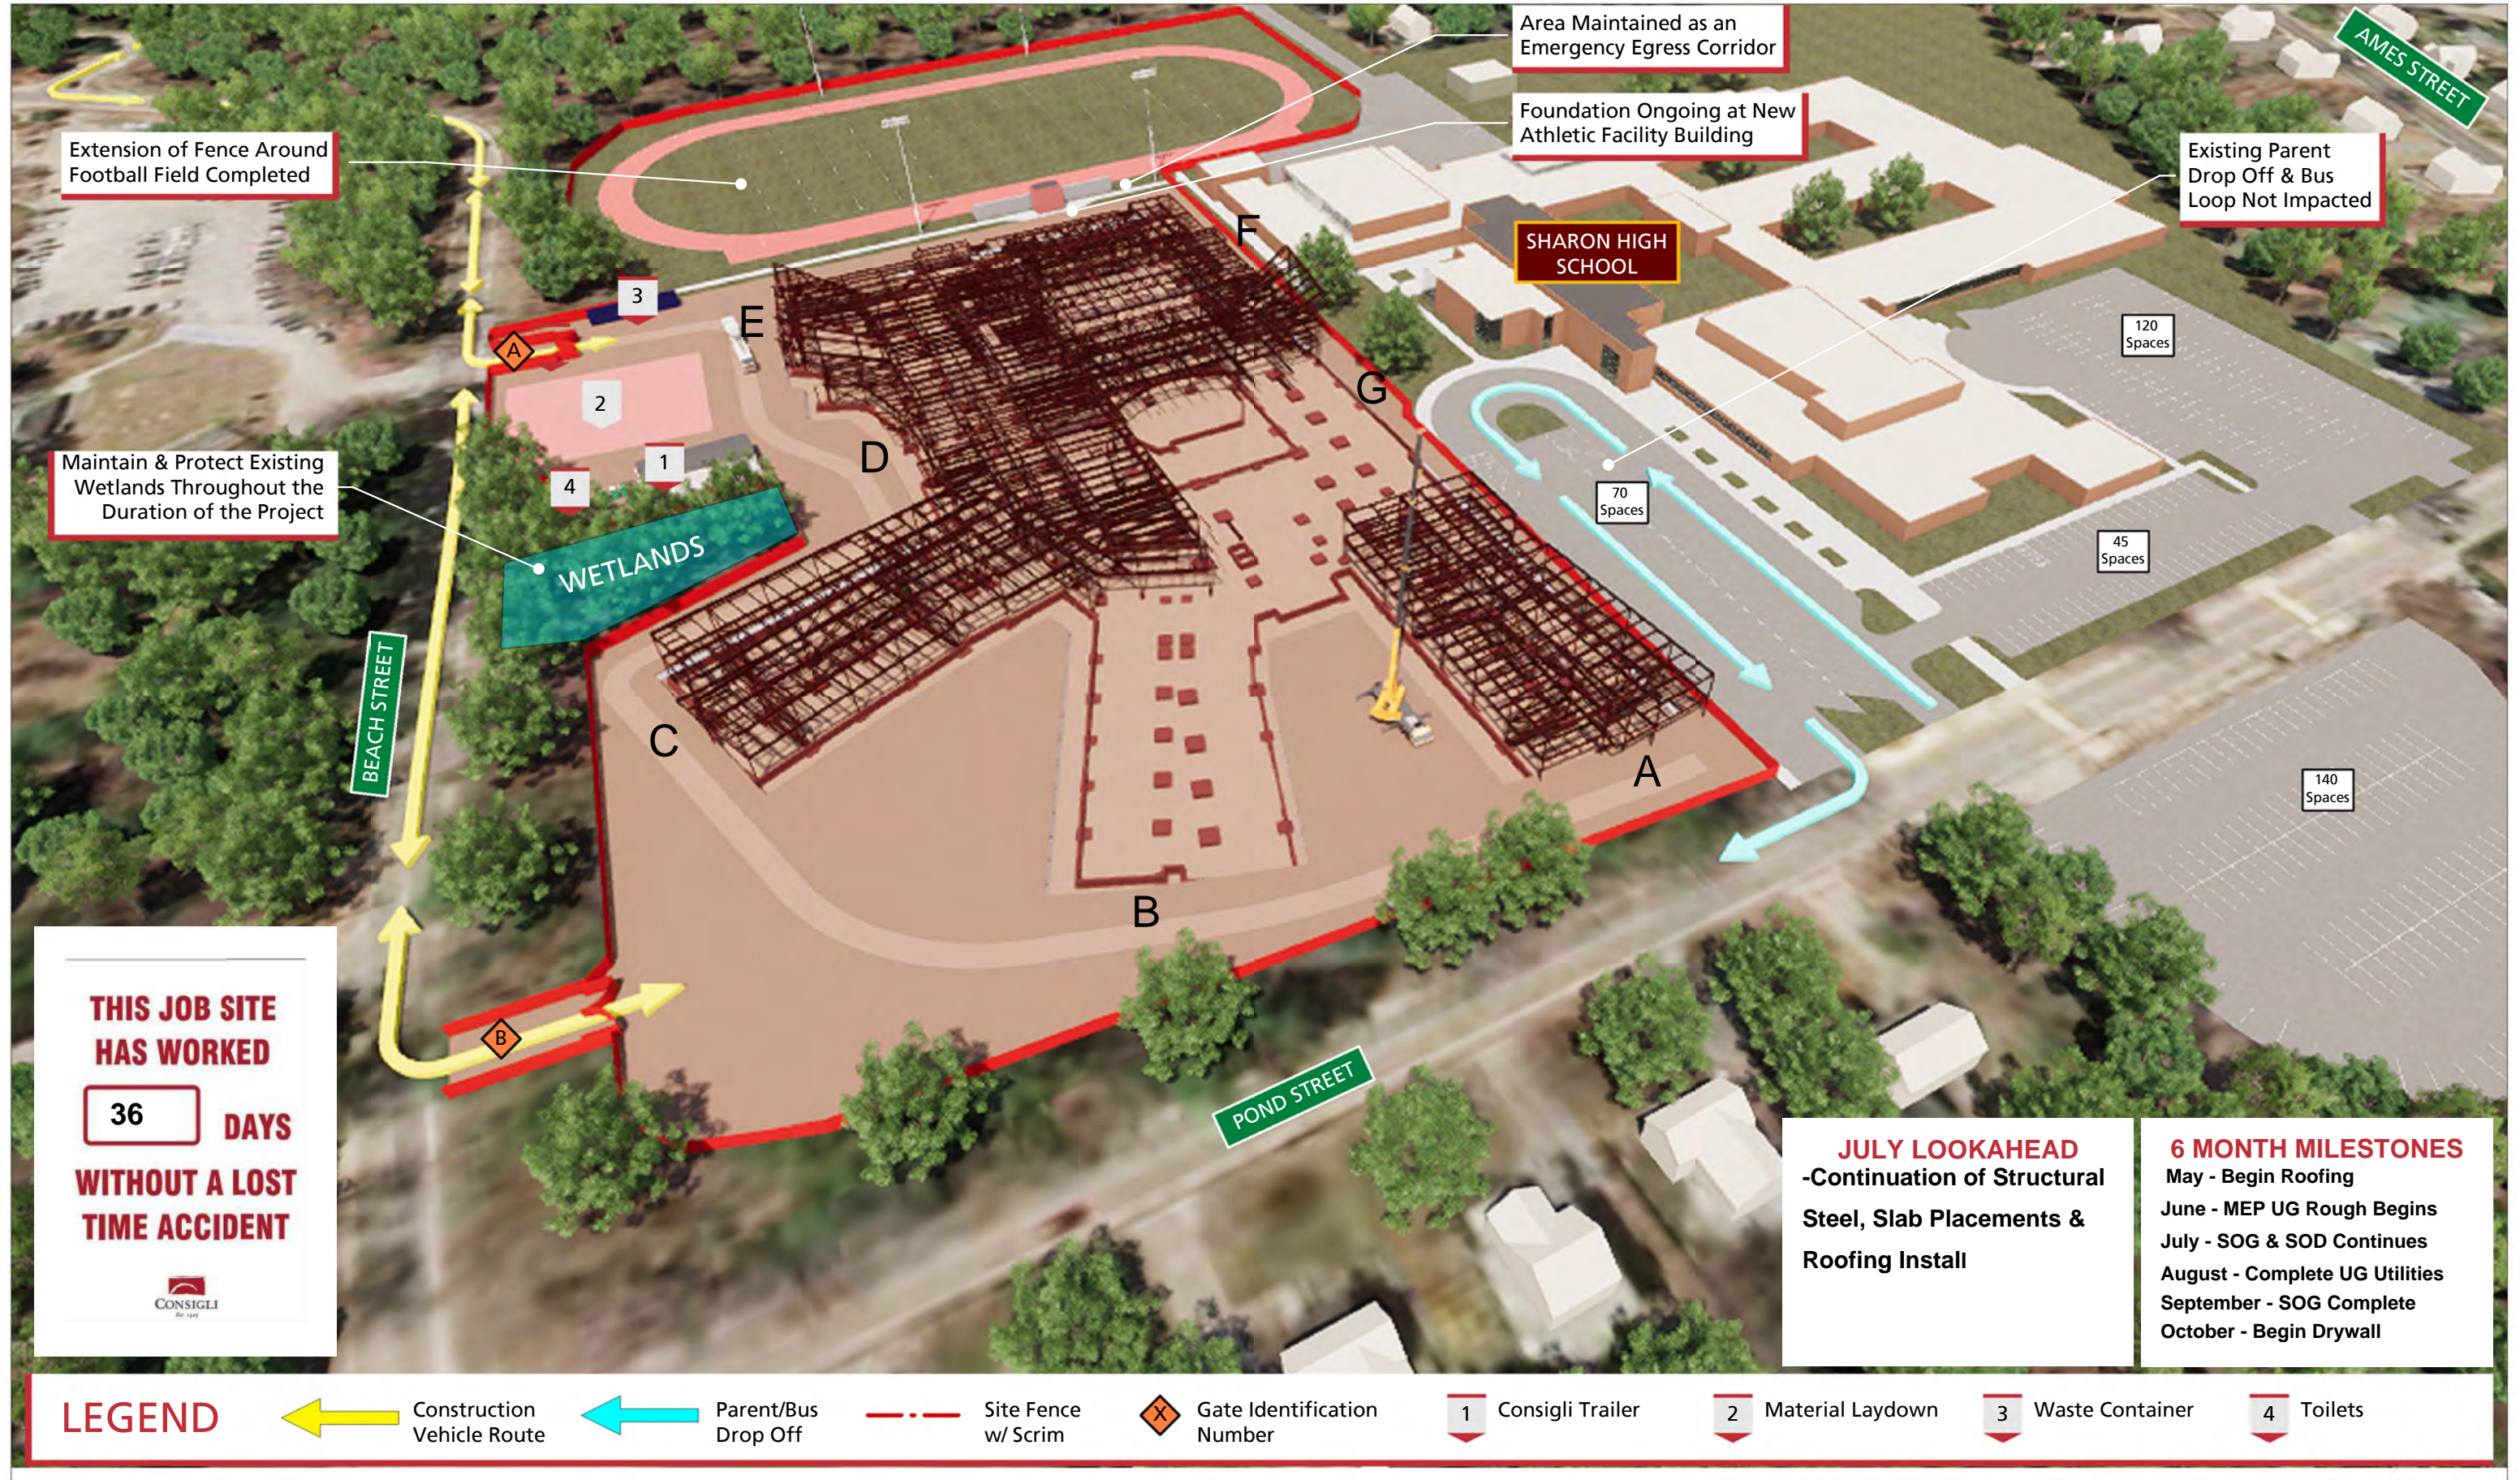

Extension of Fence Around Football Field Completed

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

Area Maintained as an Emergency Egress Corridor

Foundation Ongoing at New Athletic Facility Building

Existing Parent Drop Off & Bus Loop Not Impacted

SHARON HIGH SCHOOL

WETLANDS

**THIS JOB SITE HAS WORKED**

**36** DAYS WITHOUT A LOST TIME ACCIDENT

**JULY LOOKAHEAD**  
-Continuation of Structural Steel, Slab Placements & Roofing Install

**6 MONTH MILESTONES**  
 May - Begin Roofing  
 June - MEP UG Rough Begins  
 July - SOG & SOD Continues  
 August - Complete UG Utilities  
 September - SOG Complete  
 October - Begin Drywall

**LEGEND**

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets









**Sharon High School: Notice of Potential After-Hours Work**

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

*Matthew Gulino*

Matthew Gulino  
Associate | Owner's Project Manager  
PMA Consultants  
[mgulino@pmaconsultants.com](mailto:mgulino@pmaconsultants.com)
