

The Sharon High School Construction Project



4 Week Look Ahead Schedule 07-26-21

- Structural steel erection is complete. Minor decking & detailing is ongoing.
- Roof installation is ongoing.
- Concrete slab placements are ongoing.
- Overhead MEP rough-in is ongoing at multiple areas
- Both interior and exterior light gauge metal framing are ongoing at multiple areas.
- Masonry installation- including shafts & interior walls- are ongoing.
- Underground plumbing & electrical work is ongoing.
- Work at the athletic facility- including masonry- is ongoing.
- Work at the athletic field including drainage & athletic equipment foundations is ongoing.
- Polished concrete will begin in the coming weeks.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts




PMA Consultants



TAPPÉ
ARCHITECTS



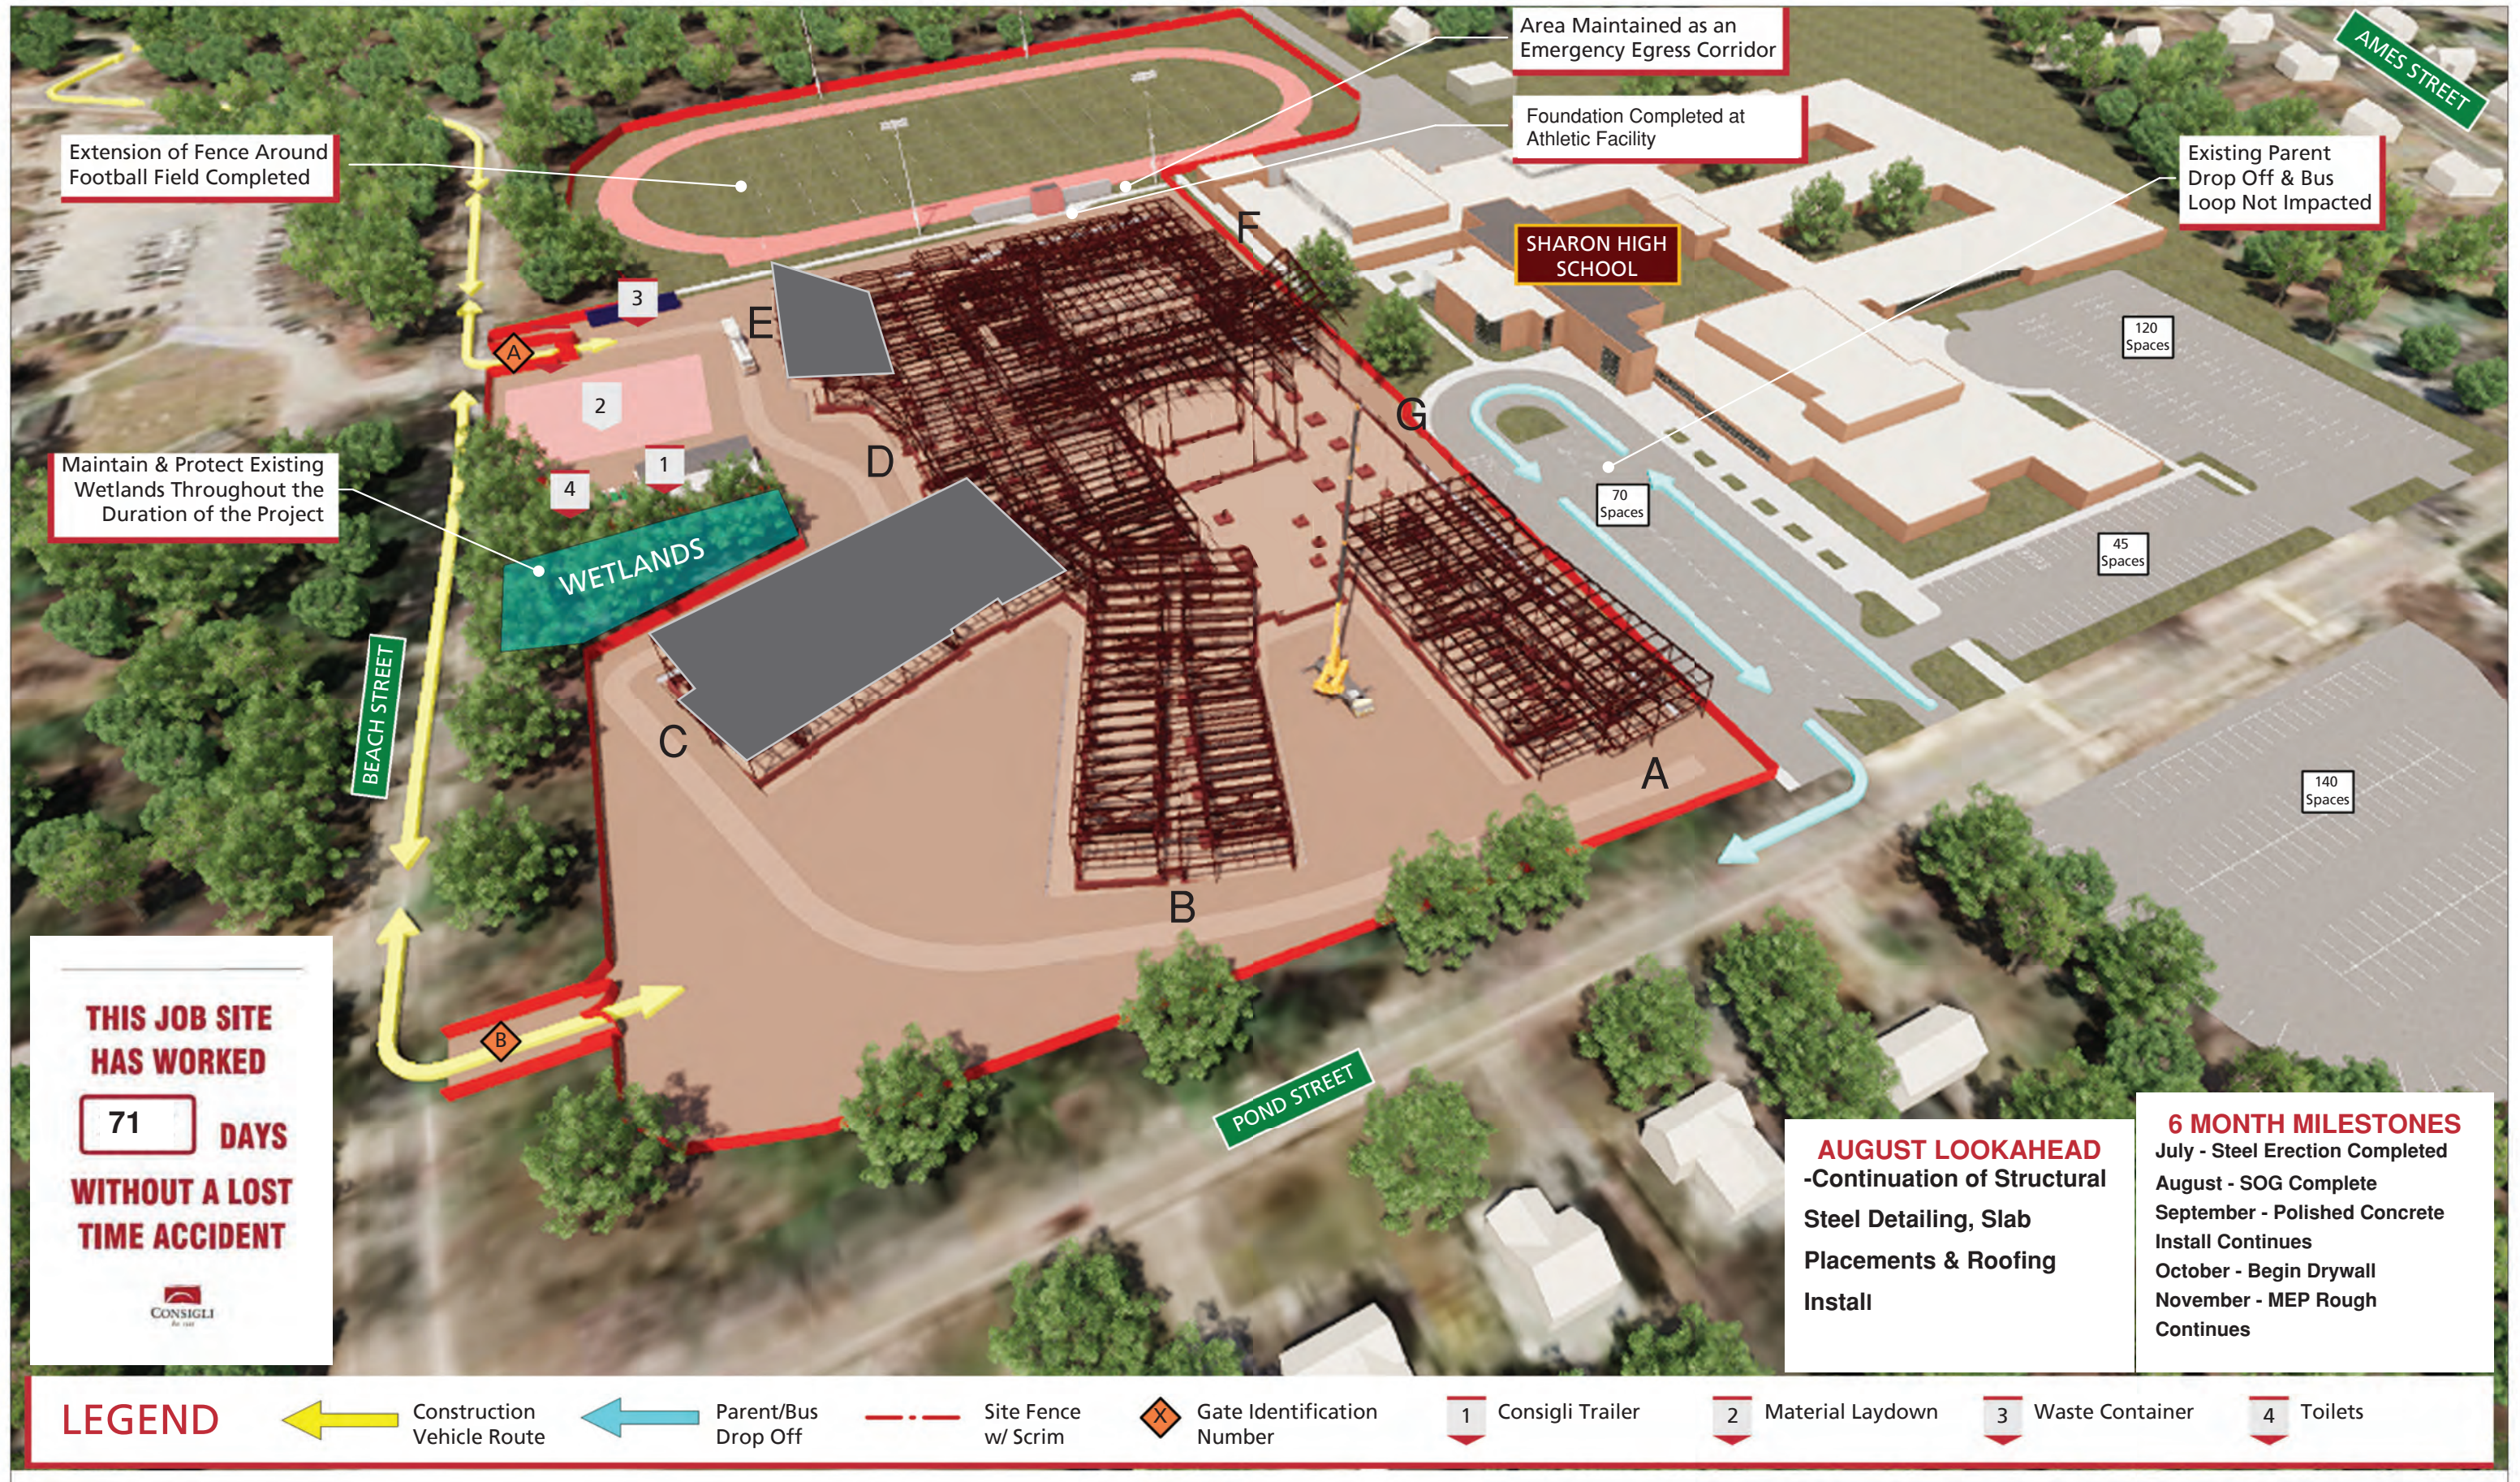

THIS JOB SITE HAS WORKED

71 DAYS

WITHOUT A LOST TIME ACCIDENT

6 MONTH MILESTONES

- July - Steel Erection Completed
- August - SOG Complete
- September - Polished Concrete Install Continues
- October - Begin Drywall
- November - MEP Rough Continues

AUGUST LOOKAHEAD

- Continuation of Structural Steel Detailing, Slab Placements & Roofing Install

LEGEND	
	Construction Vehicle Route
	Parent/Bus Drop Off
	Site Fence w/ Scrim
	Gate Identification Number
	1 Consigli Trailer
	2 Material Laydown
	3 Waste Container
	4 Toilets



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
