

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule 08-16-21

- Structural steel erection is complete. Minor decking & detailing is ongoing.
- Roof installation is ongoing.
- Concrete slab placements are ongoing. Please note: we currently have slab on grade placements - which may include late work- scheduled for 8/26- see enclosed notice.
- Overhead MEP rough-in is ongoing at multiple areas
- Both interior and exterior light gauge metal framing are ongoing at multiple areas.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation will follow.
- Masonry installation - including interior auditorium walls- is ongoing.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Polished concrete is ongoing at the 2nd floor.
- Work at the athletic field including drainage & athletic equipment foundations is ongoing.
- See attached progress update.
  
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of  
**SHARON**  
Massachusetts






# Sharon High School



**SHARON HS PROGRESS UPDATE  
AUGUST 2021**

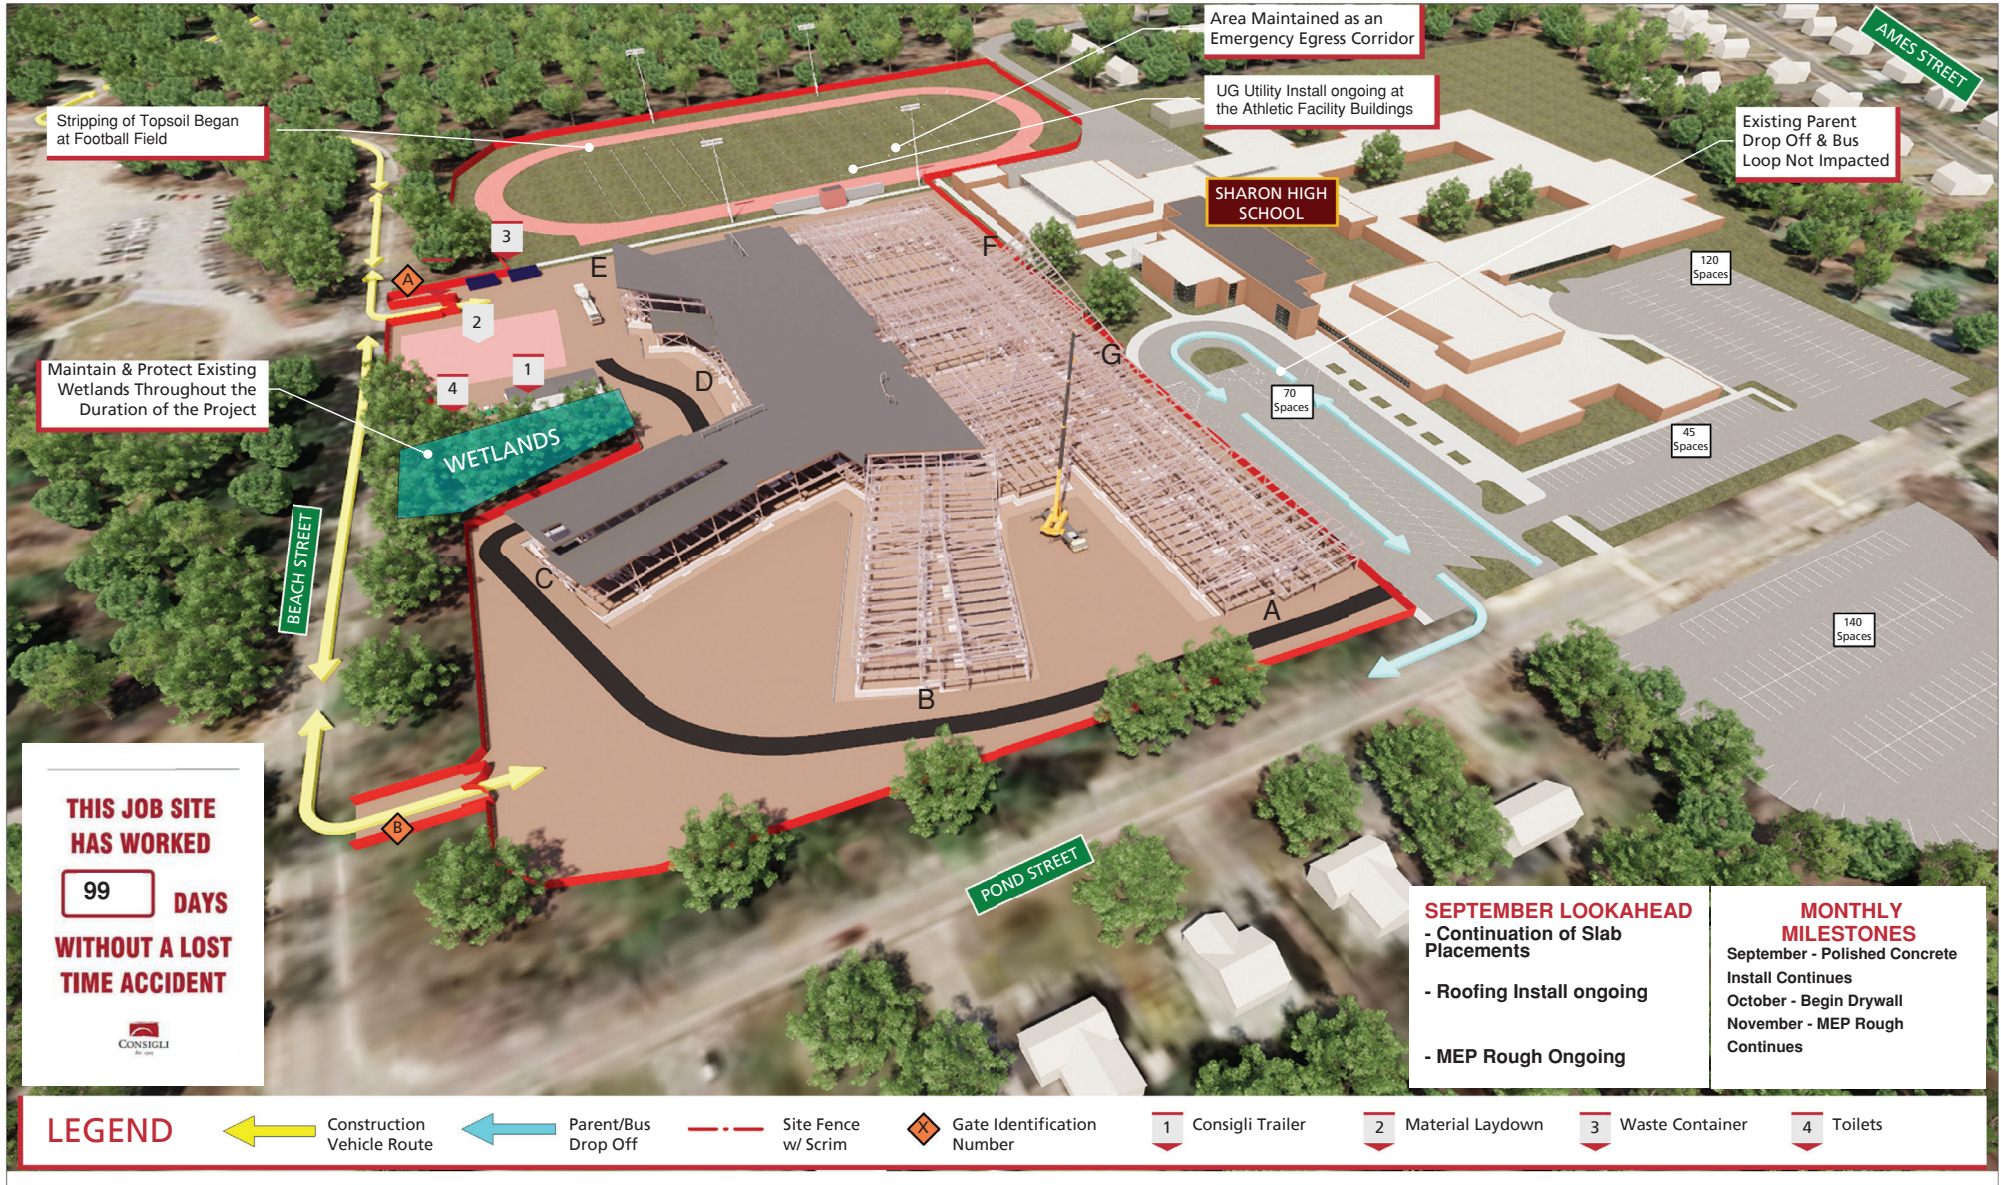

**THIS JOB SITE HAS WORKED**  
**99 DAYS**  
**WITHOUT A LOST TIME ACCIDENT**



**SEPTEMBER LOOKAHEAD**  
- Continuation of Slab Placements  
- Roofing Install ongoing  
- MEP Rough Ongoing

**MONTHLY MILESTONES**  
September - Polished Concrete Install Continues  
October - Begin Drywall  
November - MEP Rough Continues

- LEGEND**
- Construction Vehicle Route
  - Parent/Bus Drop Off
  - Site Fence w/ Scrim
  - Gate Identification Number
  - 1 Consigli Trailer
  - 2 Material Laydown
  - 3 Waste Container
  - 4 Toilets









**Sharon High School: Notice of Potential After-Hours Work**

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

*Matthew Gulino*

Matthew Gulino  
Associate | Owner's Project Manager  
PMA Consultants  
[mgulino@pmaconsultants.com](mailto:mgulino@pmaconsultants.com)
