

The Sharon High School Construction Project



4 Week Look Ahead Schedule 08-23-21

- Structural steel erection is complete. Minor decking & detailing is ongoing.
- Roof installation is ongoing.
- Concrete slab placements are ongoing. Please note: we currently have slab on grade placements - which may include late work- scheduled for 8/30- see enclosed notice.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. Installation of drywall tops is ongoing. Wall close-in is targeted over the next few weeks.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is following.
- Interior masonry installation - including auditorium walls- is ongoing.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Polished concrete is ongoing at the 2nd floor.
- Work at the athletic field- including irrigation installation- is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>


Town of
SHARON
Massachusetts



Sharon High School



**SHARON HS PROGRESS UPDATE
AUGUST 2021**

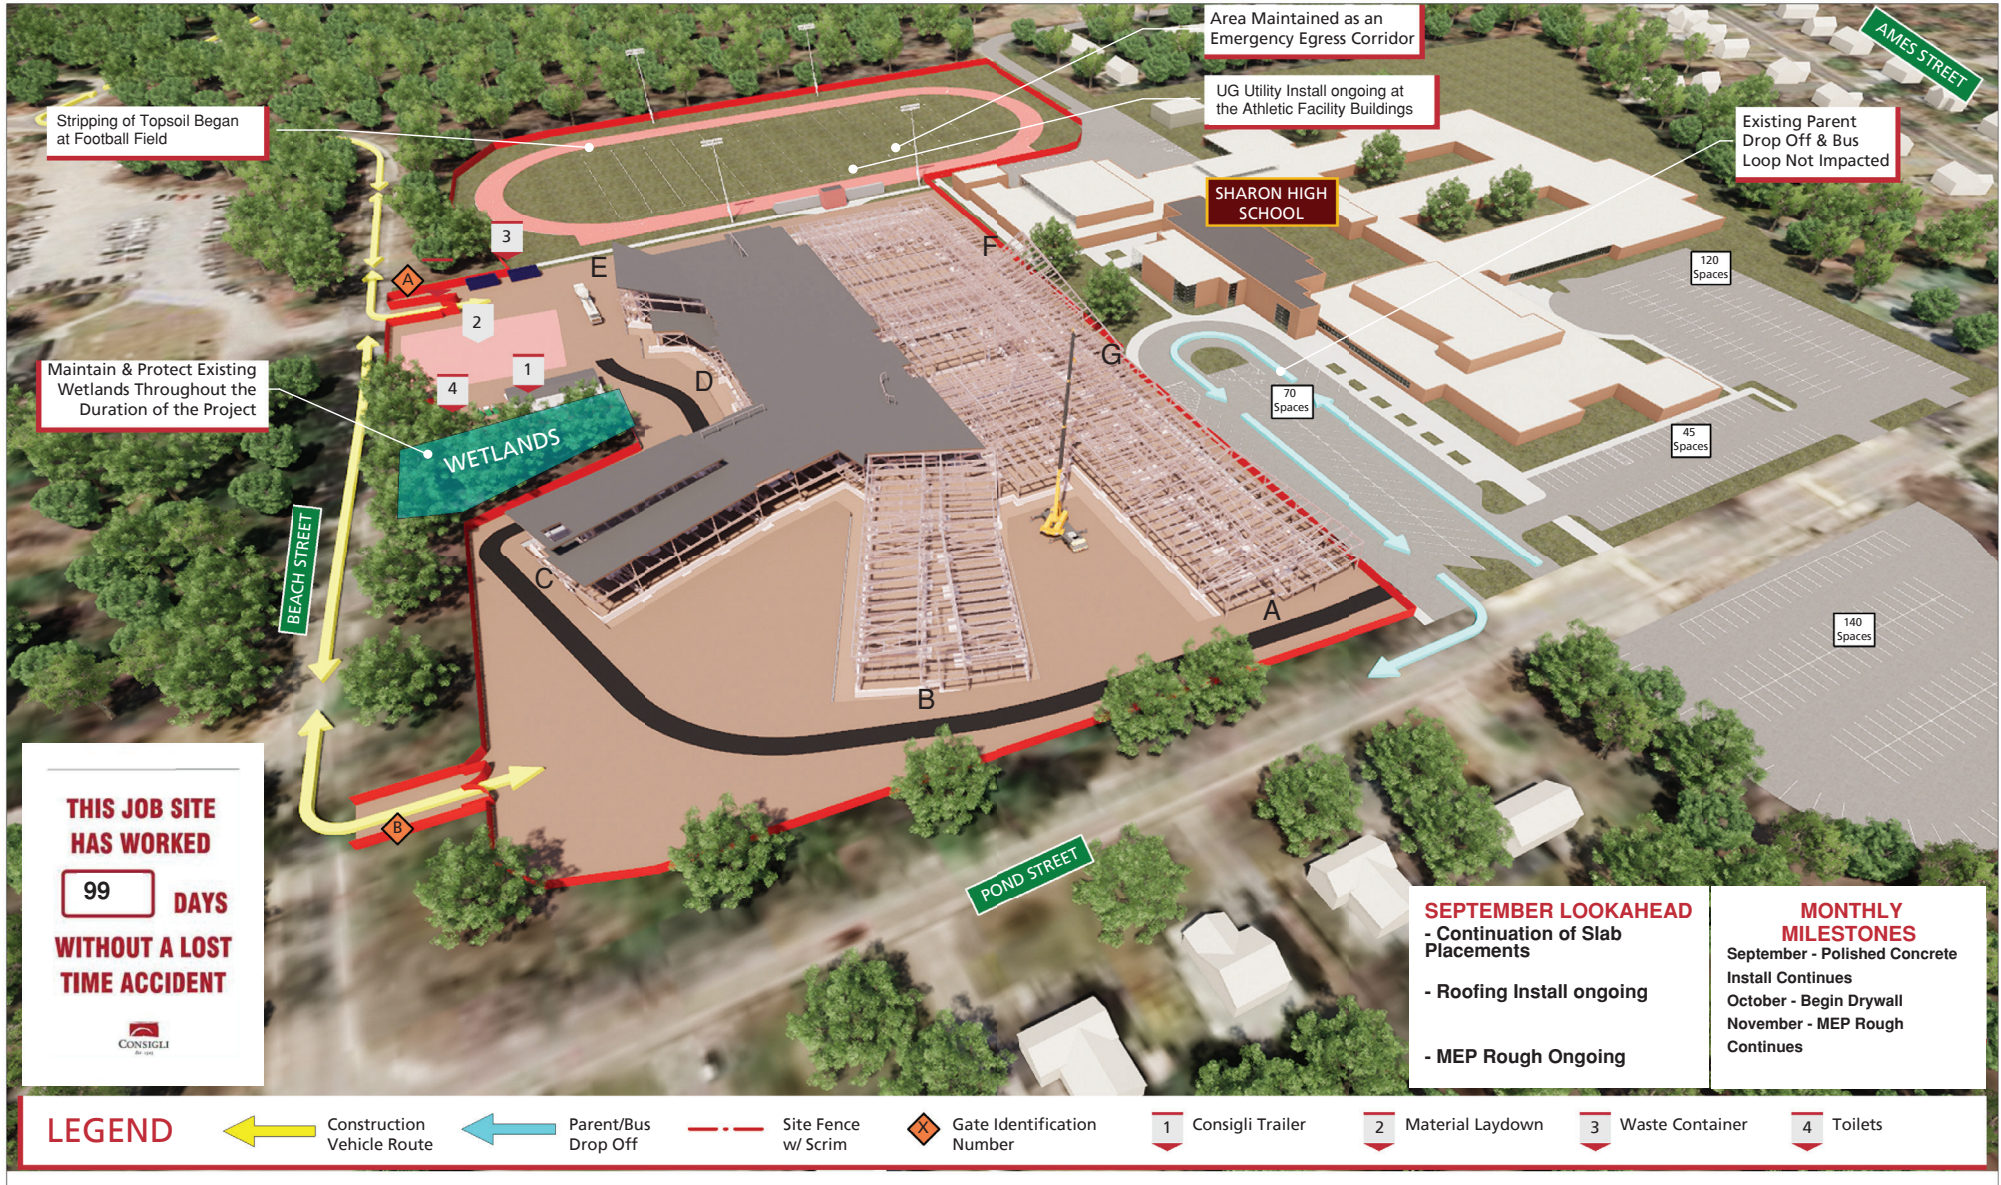

THIS JOB SITE HAS WORKED
99 DAYS
WITHOUT A LOST TIME ACCIDENT



SEPTEMBER LOOKAHEAD
- Continuation of Slab Placements
- Roofing Install ongoing
- MEP Rough Ongoing

MONTHLY MILESTONES
September - Polished Concrete Install Continues
October - Begin Drywall
November - MEP Rough Continues

- LEGEND**
- Construction Vehicle Route
 - Parent/Bus Drop Off
 - Site Fence w/ Scrim
 - Gate Identification Number
 - 1 Consigli Trailer
 - 2 Material Laydown
 - 3 Waste Container
 - 4 Toilets



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
