

The Sharon High School Construction Project



4 Week Look Ahead Schedule 09-06-21

- Structural steel erection is complete. Minor decking & detailing is ongoing.
- Roof installation is ongoing.
- Concrete slab placements are ongoing. Please note: slab on grade placements - which may include late work-are ongoing- see enclosed notice.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. Installation of drywall tops is ongoing. Wall close-in is on the radar.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry is also scheduled to begin within the next month.
- Interior masonry installation - including interior walls- is ongoing.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Polished concrete is ongoing.
- Work at the athletic field- including irrigation & athletic equipment prep- is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



PMA Consultants




TAPPÉ
ARCHITECTS



Sharon High School



**SHARON HS PROGRESS UPDATE
AUGUST 2021**

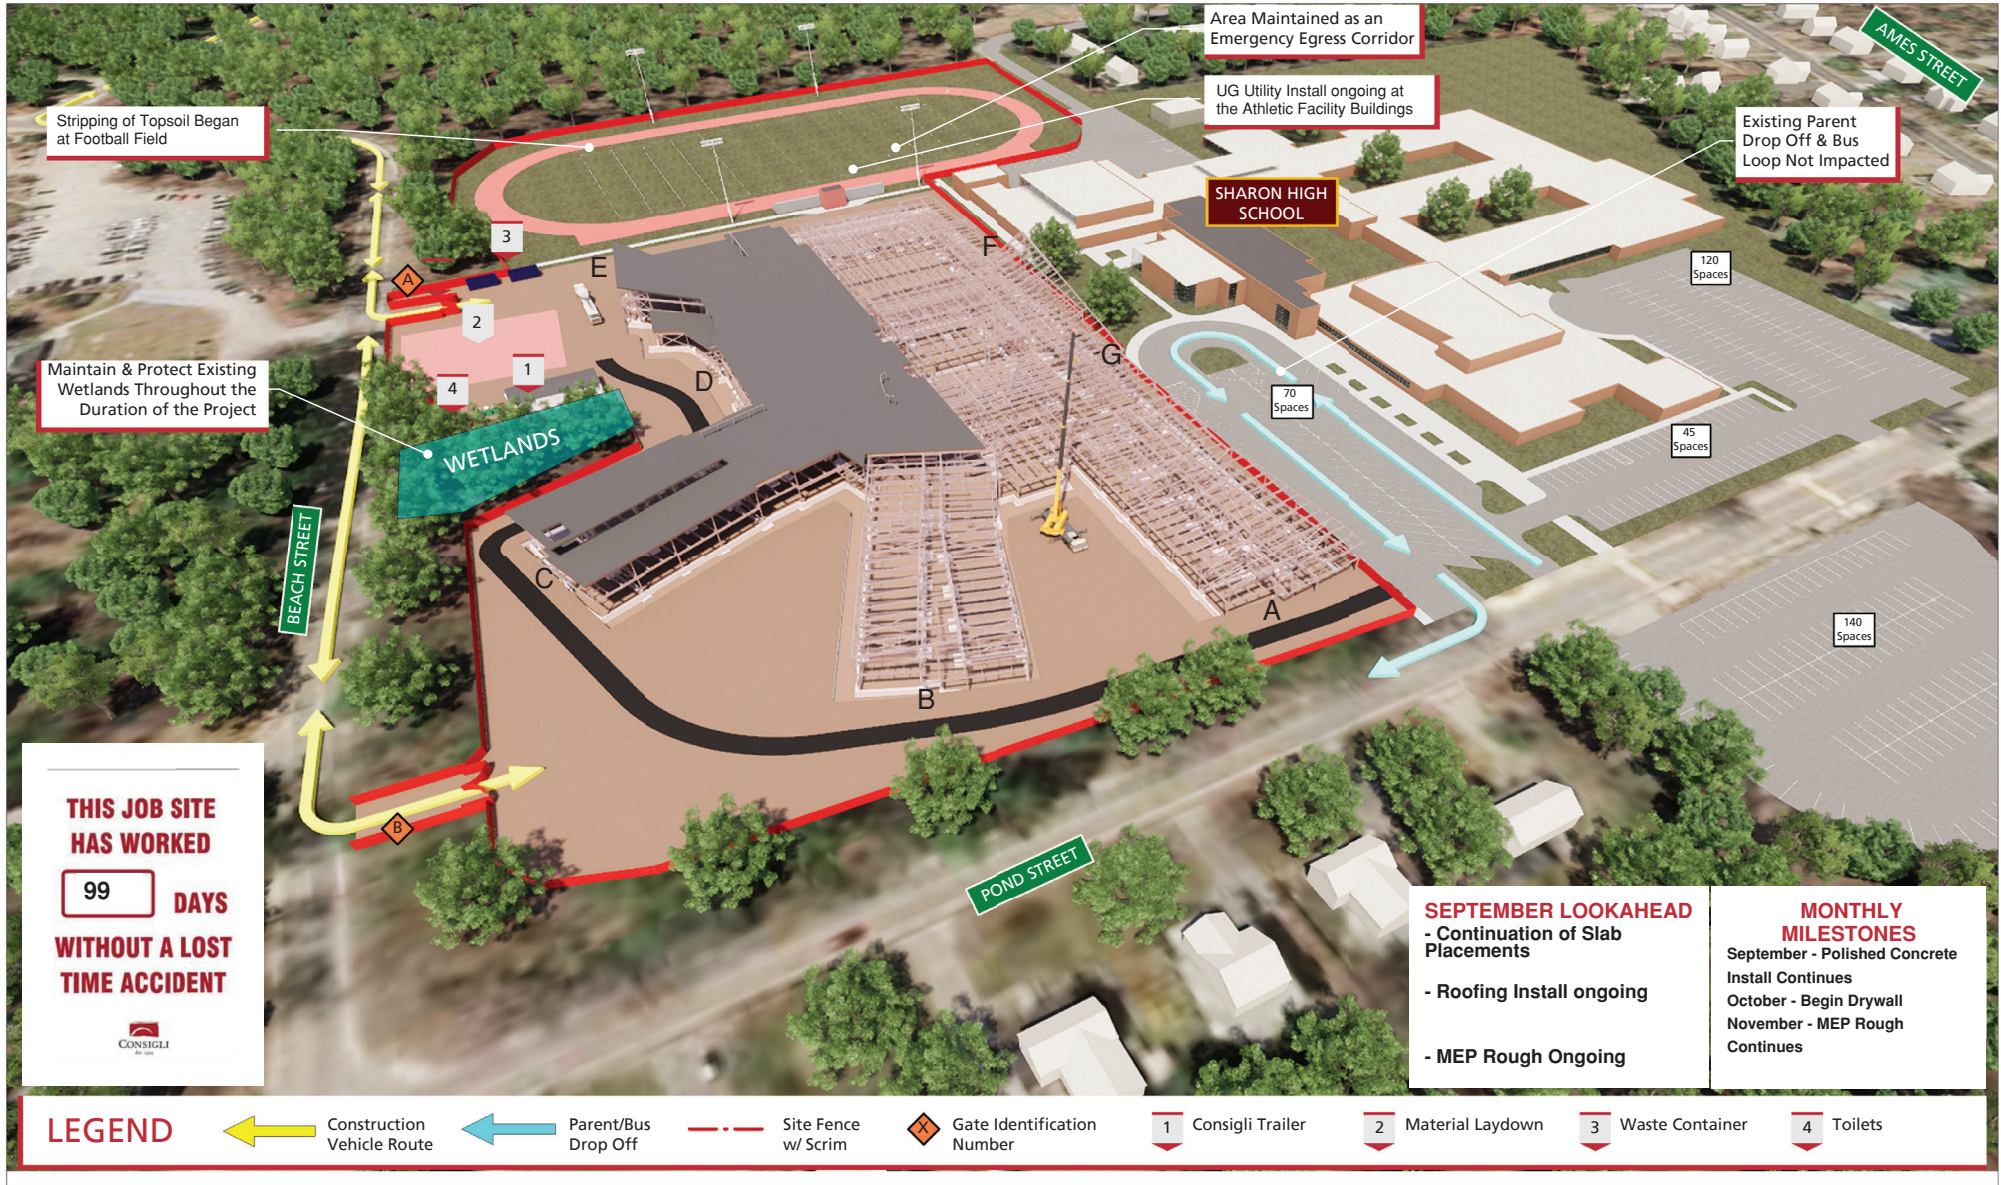

LOOK AHEAD SCHEDULE

9/7/2021

Description of Work	Notes	P6 Activity Code	Responsibility	9/6	9/7	9/8	9/9	9/10	9/11	9/12	9/13	9/14	9/15	9/16	9/17	9/18	9/19	9/20	9/21	9/22	9/23	9/24	9/25	9/26	9/27	9/28	9/29	9/30	10/1	10/2	10/3						
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S						
Set perimeter roof blocking and cantilevered supports			Supermetal/GP East								X	X	X	X	X																						
Weld roof screens and channel supports			Supermetal/GP East															X	X	X	X	X															
Building A																																					
Install all window and brick support angles			Supermetal/GP East		X	X	X	X																													
Set perimeter roof blocking and cantilevered supports			Supermetal/GP East		X	X	X	X																													
Weld roof screens and channel supports			Supermetal/GP East		X	X	X	X																													
Building G																																					
Deck and Detail Building G Roof			Supermetal/GP East		X	X	X	X																													
Weld roof screens and channel supports			Supermetal/GP East		X	X	X	X																													
Install catwalk			Supermetal/GP East								X	X	X	X																							
INTERIOR FITOUT/OH ROUGH																																					
Building C																																					
Install OH Duct - 2nd floor			NBK/APEX		X	X	X	X			X	X	X	X	X																						
Install Drywall tops - All floors			Century		X	X	X	X																													
Electrical/Fire Alarm/TelData Inwall Rough - All Floors	Not Inc. Wire		Griffin		X	X	X	X																													
Plumbing Rough in Walls at Science rooms			Grasseschi		X	X	X	X																													
Spray Intumescent Column on 1st & 2nd Floors			H. Carr																																		
Building D																																					
Frame Interior Walls - 2nd Floor			Century		X	X	X	X																													
Initial Polished Concrete - 2nd Floor		A15050	Kaloutas								X	X	X	X	X																						
Install OH Plumbing - 2nd Floor			Grasseschi																																		
Install Door Frames - 2nd Floor			Century																																		
Install OH Duct - 2nd floor			NBK/APEX																																		
Electrical/Fire Alarm/TelData Inwall Rough - 2nd Floor	Not Inc. Wire		Griffin		X	X	X	X																													
Plumbing Rough in Walls at Science rooms - 2nd Floor			Grasseschi		X	X	X	X																													
Layout & Frame Interior Walls - 1st Floor			Century		X	X	X	X			X	X	X	X	X																						
Install FP Rough - 1st Floor			JCI		X	X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Install OH HVAC Pipe - 1st Floor			NBK		X	X	X	X			X	X	X	X	X																						
Building E																																					
Install Temp Lighting & Power			Griffin																																		
Framing Exterior Walls - 2nd Floor		A9950	Century																																		
Install window blocking - 2nd Floor			Century																																		
Install OH Plumbing - 2nd Floor		A11170	Grasseschi		X	X	X	X																													
Electrical/Fire Alarm/TelData Inwall Rough - 2nd Floor			Griffin	X	X	X	X	X																													
Building F																																					
Install Temp Lighting & Power			Griffin		X	X	X																														
Patch Intumescent primer on columns			H. Carr		X	X	X	X																													
Install Intumescent FP			H. Carr		X	X	X	X																													
Install Spray Fire Proofing at gym			H Carr		X	X	X	X																													
Install Spray Fire Proofing at Locker Rooms			H Carr		X	X	X	X																													
MEP Rough in CMU Walls in Lockerrooms			MEP Trades			X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Install CMU Walls in Lockerrooms			Fernandes			X	X	X			X	X	X	X	X			X	X	X	X	X			X	X	X	X	X								
Install CMU Door Frames			Century			X	X	X			X	X	X	X	X																						
Install OH Duct			NBK/APEX																																		
Install OH HVAC Pipe		A11120	NBK/APEX																																		
Install OH Plumbing		A11210	Grasseschi		X	X	X	X																													
Install OH FP Rough		A11220	JCI																																		
Frame Interior Walls		A11440	Century																																		
Building G																																					
Patch Intumescent primer on columns			H. Carr		X	X	X	X																													
Install Intumescent FP			H. Carr																																		
Install FP on exterior columns			H. Carr		X	X																															
Sheath Walls at Low/High Roof			Century																																		
Install HM Door Frames			Century																																		
MEP Rough in CMU walls			MEP Trades		X	X	X	X																													
Install CMU walls in Auditorium			Fernandes		X	X	X	X																													
Building A																																					
Building B																																					
ROOFING & FAÇADE WORK																																					
Building C																																					
Wrap Window Sills with AVB			Armani		X	X	X																														
Install AVB at Façade - (West)			Armani		X	X	X	X			X	X																									
Install AVB at Façade - (South-East)			Armani										X	X	X			X	X	X	X	X															
Install Temp Windows			Riggs		X	X	X	X			X	X	X																								
Install Masonry at West Side			Fernandes										X	X	X			X	X	X	X	X			X	X	X	X	X								
Building D																																					
Sheath Exterior Walls and Install Blocking at CW Openings			Century		X	X	X	X			X	X	X	X	X																						
Install AVB			Armani															X	X	X	X	X			X	X	X	X	X								
Building E																																					



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
