

The Sharon High School Construction Project



4 Week Look Ahead Schedule 09-13-21

- Structural steel decking & detailing is nearing completion.
- Roof installation is ongoing.
- Concrete slab placements are ongoing. Please note: slab on grade placements - which may include late work-are scheduled for 9/20 & 9/23- see enclosed notice.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. Installation of drywall tops is ongoing. Wall close-in is on the radar.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry is also scheduled to begin within the next month.
- Interior masonry installation - including interior walls- is ongoing.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Stair installation has started.
- Work at the athletic field- including irrigation & athletic equipment prep- is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>


Town of
SHARON
Massachusetts



Sharon High School



**SHARON HS PROGRESS UPDATE
SEPTEMBER 2021**

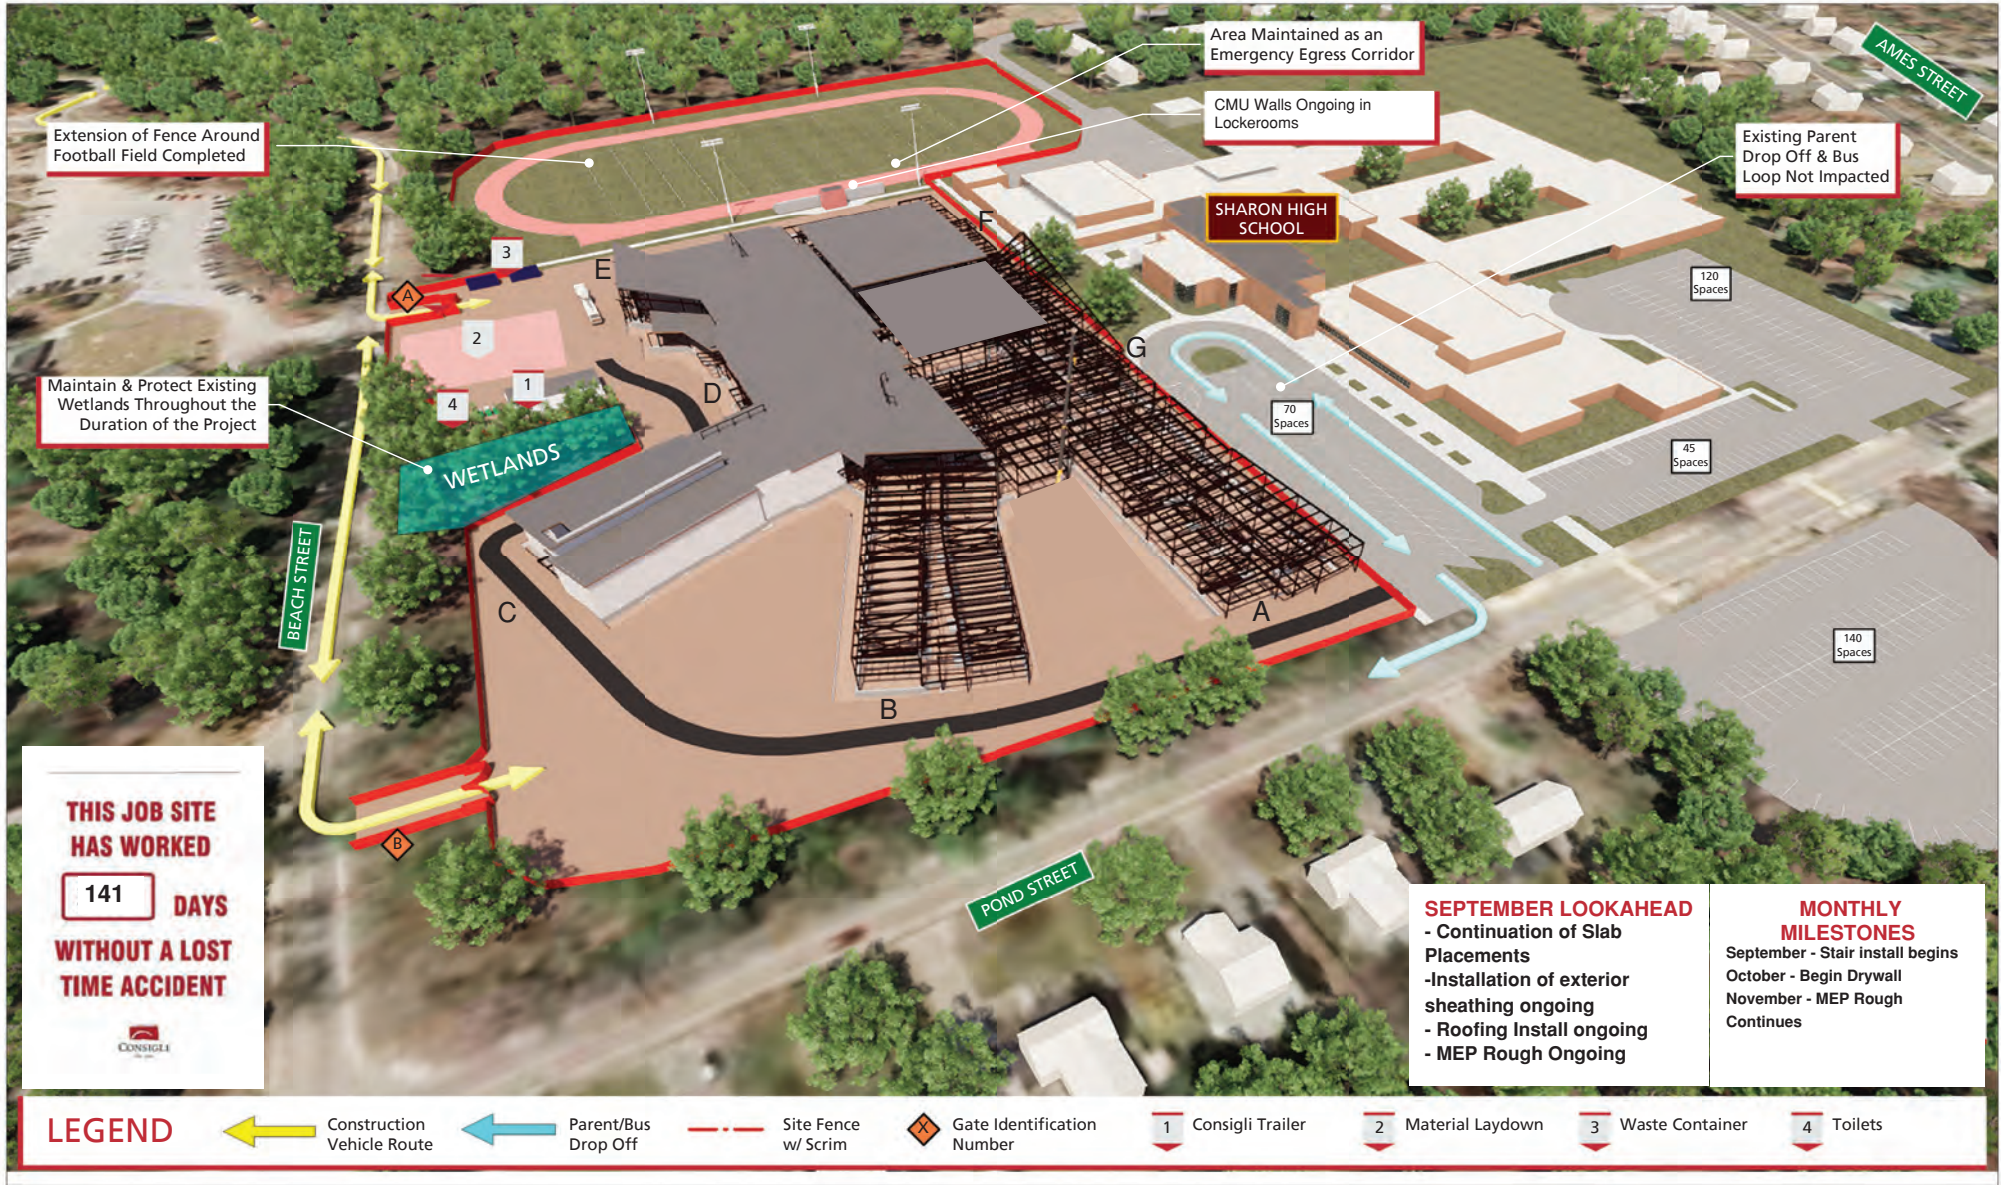

LOOK AHEAD SCHEDULE
9/13/2021

Description of Work	Notes	P6 Activity Code	Responsibility	9/13	9/14	9/15	9/16	9/17	9/18	9/19	9/20	9/21	9/22	9/23	9/24	9/25	9/26	9/27	9/28	9/29	9/30	10/1	10/2	10/3	10/4	10/5	10/6	10/7	10/8	10/9	10/10	
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	
				Install Brick Façade - West Elevation			Fernandes																									
Wash Down Brick - West Elevation			Fernades																													
Building F																																
Install Roof Drains West Low Roof			Grasseschi								X																					
Install Roofing at F low Roof - West Elevation			Capeway										X	X	X																	
Install AVB west Elevation CMU			Armani																													
Install Brick Façade - West Elevation			Fernandes															X	X	X	X	X				X	X	X	X	X		
Wash Down Brick - West Elevation			Fernades																													
Frame and Sheath North Side First Floor			Century	X	X	X	X	X			X	X	X					X	X	X					X	X	X					
Install AVB North Side First Floor Sheathing			Armani																													
Install Window Blocking on all windows			Century																													
Building F - GYM																																
Install AVB at GYM Walls	West & North Elevations		Armani			X	X	X			X	X																				
Install Brick Façade			Fernandes															X	X	X	X	X			X	X	X	X	X			
Wash Down Brick			Fernades																										X	X		
Building G																																
Install Roofing at North Canopy Roof			Capeway			X	X	X																								
Frame and Sheath North Elevation (1st Floor)			Century	X	X	X	X	X			X	X	X	X	X																	
Frame and Sheath North Elevation (2nd Floor)			Century								X	X	X	X	X			X	X	X	X	X										
Install Window Blocking at all locations			Century								X	X	X	X	X			X	X	X	X	X			X	X	X	X	X			
Install AVB			Armani																													
Building G - Auditorium																																
Install Fire Proofing at Exterior walls at Auditorium Walls			H Carr																													
Install Beam infill and Densglass at High Roof			Century				X	X																								
Install AVB - CMU Walls at High Roof			Armani															X	X	X	X	X										
Install Masonry Façade			Fernandes																						X	X	X	X	X			
Building A																																
Install Remaining Roof Blocking at Sloped Roof			Century	X	X	X	X	X			X	X	X	X	X																	
Install LGMF/Sheathing/Blocking at Low/High Roofing Wall			Century	X	X	X	X	X			X	X	X	X	X																	
Install Blocking at MEP Penetrations			Century								X	X	X	X	X																	
Install Roofing (Sloped then to Flat)			Capeway															X	X	X	X	X			X	X						
Building B																																
Install Perimeter Roof Blocking			Century										X	X	X			X	X	X	X											
Install LGMF at Low/High Roofing Wall			Century										X	X	X			X	X	X	X											
Layout of MEP Penetrations in Roof			MEP Trades										X	X	X																	
Install Blocking at MEP Penetrations			Century										X	X				X	X	X	X											
Install Roofing			Capeway																									X	X	X		



Sharon High School: Notice of Potential After-Hours Work

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
