

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule 09-20-21

- Structural steel decking & detailing is nearing completion.
- Roof installation is ongoing.
- Concrete slab on deck placements are complete. Slab on grade placements - which may include late work are ongoing & scheduled for 9/27 & 9/30- see enclosed notice.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. Pulling of electrical will begin this week.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. Installation of drywall tops is ongoing. Wall close-in is scheduled for the coming weeks.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry has begun. Interior masonry installation - including interior walls- is ongoing.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Work at the athletic field- including topsoil & athletic equipment prep- is ongoing.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>


Town of  
**SHARON**  
Massachusetts



# Sharon High School



**SHARON HS PROGRESS UPDATE  
SEPTEMBER 2021**

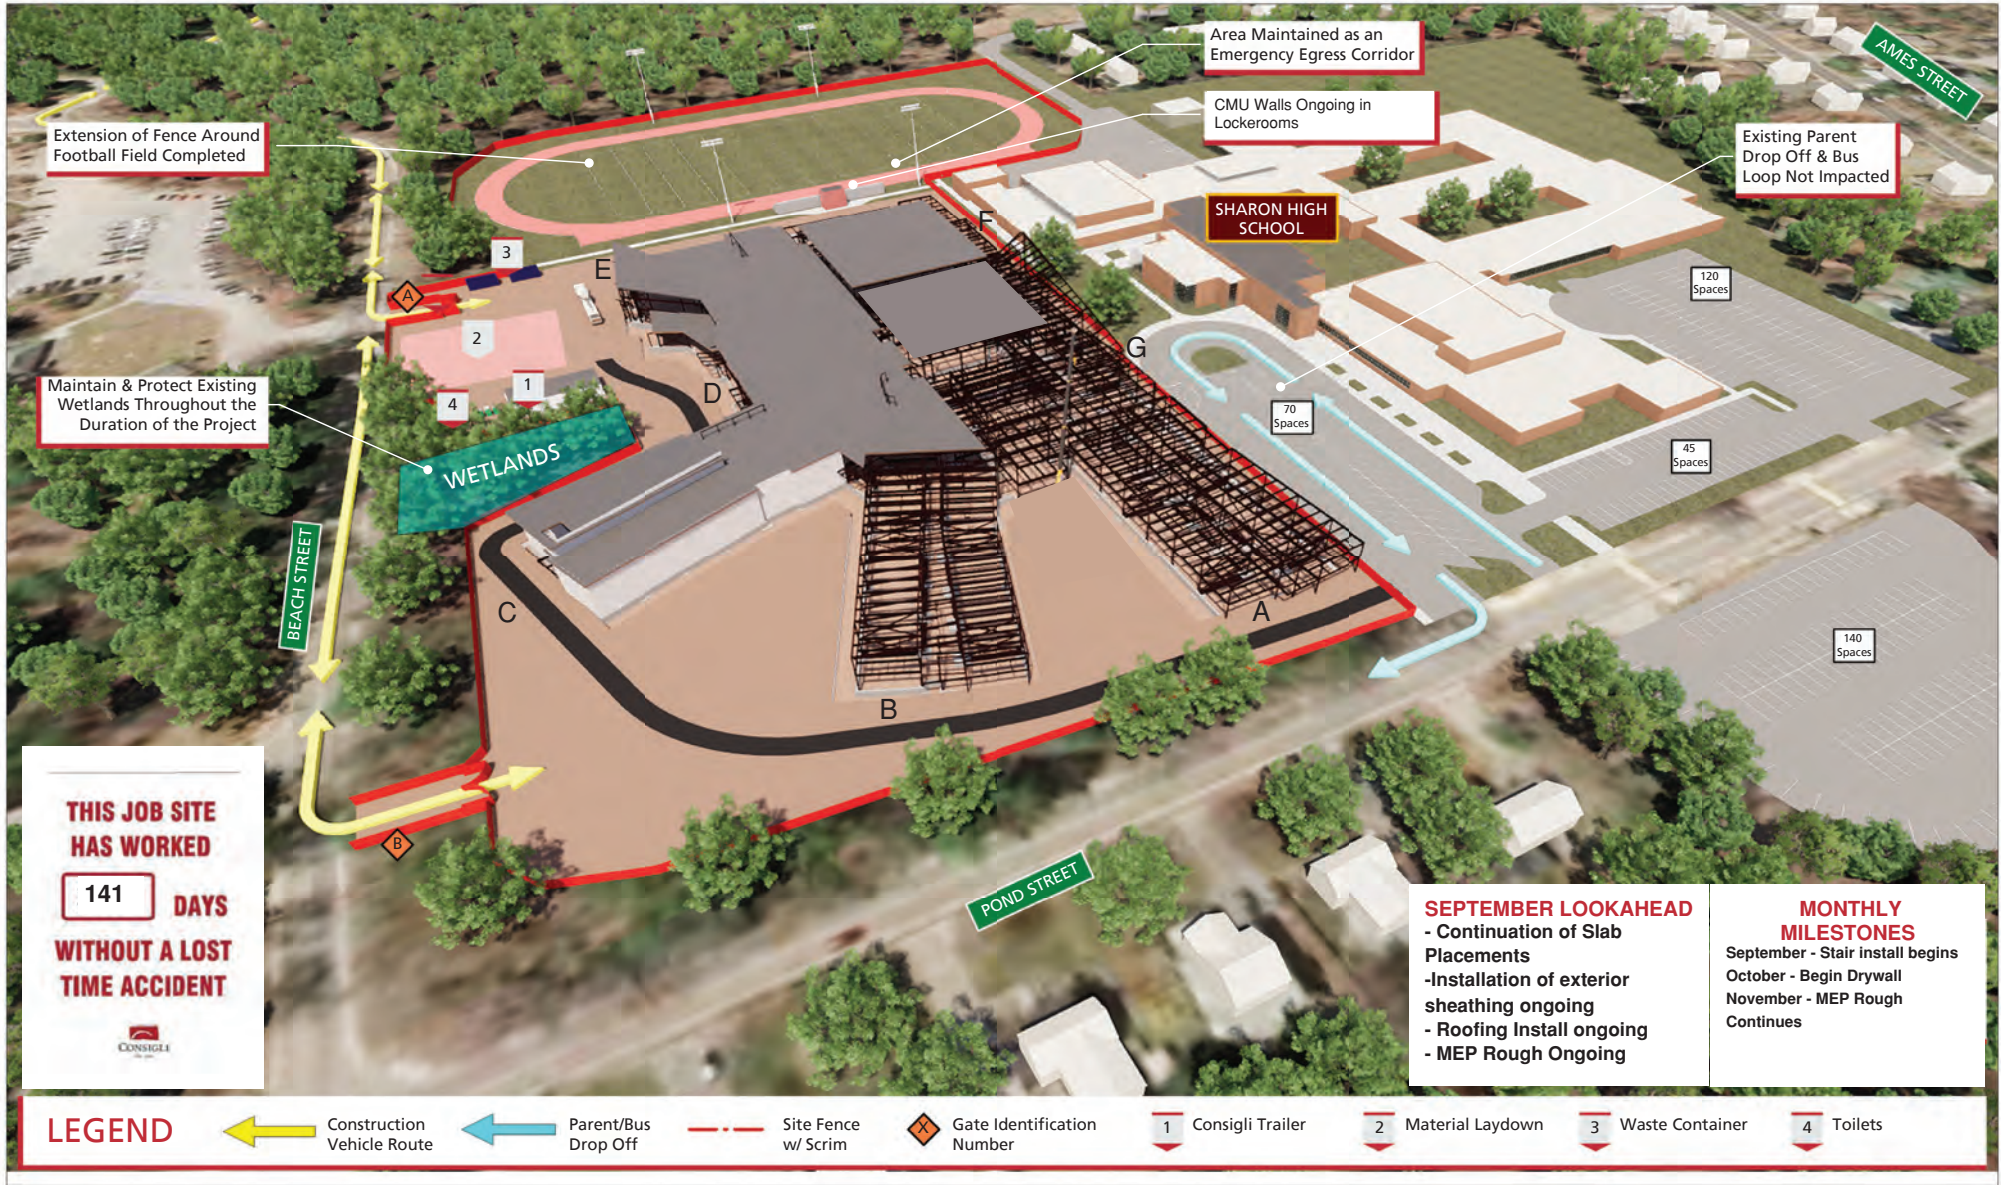

**THIS JOB SITE HAS WORKED**  
**141 DAYS**  
**WITHOUT A LOST TIME ACCIDENT**

**SEPTEMBER LOOKAHEAD**  
- Continuation of Slab Placements  
- Installation of exterior sheathing ongoing  
- Roofing Install ongoing  
- MEP Rough Ongoing

**MONTHLY MILESTONES**  
September - Stair install begins  
October - Begin Drywall  
November - MEP Rough Continues

**LEGEND**

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets









**Sharon High School: Notice of Potential After-Hours Work**

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

*Matthew Gulino*

Matthew Gulino  
Associate | Owner's Project Manager  
PMA Consultants  
[mgulino@pmaconsultants.com](mailto:mgulino@pmaconsultants.com)
