

# The Sharon High School Construction Project



## 4 Week Look Ahead Schedule 10-18-21


- Structural steel detailing is complete. Stair installation is ongoing.
- Roof installation is ongoing.
- Slab on grade placements are ongoing coordinating w/ below & in slab MEPs.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. Pulling of electrical is also ongoing.
- Interior and exterior light gauge metal framing are ongoing at multiple areas. Installation of drywall tops is ongoing. Wall close-in is scheduled to begin soon.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing.
- Installation of exterior panel back-up system is beginning in the coming weeks.
- Windows are beginning to arrive on-site. Mock up installation & testing upcoming.
- Underground plumbing & electrical work is ongoing but nearing completion.
- Work at the athletic field is ongoing- sod installation is scheduled for next week.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of  
**SHARON**  
Massachusetts





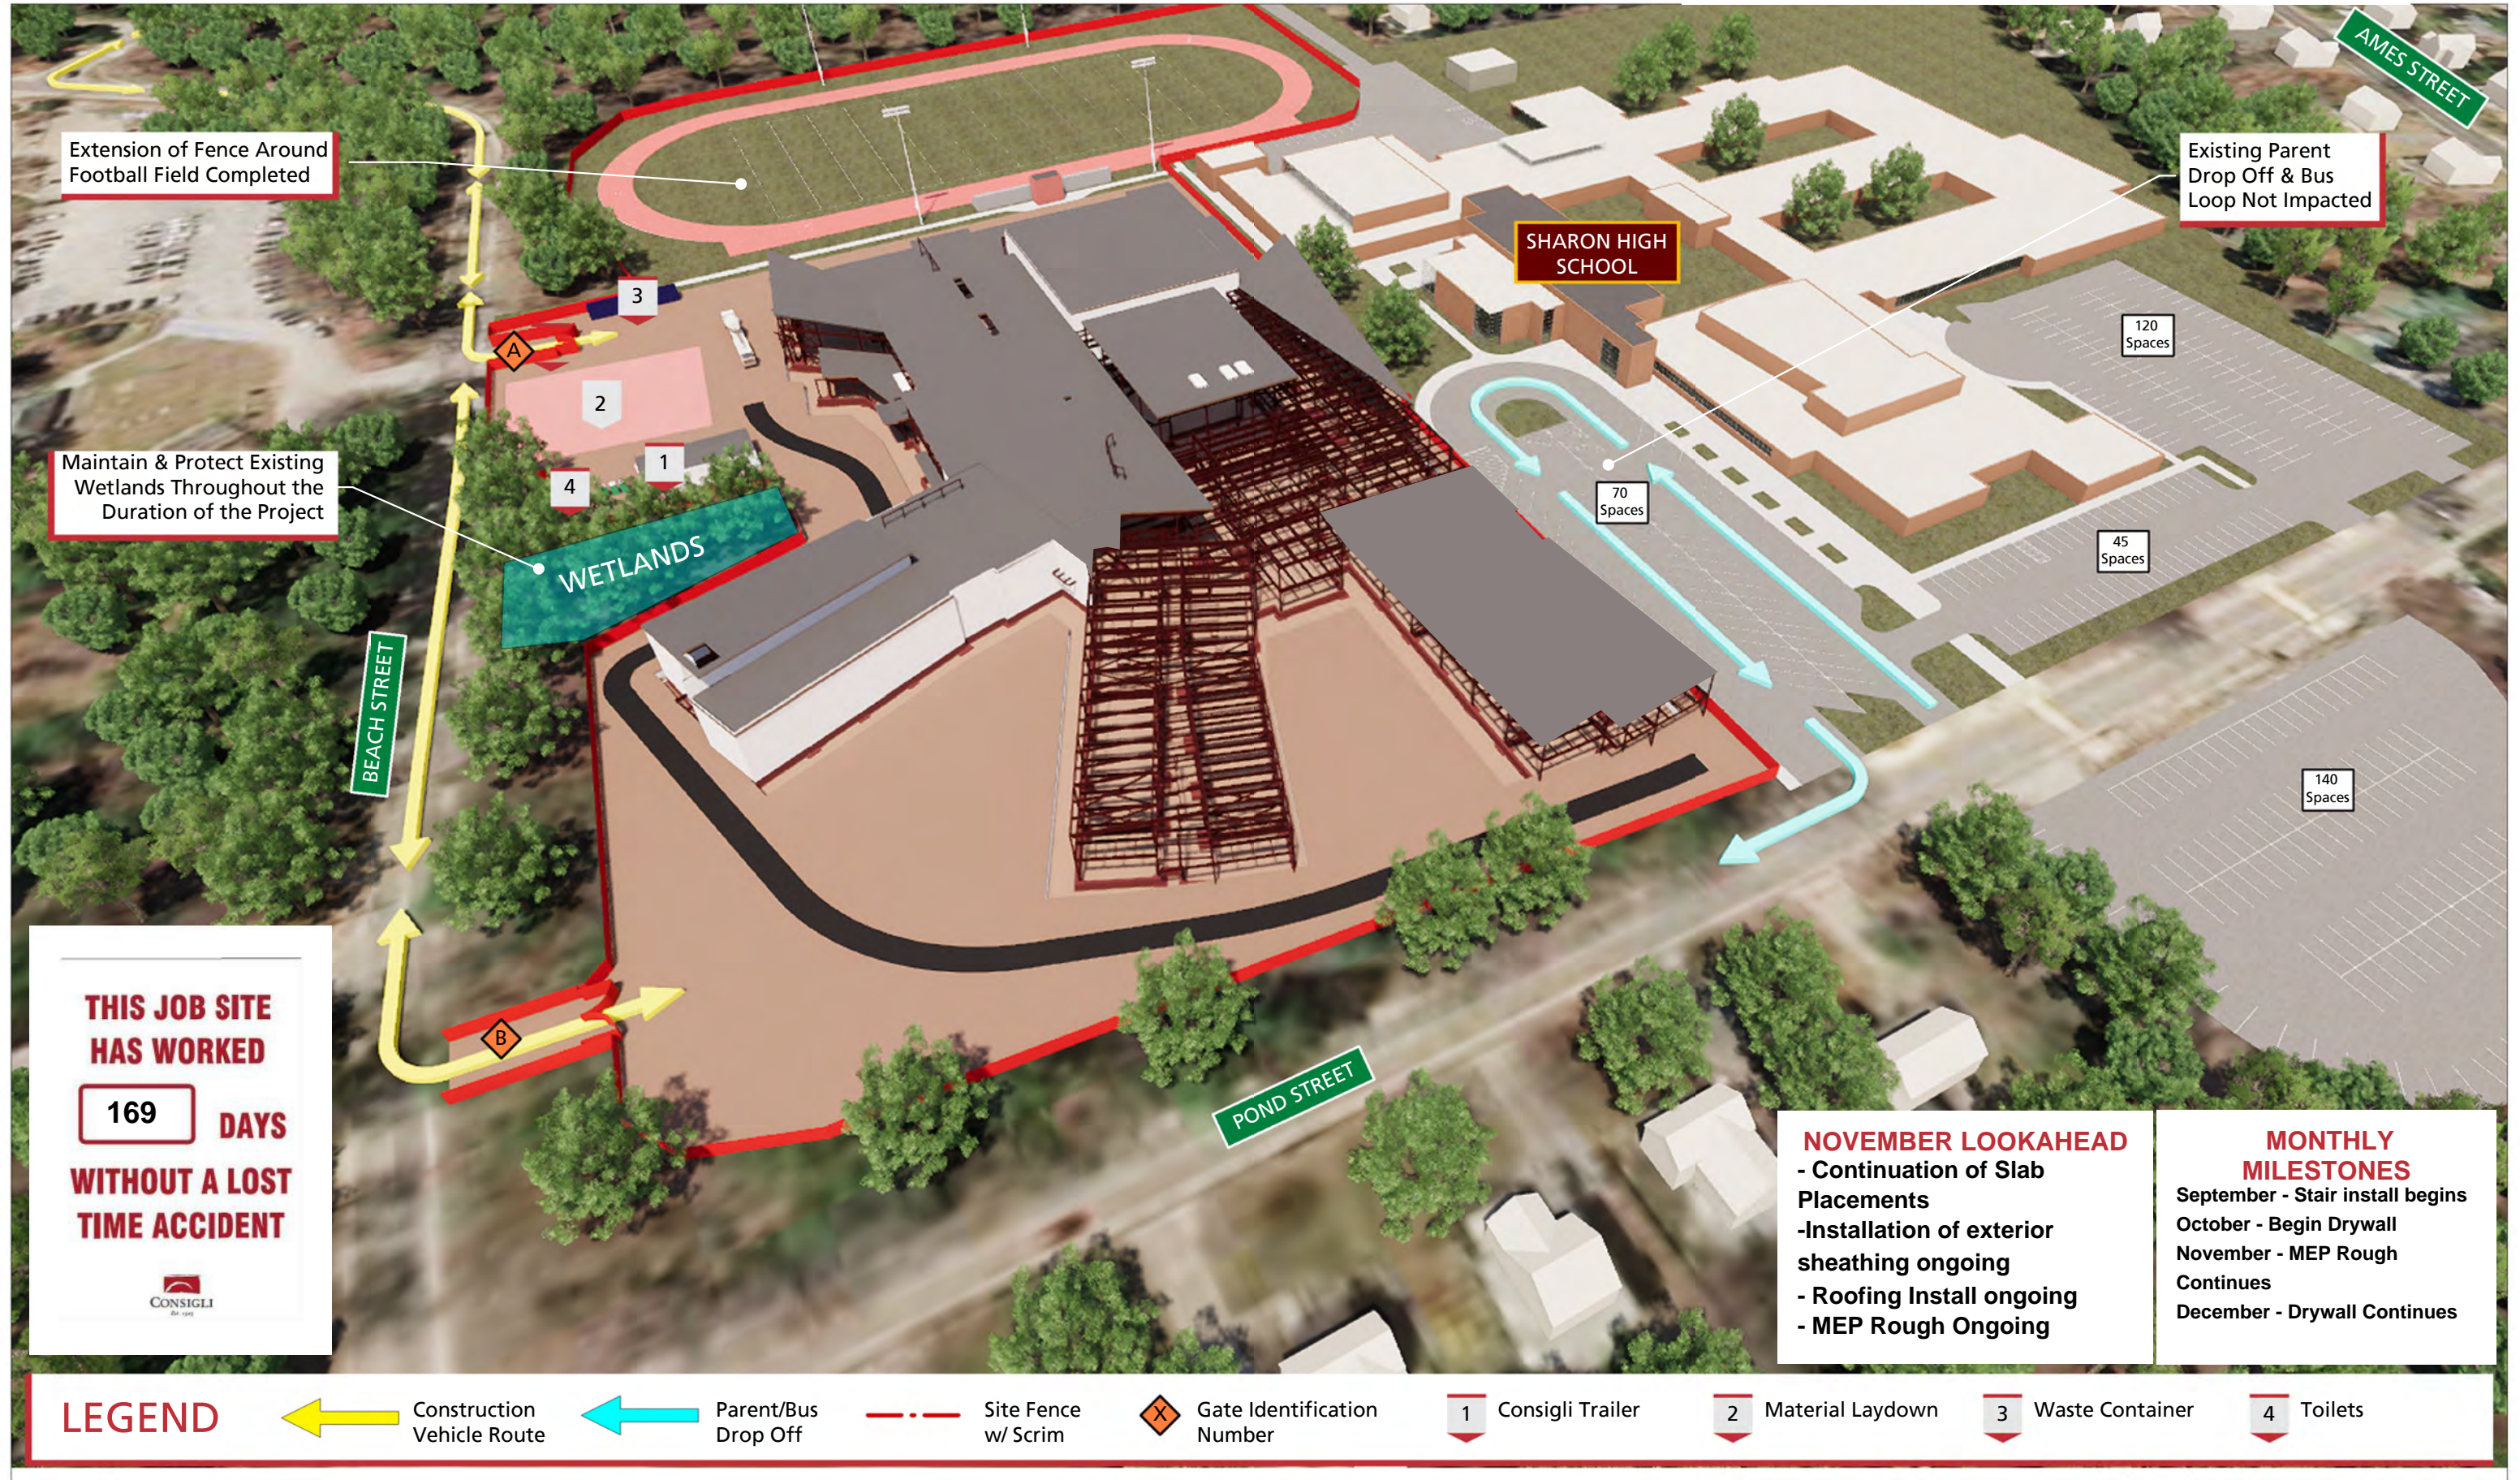





		LOOK AHEAD SCHEDULE																																			
		10/18/2021																																			
Description of Work	Notes	P6 Activity Code	Responsibility	10/18	10/19	10/20	10/21	10/22	10/23	10/24	10/25	10/26	10/27	10/28	10/29	10/30	10/31	11/1	11/2	11/3	11/4	11/5	11/6	11/7	11/8	11/9	11/10	11/11	11/12	11/13	11/14						
				M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S	M	T	W	TR	FR	S	S						
<b>Building G</b>																																					
Prep and place slab at main lobby/back half of auditorium			Riggs															X	X	X	X	X				X	X	X									
Prep and place black box theater slab			Riggs																						X	X	X	X	X								
Install Stair 2			Berlin Steel	X	X	X	X	X			X	X																									
<b>Building G - Auditorium</b>																																					
Prep for slab in auditorium			Marois								X	X	X	X	X																						
Install Waterproofing membrane underslab at auditorium			Superior											X	X																						
Install Vapor Barrier/Mesh at Stage			Riggs																																		
Install floor boxes in auditorium			Griffin															X	X	X	X	X				X	X	X									
Place slab at Auditorium Stage			Riggs																						X	X	X	X	X								
Place slab at Auditorium			Riggs																						X	X	X	X	X								
Install Dancefloor in Auditorium			Consigli																																		
Install OH FP Rough			JCI																																		
Install OH plumbing			Grasseschi																																		
Install OH ductwork																																					
<b>Building A</b>																																					
Frame interior walls			Century	X	X	X	X	X																													
Install OH MEP rough post coordination			MEP Trades																	X	X	X				X	X	X	X	X							
<b>Building B</b>																																					
Install spray fire proofing at roof structure			H Carr																																		
Frame interior walls			Century	X	X	X	X	X			X	X	X	X	X																						
Install OH MEP rough post coordination			MEP Trades																																		
<b>ROOFING &amp; FAÇADE WORK</b>																																					
<b>Building C</b>																																					
Install AVB at Façade - (South - East)			Armani	X	X	X	X	X																													
Install AVB at clerestory			Armani															X	X	X	X	X															
Install metal panel back up system			Riggs											X	X			X	X	X	X	X			X	X	X	X	X								
Wash Brick			Fernandes											X	X																						
<b>Building D</b>																																					
Frame/Sheath/Block Exterior walls			Century	X	X	X	X	X			X	X	X																								
Install AVB			Armani										X	X	X																						
Install Brick on remaining exterior walls - west elevation			Fernandes															X	X	X	X	X															
Install Skylight			Chandler Architectural																																		
Install metal panel back up system			Riggs																																		
<b>Building E</b>																																					
Temp in CW 20 - café			Commonwealth																							X	X	X	X	X							
Frame/Sheath/Block Remaining Exterior walls			Century	X	X	X	X	X			X	X	X																								
Install Roofing up to concrete roof pad			Capeway				X	X	X																												
Install Brick Façade at High Roofs	West Elevation		Fernandes				X	X			X	X	X	X	X			X	X	X	X	X															
Install AVB at CMU exterior walls - post roof install			Armani								X	X	X	X	X																						
Install Brick Façade at CMU exterior walls			Fernandes															X	X	X	X	X			X	X	X	X	X								
Install Windows at West Side			Chandler Architectural																																		
Install Skylights			Chandler Architectural																																		
<b>Building F</b>																																					
Install Roofing at low roof			Capeway	X	X	X	X																														
Install roof protection			Riggs/Capeway			X	X	X																													
Install Brick Façade at High Roofs	North & West Elevation		Fernandes								X	X	X	X	X			X	X	X	X	X			X	X	X										
Install AVB at CMU exterior walls - post roof install			Armani								X	X	X	X	X																						
Install Brick Façade at CMU exterior walls			Fernandes															X	X	X	X	X			X	X	X	X	X								
Install Windows at North & West Side			Chandler Architectural																																		
Install Skylight - Main Lobby			Chandler Architectural																							X	X	X	X	X							
<b>Building G - North</b>																																					
Frame CW opening at Stair 1			Century				X	X			X	X	X																								
Install AVB at window blocking and sheathing north elevation			Armani								X	X	X	X	X			X	X	X	X	X															
Install Masonry façade			Fernandes																						X	X	X	X	X								
Install metal panel back up system			Riggs																																		
Install low roof roofing membrane			Capeway																																		
<b>Building G - Auditorium</b>																																					
AVB remedial work at columns			Armani				X	X			X	X	X																								
Install Masonry Façade			Fernandes								X	X	X	X	X			X	X	X	X	X															
<b>Building A</b>																																					
Install sheathing on south elevation			Century	X	X	X	X	X																													
Install window blocking			Century				X	X			X	X	X																								
Install AVB at window blocking and sheathing			Armani											X	X			X	X	X	X	X															
Install Masonry Façade			Fernandes																							X	X	X	X	X							
<b>Building B</b>																																					
Install Roofing at slope and low roof			Capeway								X	X	X	X	X																						
Install exterior framing and sheathing			Century	X	X	X	X	X			X	X	X	X	X																						
Install window blocking			Century								X	X	X	X	X			X	X	X	X	X															
Install AVB at window blocking and sheathing			Armani																																		
Install Masonry Façade			Fernandes																							X	X	X	X	X							



**Sharon High School: Notice of Potential After-Hours Work**

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

*Matthew Gulino*

Matthew Gulino  
Associate | Owner's Project Manager  
PMA Consultants  
[mgulino@pmaconsultants.com](mailto:mgulino@pmaconsultants.com)
