

## 4 Week Look Ahead Schedule

- Continue Stair installation & placing concrete treads.
- Roof installation is ongoing targeting weather tight this week.
- The project's last major slab placement is targeted for Wednesday 12/1- this may include late work- please see enclosed notice.
- Overhead & in wall MEP rough-in is ongoing at multiple areas.
- interior and exterior light gauge metal framing are ongoing at multiple areas. In wall inspections are ongoing.
   Wall close-in is ongoing.
- Installation of exterior sheathing is ongoing. Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing.
- Temporary heaters will be started up this week. See enclosed notice for details- this will enable temperature sensitive interior work such as drywall taping to begin.
- Windows are beginning to arrive on-site. Mockup installation & testing upcoming.
- See attached progress update.
- See attached for details & complete look ahead schedule

Visit the Sharon HS Building website for more project information: https://www.shsbuilding.com/












## Sharon High School



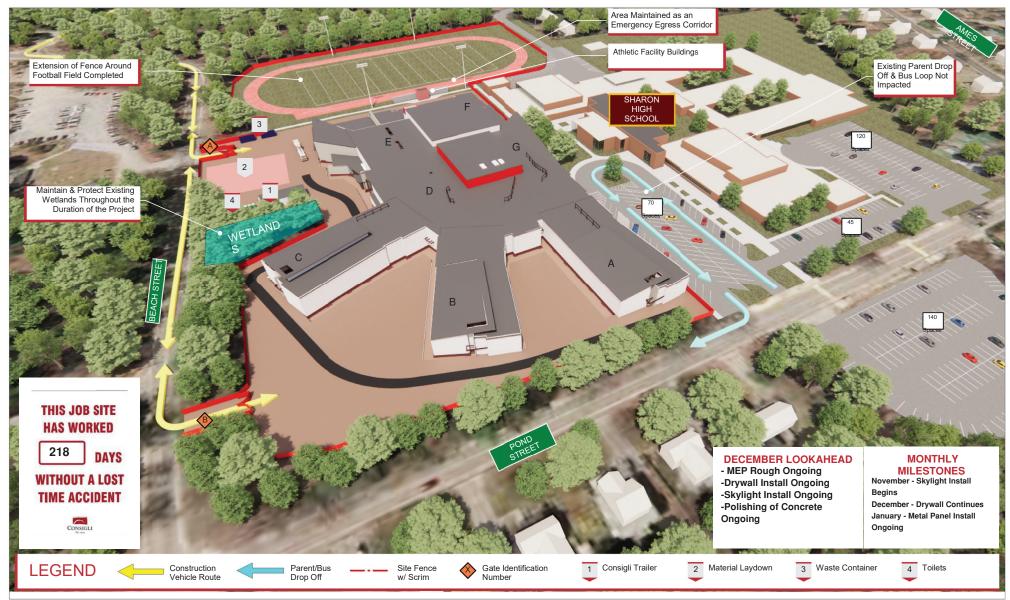

		LOOK AHEA		OULE /29/2021																						
Description of Work	Notes	P6 Activity Code	% Comp	Responsibility		11/30 T	12/1 12/2 W TR	12/3 FR	12/4 12/5 S S	5 12/6 M	12/7 T	' 12/8 1: W 1	2/9 12/10 FR FR	12/11 S	12/12 S	12/13 M	12/14 1 T	12/15 12/1 W TR	6 12/17	7 12/18 S	3 12/19 S	12/20 1 M	2/21 12/22 T W	12/23 TR	12/24 FR	12/25 12/2 S S
SCHOOL SCHEDULE MILESTONES																										
HOLIDAYS																										
Christmas Eve - Site Open																									Х	
Christmas Day																										Х
New Years Eve - Site Open																										
New Years Day WEATHER																										
MOCK UP																										
Install Masonry Façade				Fernandes	Х																					
Install Aluminum Windows				Chandler		Χ	ХХ	Х																		
Install metal panel back up system and insulation				Riggs																						
SITE UTILITIES				_																						
Continual check in with Eversource for gas service Working through verizon pole relocation issues				Eversource Verizon															+					1		
Install drainage at gate A				Vinagro																				1		
ATHLETIC FACILITY				Ţ.																						
Install Interior CMU Walls at Concession Stand & Bathrooms	PENDING COORDINATION AND TRUSS DESIGN			Fernandes																				L		
MEP Rough in CMU walls	PENDING COORDINATION AND TRUSS DESIGN			MEP Trades																						
INTERIOR FITOUT/OH ROUGH																										
Building C																										
Install OH Duct - 1st floor Plumbing Rough in Walls at Science rooms				APEX Grasseschi																						
Insulate Plumbing Lines - 1st Floor				Grasseschi																						
Insulate and board walls	Both floors			Century			Х																			
Turn on Heat				Consigli																						
Tape Walls Prime and first coat walls	Both floors			Century King						X	X		X X X X			X	X	X X X X								
Install wall tile				High Point						X	Х		X X			X		XX								
Install Ceiling grid				K&K									Х Х			Х	Х	Х Х	Х			Х	Х Х			
Frame hard ceiling				Century									X X			Χ	Χ	X X	X			Х	X X	X	Χ	
Building D  Electrical/Fire Alarm/TelData Inwall Rough				Griffin	V	Х	ХХ	X			V	X	ХХ													
Plumbing Rough in Walls				Grasseschi	^	^	A A			_ ^	^	^	^ ^													
Layout & Frame Interior Walls - 1st Floor	Remaining Walls			Century																						
Install ductwork - 1st Floor				Apex	X	Χ	X X	Х																		
Touchup fire proofing Inwall Inspections complete	Second Floor			H. Carr All Trades									X													
Insulate and board walls	Second Floor			Century								+ +	^											1		
Tape Walls	Second Floor			Century																						
Inwall Inspections complete	First Floor			All Trades																						
Insulate and board walls Tape Walls	First Floor First Floor			Century Century															+-			+		-		
Building E	I IISTI IOOI			Contary																						
Plumbing Rough in Walls	2nd floor			Grasseschi																						
Electrical/Fire Alarm/TelData Inwall Rough	2nd floor			Griffin	X	Х	X X	Х		X	X	X	X X									-				
Touchup fire proofing Inwall Inspections complete	2nd floor 2nd floor			H. Carr All Trades									X													
Insulate and board walls	2nd floor			Century									^													
Frame walls at first floor - after slabs				Century	Х	Χ	ХХ	Х																		
Install ductwork	1st floor			Apex						.,	37		V V			X	X	X X	X			Х	Х Х	Х	Х	
Plumbing Rough in Walls Electrical/Fire Alarm/TelData Inwall Rough	1st floor 1st floor			Grasseschi Griffin						X		X	X X X				X	X X X X	X					1		
Inwall Inspections complete	2nd floor			All Trades						^	^	^	A A			^	^									
Building F																										
Install Vapor Barrier in Main Lobby				Riggs		Χ																				
Install Mesh in Main Lobby Place Slab in Main Lobby				Riggs Riggs			X	X																-		
Install Intumescent FP - GYM				H. Carr	X	Χ																		1		
Install OH Duct				NBK/APEX	X	Χ	X X	Х																		
Install OH HVAC Pipe		A11120		NBK/APEX	X	Χ	X X	X																		

		LOOK AHEAD SCH	EDULE 11/29/2021																						
Description of Work	Notes	P6 Activity % Code Comp	Responsibility	11/29 M	11/30 T		2/2 12/3	12/5 S	12/6 M	12/7 T		12/9 12/1 TR FR				12/15 12/ W Ti			2/18 12/1 S S			12/22 W	12/23 TR		2/26 S
Install OH Plumbing		A11210	Grasseschi	Х	Χ	Х	Х																		
Install OH FP Rough		A11220	JCI				.,					,													
Install OH Electrical Rough Frame Interior Walls -Gym & lobby		A11220 A11440	Griffin Century	X	Χ	Х	X X		Х	X	Х	X X												$\longrightarrow$	
Frame hard ceilings in Locker rooms		A11440	Century																					$\overline{}$	
Frame hard ceilings at running track			Century																					_	
Building G			•																						
Install Stair 2 Rails			Berlin Steel																						
Spray FP in G2			H Carr	X	X	X																			
Spray FP in Black Box Install interior framing	1st floor		H Carr Century	X	^	Х																		-	
Install OH Plumbing rough	13111001		Grasseschi	Х	Χ	Х	ХХ																	-	
Install OH HVAC Pipe	1st floor		NBK		Χ		Х Х																		
Install OH FP rough	1st floor		JCI																					/	
Install OH Electrical Rough Building G - Auditorium	Not incl. wire		Griffin	X	Х	Х	XX		Х	Х	Х	X X													
Install Dancefloor in Auditorium			Consigli	X	Х	X	X X																		
Install OH FP Rough			JCI		^	^	A A		Х	Χ	Х	ХХ		Х	Х	х х	( )	X		X	Х	X	Х	X	
Install OH plumbing			Grasseschi						Х	Χ	Х	Х Х		Х	Χ	X X	( )	X		X	X	Х	Х	X	
Install OH ductwork			Apex						Χ	Х	Х	Х Х		Х	Χ	X X		X		X	Х	Х	Х	X	
Building A  Electrical/Fire Alarm/TelData Inwall Rough	1 at floor		Griffin		V																				
Install OH HVAC Pipe	1st floor 1st floor		NBK	X	X	Х	х х		Х	Х	Х	ХХ		Х	Χ	х х	( )	X						-	
Frame interior walls	2nd floor		Century				XXX					XX				X X									
Building B																									
Electrical/Fire Alarm/TelData Inwall Rough	1st floor		Griffin Century	X	Χ	Х	X X		X	X	X	х х		V	V	V V	, ,	v							
Frame interior walls Install OH MEP rough post coordination	2nd floor		MEP Trades						^^	۸	^	^ ^		^	^	Х Х	. /	^		X	X	Х	Χ	X	
ROOFING & FAÇADE WORK			IIIEI TTUGES																						
Building C																									
Install Missing Brick - At windows			Fernandes	Х	Χ	Х																			
Wash Brick			Fernandes				X																		
Building D			Famandas	V	V	V	V V		V	V	V														
Install Brick on remaining exterior walls - west elevation Wash Brick			Fernandes	X	Х	Х	Х Х		Х	Х		X X												$\rightarrow$	
Install Skylight			Chandler Architectural						Х	Х		X X		Х	Х	х х	( )	X							
Building E			Chanalor / II Chinoctarar						Λ	,,	,	X X		,	,	,	. ,								
Install Brick Façade at West CMU exterior walls			Fernandes	Х																					
Install Skylights			Chandler Architectural		Χ	Х	х х																		
Open and Patch roofing for additional blocking	E Low Roof		Capeway			Х																			
Install Curb Blocking for Rooftop Units	E Low Roof		Century			Х																			
Set Curbs for Rooftop Units			NBK/APEX									Х													
Flash Roofing Membrane to Curbs			Capeway									Х													
Set Rooftop Units			NBK/APEX																						
Open and Patch roofing for additional blocking	E High Roof		Capeway																						
Install Curb Blocking for Rooftop Units	E High Roof		Century																						
Set Curbs for Rooftop Units			NBK/APEX		Χ							Х													
Flash Roofing Membrane to Curbs			Capeway		Χ							Х													
Set Rooftop Units			NBK/APEX																						
Building F																									
Install Skylight - Main Lobby			Chandler Architectural						Х	Χ	Х	X X		Х	Х	X X	( )	X							
Open and Patch roofing for additional blocking			Capeway				X															1			
Install Curb Blocking for Rooftop Units			Century				X															1			
Set Curbs for Rooftop Units			NBK/APEX									Х										1			
Flash Roofing Membrane to Curbs			Capeway									X													
Set Rooftop Units			NBK/APEX																						
Building G - North																									
Install AVB at window blocking and sheathing north elevation			Armani																	X	X	Х	Х	X	
Install Masonry façade			Fernandes																						

		LOOK AHEA		DULE 1/29/2021																											
Description of Work	Notes	P6 Activity	%	Pospopsibility	11/29	11/30	12/1 1	2/2	12/3 1	2/4	12/5	12/6	12/7	12/8	12/9	12/10	12/11	12/12	12/13	12/14	12/15	12/16	12/17	12/18	12/19	12/20	12/21 1	12/22 12	2/23 1	2/24 12	2/25 1
Description of Work	Notes	Code	Comp	Responsibility	М						S	М	Т	W	TR	FR	S	S	М	Т	W	TR	FR	S	S	М	Т	T W TR FR S S			
Install low roof roofing membrane around Auditorium				Capeway	Х	Х	Х	X	X																						
Building A																															
Install AVB at window blocking and sheathing for Masonry Install				Armani								Х	Х	Х	Х	Х															
Install Masonry Façade				Fernandes															Χ	Χ	Х	Х	Х			Х	Х	Х	Х	X	
Building B																															
Install AVB at window blocking and sheathing for Masonry Install				Armani	Х	х	Х	X	Х																						
Install Masonry Façade				Fernandes	X	X	Χ	Χ	X			Χ	Χ	Χ	Χ	Χ															



## **Sharon High School: Notice of Ongoing Winter Heating**

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <a href="https://www.shsbuilding.com/">https://www.shsbuilding.com/</a>

Best Regards,

Matthew Gulino

Matthew Gulino

Associate | Owner's Project Manager

**PMA Consultants** 

mgulino@pmaconsultants.com



## **Sharon High School: Notice of Potential After-Hours Work**

Notice Date: June 17, 2021

Sharon High School Community:

The Sharon High School project will be placing concrete slabs on grade this summer. These slabs require cutting of concrete control joints as soon as the concrete is properly cured. This can be an unpredictable timeframe and may require after hours construction.

The work utilizes a small localized crew but will require a concrete saw and supplemental lighting. This process will take place approximately 7 times over the coming months. The first such placement will occur today 6/17/21 & we will continue to update the community of this potential after hours work within our 4 week look ahead schedule.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <a href="https://www.shsbuilding.com/">https://www.shsbuilding.com/</a>

Best Regards,

Matthew Gulino

Associate | Owner's Project Manager

**PMA Consultants** 

mgulino@pmaconsultants.com

Matthew Gulino
