

The Sharon High School Construction Project



4 Week Look Ahead Schedule

- The project recently accomplished two milestones. The roof is weather tight & our last interior slab placement is complete.
- Temporary heaters are running. See enclosed notice for details- this allows temperature sensitive interior work to begin.
- Skylight installation is ongoing.
- Major mechanical equipment (RTU's etc.) is stored locally and scheduled for installation over the coming weeks.
- Overhead & in wall MEP rough-in is ongoing at multiple areas. This includes increased wire pulling efforts.
- Interior light gauge metal framing are ongoing at multiple areas. In wall inspections are ongoing. Wall close-in is ongoing. Drywall finishing is ongoing. Paint, tile & ceiling grid installation are all upcoming.
- Air vapor barrier installation is ongoing.
- Installation of veneer masonry is ongoing. Installation of exterior panel is on the radar.
- Mock-up installation is ongoing- window testing is scheduled for early January.
- See attached progress update.
- See attached for details & complete look ahead schedule.

Visit the Sharon HS Building website for more project information: <https://www.shsbuilding.com/>

Town of
SHARON
Massachusetts



PMA Consultants




TAPPÉ
ARCHITECTS



Sharon High School



LOGISTICS UPDATE November 30, 2021

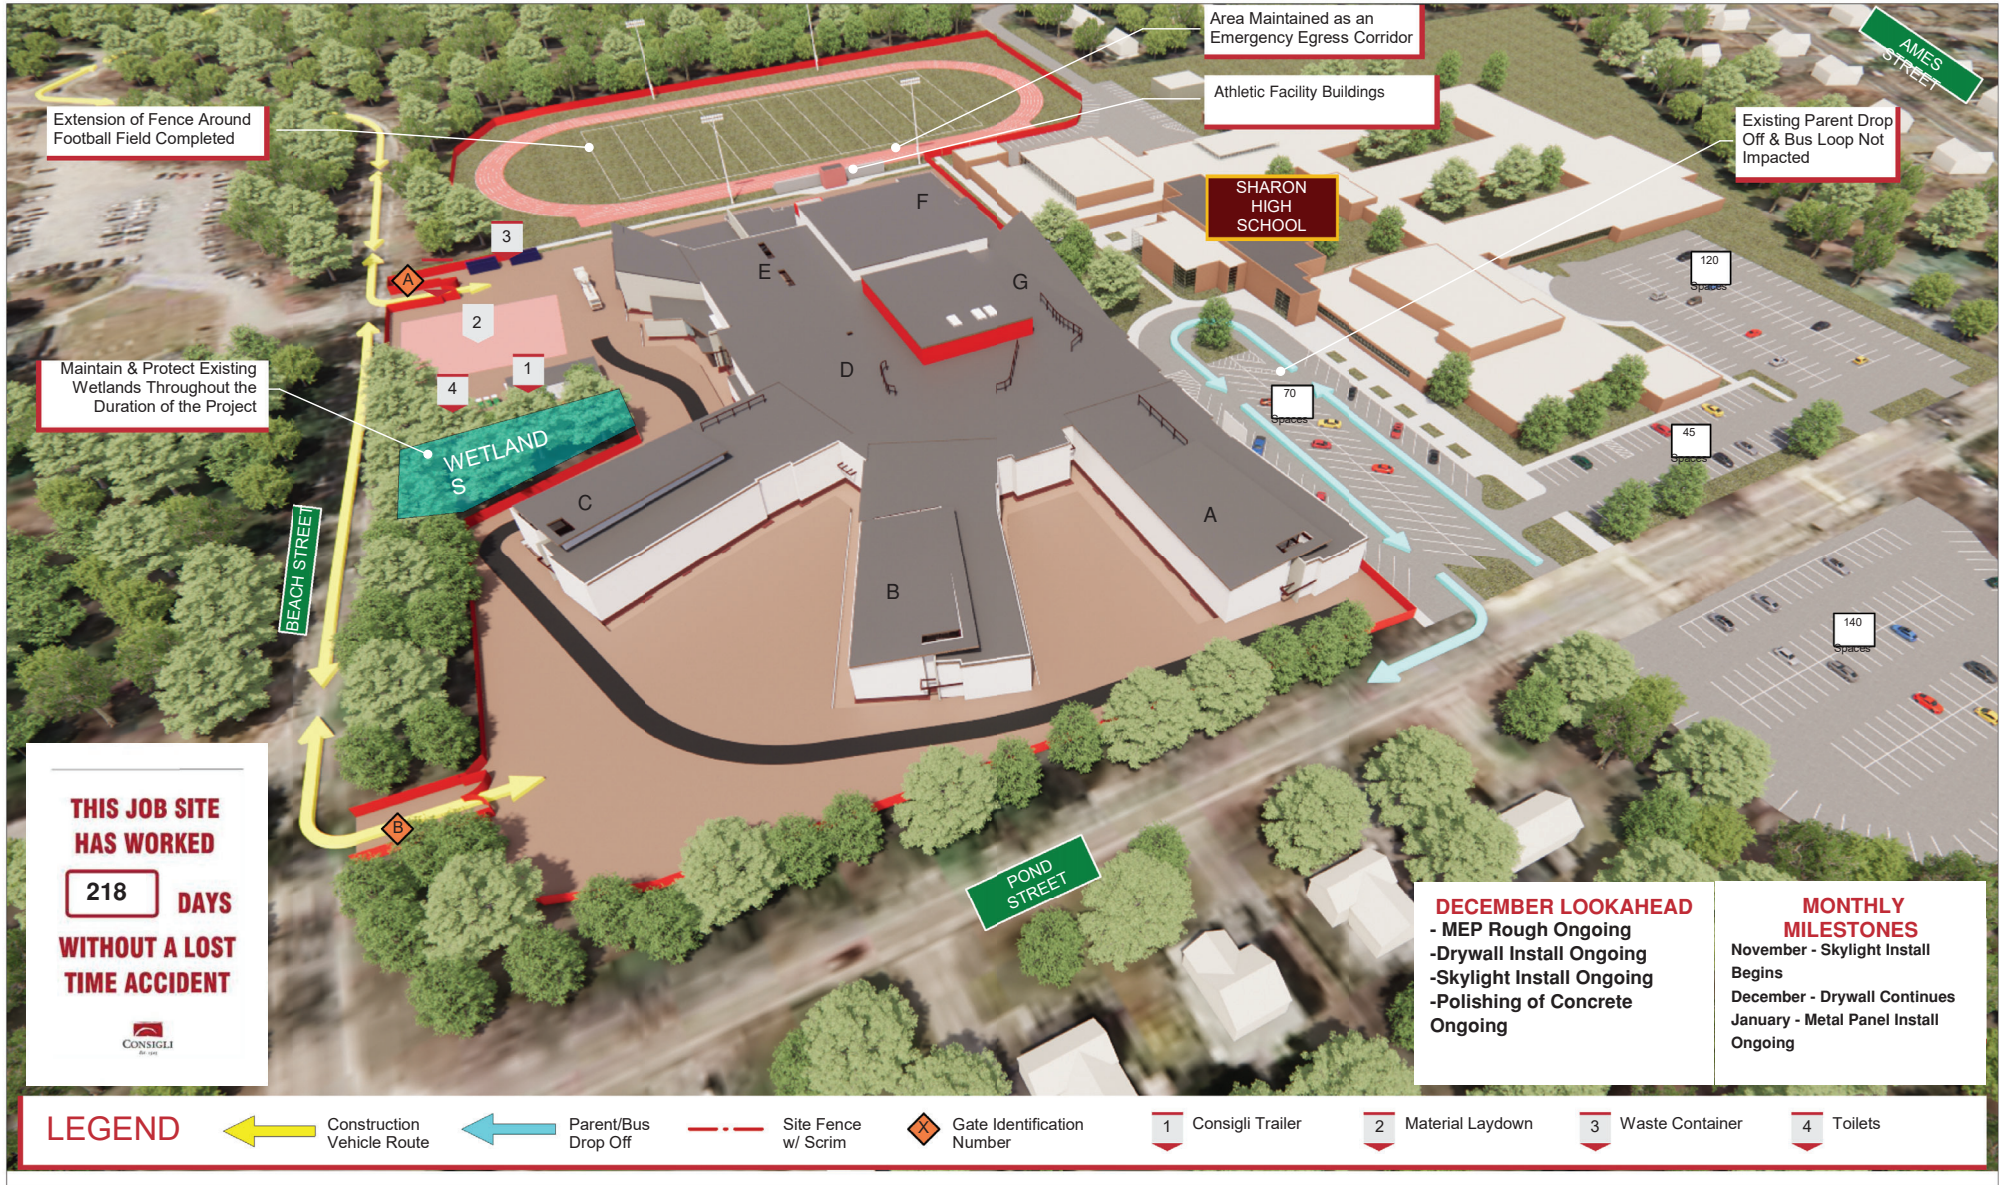

Extension of Fence Around Football Field Completed

Maintain & Protect Existing Wetlands Throughout the Duration of the Project

Area Maintained as an Emergency Egress Corridor

Athletic Facility Buildings

Existing Parent Drop Off & Bus Loop Not Impacted

SHARON HIGH SCHOOL

THIS JOB SITE HAS WORKED
218 DAYS
WITHOUT A LOST TIME ACCIDENT



DECEMBER LOOKAHEAD
- MEP Rough Ongoing
- Drywall Install Ongoing
- Skylight Install Ongoing
- Polishing of Concrete Ongoing

MONTHLY MILESTONES
November - Skylight Install Begins
December - Drywall Continues
January - Metal Panel Install Ongoing

LEGEND

- Construction Vehicle Route
- Parent/Bus Drop Off
- Site Fence w/ Scrim
- Gate Identification Number
- 1 Consigli Trailer
- 2 Material Laydown
- 3 Waste Container
- 4 Toilets



Sharon High School: Notice of Ongoing Winter Heating

Notice Date: December 1, 2021

Sharon High School Abutters & Community:

The Sharon High School project will be utilizing several large construction heaters to support interior construction this winter. To ensure required climate is maintained heaters may function 24/7 including nights and weekends. There are 5 heaters located around the perimeter of the New High School. The heaters do emit a small orange glow from the internal flame. There is a continuous fan that is powered electrically. Consigli Construction has coordinated required provisions and permits with the Sharon Fire Department.

Heaters will be started up on Wednesday, December 1, and operate throughout the winter.

Thank you for your continued cooperation & support throughout this project.

For the latest on Sharon High School construction please visit the project's website at <https://www.shsbuilding.com/>

Best Regards,

Matthew Gulino

Matthew Gulino
Associate | Owner's Project Manager
PMA Consultants
mgulino@pmaconsultants.com
